


ЈЕДИНИЦА ЗА УПРАВЉАЊЕ ПРОЈЕКТИМА  
У ЈАВНОМ СЕКТОРУ Д.О.О. БЕОГРАД  
Бр. 505/2  
29.01 2019 год.  
БЕОГРАД, НЕМАЊИНА 22-26



Јединица за управљање пројектима у јавном сектору д.о.о. Београд  
Немањина 22-26  
БЕОГРАД

**ПРОГРАМ РАДА**  
**„ЈЕДИНИЦА ЗА УПРАВЉАЊЕ ПРОЈЕКТИМА У ЈАВНОМ**  
**СЕКТОРУ“ Д.О.О. БЕОГРАД**  
**ЗА 2019. ГОДИНУ**

Београд, децембар 2018. године

## САДРЖАЈ

1. ОСНОВНИ ПОДАЦИ О ДРУШТВУ .....	3
1.1 . МИСИЈА ДРУШТВА.....	4
1.2 ВИЗИЈА ДРУШТВА.....	4
1.3. СТРАТЕГИЈА ДРУШТВА.....	4
1.4 ОРГАНИЗАЦИОНА СТРУКТУРА.....	5
2. РЕАЛИЗАЦИЈА И ПЛАНИРАНИ ОБИМ АКТИВНОСТИ ЗА 2019. ГОДИНУ (УПРАВЉАЊЕ ПОВЕРЕНИМ ПРОГРАМИМА И ПРОЈЕКТИМА).....	6
2.1. ТЕРМИН ПЛАН.....	14
2.2. ПЛАНИРАНЕ АКТИВНОСТИ.....	15
2.3. КОМИСИЈЕ, РАДНЕ ГРУПЕ, ПРОЈЕКТНИ ТИМОВИ.....	16
2.4. УПРАВЉАЊЕ РИЗИЦИМА.....	17
2.5. ИЗВЕШТАВАЊЕ.....	18
3. ПРИЛОЗИ (ГАНТОГРАМИ).....	19

## 1. ОСНОВНИ ПОДАЦИ О ДРУШТВУ

„Јединица за управљање пројектима у јавном сектору“ д.о.о. Београд је основано Одлуком Владе Републике Србије о оснивању друштва с ограниченом одговорношћу за управљање Пројектом истраживање и развој у јавном сектору („Службени гласник Републике Србије“; број 51/10, 72/2013, 24/14 и 65/14 ), и уписан у регистар привредних друштава Агенције за привредне регистре, под бројем БД 87134/2010.

**Пуно пословно име:** Друштво с ограниченом одговорношћу Јединица за управљање пројектима у јавном сектору Београд

**Адреса:** ул. Немањина бр. 22-26, Савски венац, Београд

**Матични број:** 20668890

**Број регистрације:** БД 87134/2010

**ПИБ:** 106729004

**Датум оснивања:** 09.08.2010. године

**Оснивачи друштва:** Влада Републике Србије 100%

**В.Д. Директора друштва:** Драган Катуца

**Шифра делатности:** 7022

**Назив делатности:** Консултантске активности у вези с пословањем и осталим управљањем

Влада Републике Србије је 30. децембра 2016. године донела Одлуку о изменама и допунама Одлуке о оснивању Друштва с ограниченом одговорношћу за управљање Пројектом истраживање и развој у јавном сектору (05 Број: 02-02-12814/2016) којим се врши промена пословног имена Друштва у Друштво с ограниченом одговорношћу „Јединица за управљање пројектима у јавном сектору“ Београд. Трајање Друштва је дефинисано да обавља своју делатност на неодређено време, док се опис делатности Друштва у члану 8. Одлуке о оснивању Друштва (пречишћен текст) проширује, додаје нови став да Друштво обавља послове пружање услуга консалтинга, менаџмента и стручног надзора, као и свих других услуга у вези са управљањем пројектима у јавном сектору, који су му поверени међународним уговором, законом, актом оснивача или уговором којим се уређује начин реализације сваког пројекта, права и обавезе уговорних страна у реализацији, финансирање пројеката, рокови за реализацију, начин извештавања, јавне набавке које је потребно спровести и начин њихове реализације и други потребни елементи.

## 1.1 ВИЗИЈА ДРУШТВА

„Јединица за управљање пројектима у јавном сектору“ д.о.о. Београд као кључни партнер државе за реализацији инфраструктурних пројеката велике вредности.

## 1.2 МИСИЈА ДРУШТВА

Мисија Друштва је управљање великим државним инфраструктурним пројектима у складу са позитивним прописима у Републици Србији, у складу са међународним финансијским уговорима о кредитима/зајмовима/донацијама као и уговорима о финансирању и управљању пројектима потисаним са надлежним ауторитетима Републике Србије на основу којих се врши финансирање пројекта.


Своју мисију Друштво реализује кроз:

- Планирање реализације пројекта
- Припрему тендерске документације, организовање и евалуацију јавне набавке и потписивање уговора са изабраним понуђачима;
- Управљање изградом пројектне документације;
- Координацију активности и пружања административних услуга пројектним тимовима у односу на реализацију пројекта;
- Управљање процесом плаћања;
- Консалтинг услуге укључујући услуге архитектонске и техничке делатности и пружање услуга стручног надзора изградње;
- Вођење адекватних евиденција и извештавање надлежних институција о извршењу пројекта;
- Успостављање сарадње са домаћим и међународним институцијама које финансирају или су на други начин укључене у пројекат као и надлежним ауторитетима Републике Србије у циљу квалитетне реализације пројекта.

## 1.3 СТРАТЕГИЈА ДРУШТВА

Стратегија Друштва је позиционирање, умрежавање и унапређење односа са кључним актерима (Влада Републике Србије, надлежна Министарства, КИРС, Канцеларија за јавна улагања, општине и друге државне институције, Европска инвестициона банке, Банка за развој Савета Европе, привреда, научна заједница и грађани), пружање стручних услуга на пројектима, управљање, консалтинг и технички надзор и на тај начин стварање додане вредности неопходне за развој државе и друштвау целини.

## 1.4 ОРГАНИЗАЦИОНА СТРУКТУРА

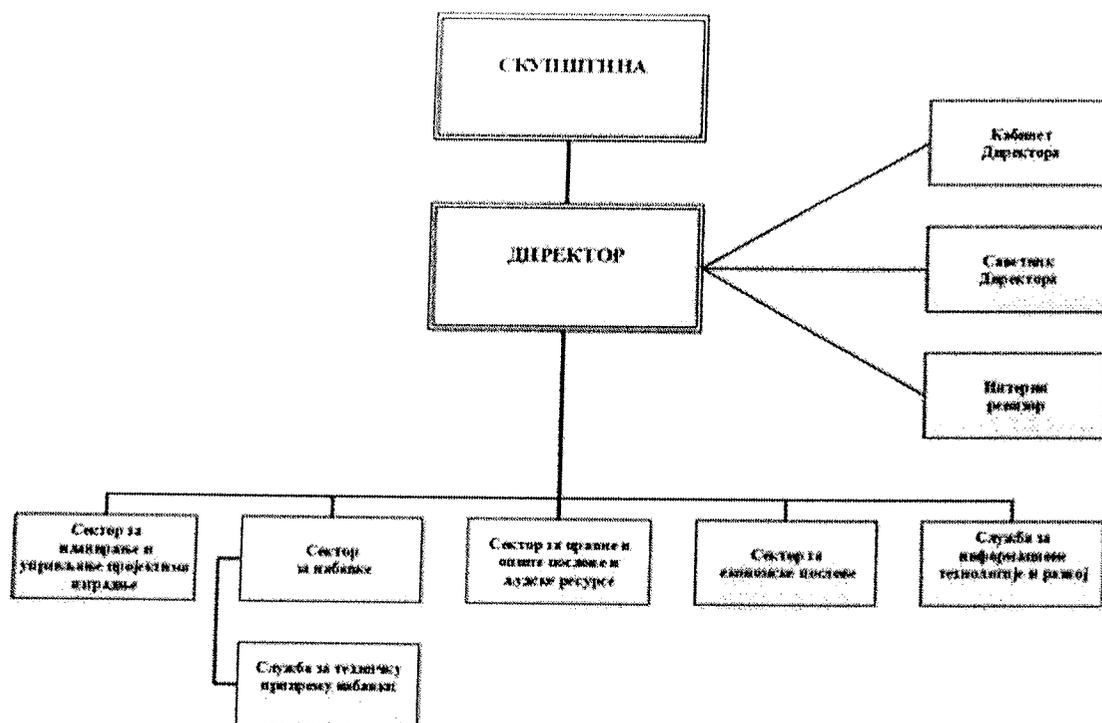

Организациона структура „Јединице за управљање пројектима у јавном сектору“ д.о.о. Београд утврђена је Правилником о организацији и систематизацији послова - радних места број: 14952 од 30.12.2016. године и изменама и допунама овог Правилника (Правилником о изменама и допунама Правилника о организацији и систематизацији радних места у “ЈУП Истраживање развој” д.о.о. Београд број 7522 од 27.11.2017. године, број 1931 од 04.04.2018. године, број 2212 од 23.04.2018. и број 6180 од 20.11.2018. године).

Полазећи од врсте послова и потребе да се на функционалном принципу обезбеди обављање сродних међусобно повезаних послова, Правилником су образоване основне организационе јединице, и то:

1. Кабинет директора Друштва;
2. Сектор за планирање и управљање пројектима изградње;
3. Сектор за набавке;
4. Сектор за правне и опште послове и људске ресурсе;
5. Сектор за економске послове;
6. Служба за информационе технологије и развој.

Ради обављања појединих врста сродних или истих међусобно повезаних послова, у оквиру Сектора за набавке, образује се унутрашња организациона јединица и то Служба за техничку припрему набавки.

Правилником о организацији и систематизацији послова предвиђено је самостални извршилац:

- Интерни ревизор.

## **2. РЕАЛИЗАЦИЈА И ПЛАНИРАНИ ОБИМ АКТИВНОСТИ ЗА 2019. ГОДИНУ (УПРАВЉАЊЕ ПОВЕРЕНИМ ПРОГРАМИМА И ПРОЈЕКТИМА)**

План рада привредног друштва „Јединица за управљање пројектима у јавном сектору“ д.о.о. Београд првенствено се односи на управљање пројектима у оквиру три програма:

### **ИСТРАЖИВАЊЕ И РАЗВОЈ У ЈАВНОМ СЕКТОРУ**

Први програм обухвата пројекте „Ревитализације истраживања и развоја у јавном сектору у Србији“, укључујући модернизацију постојећих истраживачких капацитета и инфраструктуре, формирање новог научног центра за унапређење научне писмености становништва, изградњу смештаја за студенте и младе научнике и модернизацију академске рачунарске мреже. Оквирна вредност Програма процењена је на износ ЕУР 420,8 милиона који се финансирају на следећи начин: из средстава кредита Европске инвестиционе банке (ЕИБ) у износу од ЕУР 200 милиона, из два зајма које је одобрила Развојне банке Савета Европе (ЦЕБ) на по ЕУР 35 милиона и ЕУР 70 милиона, Инструмента претприступне помоћи ЕУ (ИПА) у износу од ЕУР 25,6), остало из средстава Буџета Републике Србије и других извора.

Финансијским уговором (Истраживање и развој у јавном сектору) потписаним са ЕИБ-ом, предвиђено је да Република Србија образује јединицу за управљање оквирним Пројектом и да обезбеди средства за њено квалитетно функционисање за време трајања Програма, док је за промотера пројекта именовано Министарство просвете, науке и технолошког развоја. Првобитни рок за завршетак пројекта био је 31.12.2015. године али је рок продужен Анексом на период до краја 2020. године.

Влада РС је дана 13. јуна 2016. године донела Закључак 05 Број: 48-5555/2016 којим се сагласила да Канцеларија за управљање јавним улагањима преузме даље управљање пројектом док је Друштво у обавези да заврши све потписане уговоре са трећим лицима..

У оквиру програма „Истраживање и развој у јавном сектору“ квалификовано је, Стратегијом научног и технолошког развоја, 29 потпројеката за финансирање из средстава Европске инвестиционе банке, Банке за развој Савета Европе и других средстава које обезбеди Република Србија. За 20 предвиђених потпројеката закључени су Уговори о реализацији са Министарством просвете, науке и технолошког развоја.

Од тог броја, 7 потпројеката односно Уговора је реализовано, и то: Централна зграда Универзитета у Новом Саду, НТП Нови Сад 1. фаза, НТП Звездара Београд, Санација темеља Хемијски факултет у Београду, Природњачки центар Свилајнац, Истраживачка станица Петница и Станови за младе истраживаче у Блоку 32 (Фаза 1.).

За 3 потпројекта: Капитална опрема, Потрошни материјал и Станови за младе истраживаче Крагујевац, која су фактички завршена, остало је да се заврше финалне исплате по стицању услова за неколико уговора.

За 2 потпројекта, Центар за промоцију науке и Нано-Центар Београд завршено је пројектовање али пројекти нису добили позитивно мишљење од стране Ревизионе комисије. Промотер и друге надлежне институције се још увек нису дефинитивно изјаснили по питању наставка

њихове реализације. Обавеза ЈУП-а је да изврши финалне исплате (након стицања услова за исплату) по потписаним уговорима са испоручиоцима услуга.

У 2018. години у току је била реализација два потпројекта, и то Научно-технолошког парка Нови Сад (Фаза 2./1) и Центра изврсности у Крагујевцу.

Током 2018. године са Министарством просвете, науке и технолошког развоја потписани су Анекси везано за ова два потпројекта. Анексом је предвиђено да ће ЈУП реализовати и Фазу II/2 и II/2а Научно-технолошког парка Нови Сад у вредности од ЕУР 10 милиона, а за оба пројекта је продужен рок за реализацију до 2020. године.

Друштво је са Министарством просвете, науке и технолошког развоја потписало и Посебан споразум везано за Истраживачку станицу Петница којим је предвиђено извођење додатних радова на отклањању недостатака на објектима у вредности од РСД 5,8 милиона.

Везано за претходно наведено за 2019. и 2020. годину предвиђено је да Друштво реализује следеће потпројекте: Центар изврсности Крагујевац, Научно-технолошки парк Нови Сад Фаза 2/1, фаза 2/2 и фаза 2/2а и додатни радови на ИС Петница. Друштво је планом предвидело и набавку капиталне опреме у вредности од ЕУР 4 милиона за потпројекат Центри изврсности у Крагујевцу с обзиром да има потписан Уговор о реализацији овог потпројекта са Министарством и да исти није још увек ревидиран те та обавеза ЈУП-а остаје актуелна.

Програм рада за 2019. годину базиран на потписаним уговорима и анексима са Министарством просвете, науке и технолошког развоја о реализацији горе поменутих потпројеката у току, потписаним уговорима које Друштво има са трећим лицима и уговорима које Друштво планира да закључи ради завршетка започетих потпројеката.

## **РЕГИОНАЛНИ СТАМБЕНИ ПРОГРАМ**

Други програм обухвата пројекте „Националног дела регионалног програма о трајним решењима за избегла лица“.

Влада Републике Србије закључила је са Европском банком за развој Савета Европе (ЦЕБ) оквирни Уговор о спровођењу Програма чија вредност за Републику Србију износи ЕУР 335,2 милиона од чега су планирана средства донатора ЕУР 301,7 милиона, док Република Србија треба да обезбеди ЕУР 33,5 милиона кроз обезбеђење земљишта, инфраструктуре, дозвола и сл. Основним пројектним планом су предвиђене четири компоненте, и то: изградња стамбених зграда, изградња монтажних кућа, куповина сеоских домаћинстава и набавка грађевинског материјала за избегла лица. „Грант Уговори“ (уговори о донацији) потписују се сукцесивно на вредност потпројеката по динамици којом буду спремни за реализацију.

Првобитно је предвиђено да се Програм реализује до краја 2018. године, али је Скупштина донатора 2017. године одобрила куповину станова, као нови модалитет у спровођењу РХП пројекта Републике Србије. Донета је одлука да се шест Грант уговора који су потписани закључно са 2017. годином морају реализовати до краја 2019. године, а реализација пројеката СРБ 8 и СРБ 9 предвиђена је до краја 2021. године. У току је потписивање Грант уговора за пројекат СРБ 9 и Анекса за СРБ 3 и СРБ 8.

Комесаријат за избеглице и миграције Републике Србије (КИРС), Уговором одређен као „водећа институција“, задужен је за одређивање корисника подобних за помоћ из средстава донација и социјалну компоненту Програма, док је Јединица за управљање пројектима у

јавном сектору д.о.о. Београд задужена за материјалну реализацију Програма (спровођење поступака јавних набавки, потписивање и реализација уговора са понуђачима, управљање средствима донација, контролу реализације, извештавање и сл.).

Током 2014. године активности на овом Програму углавном су се односиле на избор корисника и стварање техничких и административних услова за реализацију. Током 2015. године су повучене прве транше средстава донација, завршене јавне набавке, потписани уговори са одабраним понуђачима. Програм је почео у 2016. години интензивно да се реализује на терену што је настављено и током 2017. и 2018. године.

## РЕАЛИЗАЦИЈЕ И ПЛАН ДАЉИХ АКТИВНОСТИ ПОТПРОЈЕКТА У ОКВИРУ РХП

### ПРВИ ПОТПРОЈЕКАТ (СРБ1)

#### Компонента 1- монтажне куће:

Потписани уговори у укупној вредности 978.917,18 евра. Извршена изградња и примопредаја 64 монтажних објекта. Добијено 59 употребних дозвола. У првом кварталу 2019. године, очекујемо да ћемо добити преосталих 5 употребних дозвола и затварање целокупне компоненте.

#### Компонента 2 - испорука и уградња грађевинског материјала

Потписани уговори у укупној вредности 733.657,88 евра. Извршена испорука 104 пакета грађевинског материјала. До краја године се очекује се целокупна уградња пакета грађевинског материјала и затварање целокупне компоненте.

### ДРУГИ ПОТПРОЈЕКАТ (СРБ2)

#### Компонента 1- додела стамбених решења:

Потписани уговори у укупној вредности 4.418.537,7 евра. 2018 године усељено је 40 корисника у Сремској Митровици. Завршена је изградња објекта у Параћину и очекује се усељење 20 породица у фебруару 2019. године. У првој половини 2019. године се очекује да се заврше радови и усеље корисници у преосталим јединицама локалне самоуправе (Бајина Башта – 20 породица, Вршац – 20 породица, Кикинда – 25 породица, Крушевац – 20 породица, Прокупље – 20 породица, Шабац – 25 породица, Шид – 10 породица). Овим ће се завршити реализација компоненте 1.

#### Компонента 2- монтажне куће

Потписани уговори у укупној вредности 1.909.864 евра. Крај реализација изградње монтажних кућа планирана је за 2019. годину. Изграђено и примопредато је 117 од 120 кућа, урађен је технички преглед за 70 кућа, а издато 20 употребних дозвола.

#### Компонента 3 - испорука и уградња грађевинског материјала-ГРАНТ ШЕМЕ

Потписани уговори у укупној вредности 2.230.369 евра за 20 Јединица локалне самоуправе. До краја 2018. године у седамнаест општина испоручено 225 пакета грађевинског материјала, од чега је 198 пакета уграђено. У 2019. години се очекује испорука и уградња грађевинског материјала у општинама Нови Београд, Темерин и Гроцка чиме би се завршила пуна реализација компоненте 3.

#### Компонента 4 - додела сеоских домаћинстава - ГРАНТ ШЕМЕ

Потписани уговори са јединицама локалне самоуправе у 2015. години у укупној вредности 2.750.000 евра. Укупно је купљено 245 сеоских домаћинстава. Почетком 2019. године очекује се додела пакета помоћи (мали грант) у општини Параћин и реализација компоненте 4.

#### ТРЕЋИ ПОТПРОЈЕКАТ (СРБЗ)

##### Компонента 1- додела стамбених решења-Овча 235 стамбених решења:

Потписани уговори у укупној вредности 5.004.412,35 евра. У марту 2018. године усељено је 235 породица.

##### Компонента 2- монтажне куће

Потписани уговори у укупној вредности 736.450 евра. Реализација изградње монтажних кућа планирана је за 2019. годину. Изграђено и примопредато је 19 од 49 објеката. Крај реализације се очекује у трећем кварталу 2019.

##### Компонента 3 - испорука и уградња грађевинског материјала

Потписани уговори у укупној вредности 73.732 евра. До краја 2018. године очекује се потписивање уговора са добављачима за испоруку 302 пакета грађевинског материјала. У 2019. години очекује се испорука, уградња и комплетна реализација компоненте 3.

##### Компонента 4 - додела сеоских домаћинстава

Укупно купљено 69 сеоских домаћинстава укупне вредности 640.000 евра и додељени су пакети грађевинског материјала у вредности 98.392,02 евра. У 2019 . години очекује се проширење пројекта СРБЗ, којим је предвиђено куповина 145 сеоских кућа (предвиђена решења у СРБ8 пребачена у СРБЗ да би се искористила уштеда на пројекту). Комплетна реализација компоненте 4 предвиђена је у 2019. години.

#### ЧЕТВРТИ ПОТПРОЈЕКАТ (СРБ4)

#### ОСНОВНИ УГОВОР

##### Компонента 1- додела стамбених решења:

Потписани уговори у укупној вредности 6.162.420 евра. 2018. године усељено је 15 породица у Ариљу. У првој половини 2019. године очекује се да се заврше радови и уселе корисници у преосталим јединицама локалне самоуправе (Бор – 15 породица, Брус – 10 породица, Кладово – 10 породица, Лозница – 30 породица, Неготин – 20 породица, Ужице – 20 породица, Врњачка Бања - 20 породица, Сомбор – 40 породица, Стара Пазова – 30 породица, Темерин – 20 породица, Зрењанин – 11 породица, Озаци – 20 породица) Овим ће се завршити реализација компоненте 1.

##### Компонента 2 – монтажне куће

Потписани уговори у укупној вредности 1.200.113 евра. Реализација изградње монтажних кућа прибављање употребних дозвола и примопредаја планирана је за 2019. годину. До краја 2018. године је завршено и примопредато 58 од 70 објеката. У току је технички преглед.

### Компонента 3- испорука и уградња грађевинског материјала

Потписани уговори у укупној вредности 2.442.680,19 евра. У централизованом моделу испоруке и уградње грађевинског материјала (ЈУП спроводи набавке и потписује уговоре са добављачима) додељено је 161 пакета помоћи. Комплетна уградња и реализација пројекта очекује се у 2019. години. У децентрализованом моделу (Јединице локалне самоуправе (ЈЛС) спровode набавке и потписују уговоре са добављачима) потписано је 36 уговора са ЈЛС, којим је предвиђена додела 402 пакета грађевинског материјала. У 2019. Години очекује се потписивање још 11 уговора са ЈЛС за 114 пакета грађевинског материјала. Комплекта уградња и реализација пројекта очекује се у 2019. години.

### Компонента 4 - додела сеоских домаћинстава -

Потписани уговори са 26 Јединица локалне самоуправе у укупној вредности 2.588.000 евра. Укупно је купљено 202 сеоске куће у 24 ЈЛС. Ради искориштавања уштеда из пројекта, планирано је анексирање 12 Уговора о гранту са ЈЛС (решења са пројекта СРБ8), којим је предвиђена куповина 76 сеоских кућа. У 2019. години очекује се укупна реализација компоненте 4.

### **ПЕТИ ПОТПРОЈЕКАТ (СРБ5)**

#### Компонента 1- додела стамбених решења:

Потписани уговори у укупној вредности 31.322.482,51 евра. У 2018. години почела је изградња објеката у 26 Јединица локалне самоуправе (Шожаревац – 20 породица, Београд (Земун-Камендин) – 270 породица, Мало Црниће – 6 породица, Жабари – 12 породица, Свилајнац – 15 породица, Крушевац – 40 породица, Ниш – 75 породица, Лозница – 60 породица, Крупањ – 5 породица, Уб – 20 породица, Ваљево – 20 породица, Мионица – 16 породица, Ужице – 10 породица, Чајетина – 12 породица, Нови Пазар – 20 породица, Темерин – 64 породице, Зрењанин – 40 породица, Бачка Паланка – 16 породица, Сремска Митровица – 30 породица, Ириг – 13 породица, Сремски Карловци – 16 породица, Панчево – 8 породица, Стара Пазова – 169 породица, Нови Сад – 276 породица, Бачки Петровац – 3 породице, Кикинда – 16 породица). Почетком 2019. године се очекује и потписивање уговора за објекат у Лучанима за 15 породица. Планиран крај реализације компоненте 1 је децембар 2019. године.

#### Компонента 2 - испорука и уградња грађевинског материјала - ГРАНТ ШЕМЕ

Потписани уговори о гранту у укупној вредности 1.863.000 евра са 11 ЈЛС. Испоручени пакети грађевинског материјала у 2 ЈЛС. У 2019. години очекује се испорука, уградња и укупна реализација компоненте.

#### Компонента 3-додела сеоских домаћинстава - ГРАНТ ШЕМЕ

Потписани уговори о гранту са 16 ЈЛС укупне вредности 2.651.000 евра. Укупно је купљено 193 сеоске куће. У 2019. години очекује се укупна реализација компоненте 3.

## СЕДМИ ПОТПОРЈЕКАТ (СРБ7)

### Компонента 1 – куповина 130 станова

Вредност 4.232.000 евра. Планиран крај реализације компоненте је 2019. година.

### Компонента 2- додела сеоских домаћинстава - ГРАНТ ШЕМЕ

Потписани уговори о гранту са 22 ЈЛС укупне вредности 1.980.000 евра. Укупно је купљено 140 сеоских кућа. У 2019. години очекује се укупна реализација компоненте 3.

### Компонента 3 – испорука и уградња грађевинског материјала

Пројекат предвиђа доделу 221 пакета грађевинског материјала. Потписивање уговора очекује се почетком 2019. године, а додела пакета, уградња и укупна реализација компоненте 3. очекује се до 2020, године.

### Компонента 4 – пројектовање 358 стамбених јединица

Потписани уговори у укупној вредности 654.345,29 евра.

У 2018. години је започело пројектовање објеката у 9 јединица локалне самоуправе (Врњачка Бања – 20 станова, Аранђеловац – 18 станова, Лозница – 30 станова, Ариље – 8 станова, Суботица – 44 стана, Вршац – 40 станова, Панчево – 40 станова, Бачки Петровац – 6 станова, Нови Сад – 152 стана). Планирани крај реализације ове активности је прва половина 2019. године (у овом потпројекту је предвиђена само израда техничке документације).

У 2018. години започело је у оквиру проширења потпројекта СРБ7 и пројектовање објеката у 9 јединица локалне самоуправе (Нови Сад – 94 стана, Пећинци – 15 станова, Смедерево – 20 станова, Смедеревска Паланка – 15 станова, Кучево – 6 станова, Варварин – 7 станова, Панчево – 36 станова, Краљево – 10 станова, Врбас – 14 станова), као и ажурирање техничке документације за 133 стана у Београду у улици др Ивана Рибара. Планирани крај реализације ове активности је прва половина 2019. године (у овом потпројекту је предвиђена само израда техничке документације).

## ОСМИ ПОТПОРЈЕКАТ

### Компонента 1 – додела стамбених решења:

Планирана вредност компоненте износи 18.452.329 евра. У овој компоненти се планира изградња 358 станова који се пројектују у потпројекту СРБ7. Планирани почетак изградње је у другој половини 2019. године, а планиран крај реализације ове активности је крај 2020. године.

У оквиру проширења потпројекта СРБ8 је у другој половини 2019. године планиран почетак изградње 250 стамбених јединица у Београду у насељу Овча. Процењена вредност ових радова износи 8.778.547,00 евра. Планирани крај компоненте је прва половина 2021. године.

### Компонента 2 – куповина 79 сеоских домаћинстава

Вредност 873.500 евра. Планиран крај реализације компоненте је 2020. година.

### Компонента 3 – набавка и уградња 135 пакета грађевинског материјала

Вредност 1.265.000 евра. Планиран крај реализације компоненте је 2020. година.

Компонента 4 – пројектовање и изградња 30 монтажних кућа

Вредност 502.000 евра. Планиран крај реализације компоненте је 2020. година.

#### ДЕВЕТИ ПОТПОРЈЕКАТ

Очекује се потписивање уговора СРБ9 ускоро.

Компоненте овог потпројекта су :

Компонента 1 – додела 350 стамбених решења

Вредност 9.652.832 евра. Планиран крај реализације компоненте је 2021. година.

Компонента 2 – куповина 100 станова

Вредност 3.255.000 евра. Планиран крај реализације компоненте је 2021. година.

Компонента 3 – куповина 200 сеоских домаћинстава

Вредност 2.228.000 евра. Планиран крај реализације компоненте је 2021. година.

Компонента 4 – набавка и уградња 200 пакета грађевинског материјала

Вредност 1.897.500 евра. Планиран крај реализације компоненте је 2021. година.

Компонента 5 – пројектовање и изградња 50 монтажних кућа

Вредност 808.325 евра. Планиран крај реализације компоненте је 2021. година.

#### ПРОГРАМ МОДЕРНИЗАЦИЈА ШКОЛА

Трећи програм који реализује ЈУП је „Програм модернизација школа“ који је дефинисан Финансијским уговором ФИ. Н 25.610 између Републике Србије и Европске инвестиционе банке, одобрен је зајам у износу од 50 милиона ЕУР-а у циљу модернизације образовања у Србији. Анексом 2 Финансијског уговора, потписаног у Београду, 6. марта 2017. године дефинисан је нови рок реализације Програма, као и крајњи рок за повлачење средстава зајма 31.12.2018. године. У току 2018. године покренута је процедура за анексирање Финансијског уговора. Као нови рок реализације Програма предложен је крај 2021. године. Промотер Пројекта је Министарство просвете, науке и технолошког развоја Републике Србије, а управљање оперативном реализацијом пројекта поверено је „Јединици за управљање пројектима у јавном сектору“ д.о.о. Београд.

Пројекат обухвата следеће три компоненте:

Компонента 1 – нова изградња односно проширење 8 основних и 2 средње школе као и набавка опреме за поменутих 10 школа и још 2 основне школе (Борча, Калуђерица) чија је изградња финансирана од стране локалне самоуправе, а радови завршени.

Компонента 2 – стратешки развој образовног система у Србији. Садржи три активности:

- Развој плана имплементације за Националну образовну стратегију, укључујући и учешће Србије у међународним тестирањима вредновања знања
- Подршка за завршетак концепције и имплементацију Информационог и система управљања у образовању (делимично суфинансираног зајмом Светске банке)
- Развој методологије за стратешко планирање улагања за образовну инфраструктуру

Компонента 3 – нова изградња односно адаптација основних и средњих школа са опремањем, како би се школама омогућило да адекватно функционишу и спроводе модеран наставни план и програм.

У оквиру ове фазе радови су подељени у четири групе:

Прва група радова обухвата изградњу, доградњу и адаптацију 50 +1 објекат ( ради се о Основној школи „Војвода Степе“ из Компоненте 1), радови на свим објектима су завршени, преостало је урадити коначне обрачунае и платити Окончане ситуације. Стручни надзор над радовима ради „Јединица за управљање пројектима у јавном сектору“ д.о.о. Опремање школа из ове групе је делимично завршено.

Друга група радова обухвата изградњу, доградњу и адаптацију 41-ног објекта, радови на овим објектима се приводе крају, уговорени су и сви непредвиђени радови. Стручни надзор над радовима ради „Јединица за управљање пројектима у јавном сектору“ д.о.о. Београд .

Трећа група радова обухвата изградњу, доградњу и адаптацију 31-ног објекта, радови на овој групи објеката су у току, уговорени су непредвиђени радови. Стручни надзор над радовима ради „Јединица за управљање пројектима у јавном сектору“ д.о.о. Београд .

Потписан је и Уговор о наставку радова на Основној школи „Љупче Николић“ у Алексинцу (наставак радова на школи из Компоненте 1), радови су завршени. Стручни надзор над радовима ради „Јединица за управљање пројектима у јавном сектору“ д.о.о. Београд.

Четврта група радова обухвата изградњу, доградњу и адаптацију 33 објекта подељено у 15 лотова. Јавна набавка за радове расписана је у 2018. години.

„Јединица за управљање пројектима у јавном сектору“ д.о.о. Београд на пословима Управљања пројектом ПРОГРАМ МОДЕРНИЗАЦИЈЕ ШКОЛА у 2019. години планира активности на следећи начин:

- Наставак реализације свих Уговора о извођењу радова који су у току, што укључује праћење реализације у техничком и финансијском смислу, као и вршење Стручног надзора по закљученим Споразумима
- Завршетак јавне набавке радова за Четврту групу школа у првом кварталу године и потписивање Уговора за извођење радова и отварање градилишта.
- У првом кварталу 2019. године неопходно је, пре свега, припремити тендерску документацију за набавку Опремања Друге групе школа. Након сагласности Банке спровести поступак набавке.
- Неопходно је са надлежним институцијама дефинисати форме и процедуре извештавања и коначних обрачуна вредности објеката који су предмет извођења радова и опремања као и питање обрачуна учешћа Републике Србије (податке и документацију

коју је потребно да доставе локалне самоуправе) у циљу утврђивања укупне додате вредности објеката.

- У току године, након добијања Пројектног задатка Јединственог информационог система просвете (део Компоненте 2) припремити и објавити Јавну набавку за реализацију овог дела Пројекта

## 2.1 ТЕРМИН ПЛАН

*Програми и пројекти којима управља „ЈУП Истраживање и развој“ д.о.о. Београд:*

1	ИСТРАЖИВАЊЕ И РАЗВОЈ У ЈАВНОМ СЕКТОРУ У СРБИЈИ – ЗАПОЧЕТИ ПРОЈЕКТИ ДО ЗАКЉУЧКА ВЛАДЕ 48-5555/2016 КОЈЕ ЈЕ ПОТРЕБНО ЗАВРШИТИ
2	НАЦИОНАЛНИ ДЕО РЕГИОНАЛНОГ ПРОГРАМА О ТРАЈНИМ РЕШЕЊИМА ЗА ИЗБЕГЛА ЛИЦА
3	ПРОГРАМ МОДЕРНИЗАЦИЈА ШКОЛА

### 1. РЕВИТАЛИЗАЦИЈЕ ИСТРАЖИВАЊА И РАЗВОЈА У ЈАВНОМ СЕКТОРУ У СРБИЈИ

ID	FOUND	WBS	Text1	09	10	11	12	13	14	15	16	17	18	19	20	21	22
0			Истраживање и развој														
1	EIB	PR001	Природњачки центар Свилајнац														
13	EIB	CEB1	PR016	Набавка капиталне опреме за истраживање													
17	EIB	PR023	Систем за централизовану набавку потрошног материјала														
24	EIB	PR003	Централна зграда Универзитета у Новом Саду														
33	EIB	PR004	Научно технолошки парк Звездара, Београд														
44	EIB	PR006	Научно технолошки парк, фаза I, Нови Сад														
53	EIB	PR008	Истраживачка станица Петница, Ваљево														
64	CEB1	PR010	Станови за младе истраживаче - Блок 32, Београд Фаза 1														
73	EIB	PR022	Санација темеља - Хенијски факултет Универзитета у Београду														
81	CEB2	PR009	Станови за младе истраживаче - Крагујевац														
92	EIB	PR030	Центри изврности Универзитета у Крагујевцу														
103	EIB	PR007	Научно технолошки парк, фаза II, Нови Сад														

### 2. НАЦИОНАЛНИ ДЕО РЕГИОНАЛНОГ ПРОГРАМА О ТРАЈНИМ РЕШЕЊИМА ЗА ИЗБЕГЛА ЛИЦА

Термин план за сваки потпројекат дат је у прилогу.

### 3. ПРОГРАМ МОДЕРНИЗАЦИЈА ШКОЛА

Термин план дат је у прилогу.

## 2.2 ПЛАНИРАНЕ АКТИВНОСТИ

Активности привредног друштва су планирање, реализација, праћење и контрола пројеката.

Ове активности обухватају:

- формирање комисија, радних група и пројектних тимова који ће бити одговорни за управљање пројектима;
- дефинисање система контроле времена, квалитета и трошкова;
- прописивање система комуникације и извештавања на пројектима;
- анализу трошкова, анализу и утврђивање термин плана реализације;
- израду пројектних задатака;
- израду шеме управљања пројектом;

### *Поступак набавки добара, услуга и радова обухвата*

- припрему и доношење одлуке о покретању поступка јавне набавке за избор добављача добара, пружаоца услуга пројектовања и избор извођача радова и формирање одговарајуће комисије за спровођење поступка и избор;
- припрему конкурсне документације, укључујући техничке и финансијске критеријуме за избор најповољнијег понуђача, у складу са Смерницама за набавке Европске инвестиционе банке, Упутством за набавке у оквиру Регионалног стамбеног програма, Законом о јавним набавкама („Службени гласник РС“ бр. 124/12,14/2015, 68/2015) и другим прописима којима је регулисана предметна материја;
- припрему и објављивање јавних позива за подношење понуда за набавку добара, пружање услуга пројектовања и извођења радова;
- спровођење поступка уступања услуга и/или радова, закључно са предлогом за избор најповољнијег понуђача, према дефинисаним и усвојеним критеријумима;
- спровођење поступка набавке добара, закључно са предлогом за избор најповољнијег понуђача, према дефинисаним и усвојеним критеријумима;
- припремање и закључење уговора о испоруци добара, извођењу радова и обављању услуга, између ЈУП-а и најповољнијих понуђача.

### *управљање израдом пројектне документације*

- контролу и праћење процеса израде пројектне документације;
- именовање вршиоца техничке контроле пројектне документације;
- прибављање свих потребних сагласности, одобрења, дозвола и сл. у складу са важећим законима неопходних за увођење извођача у посао.

### *управљање изградњом објеката*

- обезбеђење предуслова за прибављање грађевинске дозволе;
- увођење извођача у посао;
- одобравање детаљног термин плана извођења радова, а по потреби иницирање израде и одобравање ребаланса плана, као и оперативних месечних планова;
- праћење изградње објеката и предузимање свих потребних мера за извршавање планова;
- контролу правовременог наручивања тј. набавки компоненти које имају дужи рок производње тј. Испоруке;
- прибављање сертификата о осигурању радова и особља од извођача;

- уговарање и организовање стручног надзора над извођењем радова на градилиштима у току читавог периода изградње, сагласно Закону о планирању и изградњи, Правилнику о садржини и начину вођења књиге инспекције и грађевинског дневника и Правилнику о начину и поступку вршења стручног надзора у току грађења;
- вршење стручног надзора над извођењем радова на градилиштима у току читавог периода изградње, сагласно Закону о планирању и изградњи, Правилнику о садржини и начину вођења књиге инспекције и грађевинског дневника и Правилнику о начину и поступку вршења стручног надзора у току грађења;
- координацију рада са надлежним управама, инспекцијским службама, јавним предузећима и комуналним службама;
- издавање налога о техничким изменама и обезбеђивање сагласности на те измене;
- припремање процене радова: основних и додатних и њиховог утицаја на пројекат (финансије и рок) и рад на припреми елемената коначног обрачуна;
- формирање и учествовање у раду Комисије за технички преглед изведених радова на градилишту и сачињавање коначног обрачуна са извођачем радова;
- реализација свих финансијских трансакција у погледу плаћања извођачу радова, укључујући финалну исплату после коначног обрачуна, као и пријем гаранције којом се извођач обавезује на отклањање примедби у гарантном року;
- пријем сертификата противпожарне службе за изведене радове;
- издавање сертификата о примопредаји објеката;
- прибављање употребне дозволе;
- уколико је неопходно - израда Пројекта изведеног објекта;
- припрема потребне документације за упис објекта у земљишне књиге или катастар непокретности, као предуслова за појединачну укњижбу изграђених јединица објекта;
- ангажовање потребног броја извршилаца за праћење и обављање послова у периоду трајања гарантног рока од 2 године;
- организовање периодичних састанака са извођачима радова, извештавање о напредовању истих и мерама које се предузимају у циљу реализације пројекта у уговореним роковима;
- припреме извештаја за надлежне институције, Европску инвестициону банку и Банку за развој Савета Европе у вези са спровођењем пројекта.

### **2.3. КОМИСИЈЕ, РАДНЕ ГРУПЕ, ПРОЈЕКТНИ ТИМОВИ**

За сваки пројекат биће формиране комисије, радне групе или пројектни тимови од запослених у „Јединици за управљање пројектима у јавном сектору“ д.о.о. Београд и од спољних чланова из организација које учествују у реализацији пројекта. Чланови комисија, радних група и тимова су:

- Председник комисије / Руководилац радне групе / Руководилац тима;
- Чланови комисије / Чланови радне групе / Чланови пројектног тима;
- Директори сектора и координатори;
- Руководиоци пројекта спровођење грант шема и координатори пројекта (РСЦ);
- Руководиоци служби;
- Представници извођача;
- Стручни надзор;
- Представници локалне самоуправе;
- Представници осталих значајних, заинтересованих страна на пројекту.

## 2.4. УПРАВЉАЊЕ РИЗИЦИМА

Управљање ризицима је скуп поступака и метода за утврђивање, мерење односно процењивање, савладавање и праћење ризика, укључујући и извештавање о ризицима којима је „Јединица за управљање пројектима у јавном сектору“ д.о.о. Београд (у даљем тексту: Друштво) изложено или би могло бити изложено у свом пословању.

Утврђивање и процена ризика представља део система управљања ризицима којима Друштво идентификује ризике којима је изложено или би могло бити изложено, процењује интензитет утицаја ризика као и њихов потенцијални утицај на континуитет пословања Друштва и остварење постављених пословних циљева.

Ризик је било који догађај или проблем, чије би наступање могло неповољно утицати на остварење пословних, стратешких, оперативних и финансијских циљева Друштва. Пропуштене прилике такође се сматрају ризиком.

За утврђивање и процену утицаја ризика којима је Друштво изложено или би могло бити изложено примењује се:

1. Процена финансијског и пословног положаја Друштва, а која обухвата:
  - а) процену билансног стања Друштва,
  - б) процену будућих оперативних и других прихода и трошкова Друштва,
2. Анализа спољног окружења Друштва,
3. Анализа пословних процеса и критичних тачака у пословним процесима,
4. Анализа претходних информација и искустава,
5. Редовни колегијуми менаџмента Друштва,
6. Извештаји интерног ревизора,
7. Извештаји функције праћења усклађености с релевантним прописима,
8. Остале интерне евиденције и извештаји.

Матрица ризика:

Вероватноћа	Висока (3)	3	6	9
	Средња (2)	2	4	6
	Ниска (1)	1	2	3
		Мали (1)	Средњи (2)	Велики (3)
		Утицај		

Процена ризика у пословању Друштва врши се према матрици за мерење ризика 3x3, која има две врсте улазних информација – процене утицаја ризика и процене вероватноће појаве ризика. Укупна изложеност ризику добија се множењем бодова за утицај са бодовима за вероватноћу.

## 2.5. ИЗВЕШТАВАЊЕ

Током периода реализације започетих Пројеката истраживање и развој у јавном сектору у 2019. години, ЈУП ће организовати периодичне информативне састанке у циљу информисања представника Министарства просвете, науке и технолошког развоја о напретку у реализацији или евентуалним одступањима од плана и другим питањима која утичу на реализацију пројеката и подносити периодичне извештаје. За пројекте ће бити израђивани периодични извештаји о напретку пројекта.

У оквиру пројекта Националног дела регионалног програма о трајним решењима за избеглице и расељена лица извештавање ће се вршити у складу са упутством за имплементацију пројеката у оквиру Регионалног стамбеног програма на свака четири месеца, кроз информациони систем који је израђен за ово извештавање (ММИС).

Извештавање у оквиру пројеката Програм модернизације школа у Србији у 2019. години дефинисано је у складу са потписаним уговором са Министарством просвете, науке и технолошког развоја.

ПРЕДСЕДНИК СКУПШТИНЕ ДРУШТВА

НЕМАЊИЈА  
БЕОГРАД  
Наталија Дуговић




ТЕРМИН ПЛАН - ПРОГРАМ МОДЕРНИЗАЦИЈЕ ШКОЛА

ПРОГРАМ МОДЕРНИЗАЦИЈЕ ШКОЛА  
 период: 2019-2021.


No.	GLAVNE AKTIVNOSTI	Period																							
		2019												2020											
		1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12
<b>I КОМПОНЕНТА 1</b>		1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12
В Оријентације																									
OS Црвена Милоси, Апатинас - Испорука опреме																									
<b>II КОМПОНЕНТА 2</b>		1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12
AG ШКОЛ - Јединствени информациони систем у пројекту***																									
<b>III КОМПОНЕНТА 3 - радони</b>		1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12
A																									
1																									
PRVA GRUPA ШКОЛА - 50 објекта - изградња примострепу																									
A																									
1																									
ЧЕТВРТА ГРУПА ШКОЛА - 33 објекта																									
2																									
Услуга стручних надзора - четврта група школа																									
B																									
5																									
Извођење радова (укључујући и означавање раскове коначног борачуња)																									
1																									
PRVA GRUPA ШКОЛА																									
2																									
DRUGA GRUPA ШКОЛА																									
3																									
TREĆA GRUPA ШКОЛА																									
4																									
ЧЕТВРТА ГРУПА ШКОЛА																									
6																									
СТРУЧНИ НАДЗОР																									
1																									
PRVA GRUPA ШКОЛА																									
2																									
DRUGA GRUPA ШКОЛА																									
3																									
TREĆA GRUPA ШКОЛА																									
4																									
ЧЕТВРТА ГРУПА ШКОЛА																									
<b>III КОМПОНЕНТА 3 - Опремање</b>		1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12
A																									
1																									
Набавке																									
1																									
Припрема података о потражњи опреме-друга група																									
2																									
DRUGA GRUPA ШКОЛА																									
3																									
TREĆA GRUPA ШКОЛА***																									
6																									
Испорука опреме																									
1																									
DRUGA GRUPA ШКОЛА																									
2																									
TREĆA GRUPA ШКОЛА***																									
<b>ПРИКОЉАЊЕ ПОДАТАКА О УЧЕЊУ РЕПУБЛИКЕ СРБИЈЕ У ПРОЈЕКТУ</b>		1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12
A																									
1																									
Набавке																									
1																									
Припрема података о потражњи опреме-друга група																									
2																									
DRUGA GRUPA ШКОЛА																									
3																									
TREĆA GRUPA ШКОЛА***																									
6																									
Испорука опреме																									
1																									
DRUGA GRUPA ШКОЛА																									
2																									
TREĆA GRUPA ШКОЛА***																									

\*\*\* потражна дефиниција динамичу активности  
 означени радови за коначни обрачу  
 потражње набави





**RHP: CHP SERBIA - SRB 1.2.2 - PROVISION OF 104 PACKAGES OF BUILDING MATERIAL**  
**- BASELINE AND ACTUAL SCHEDULE.**

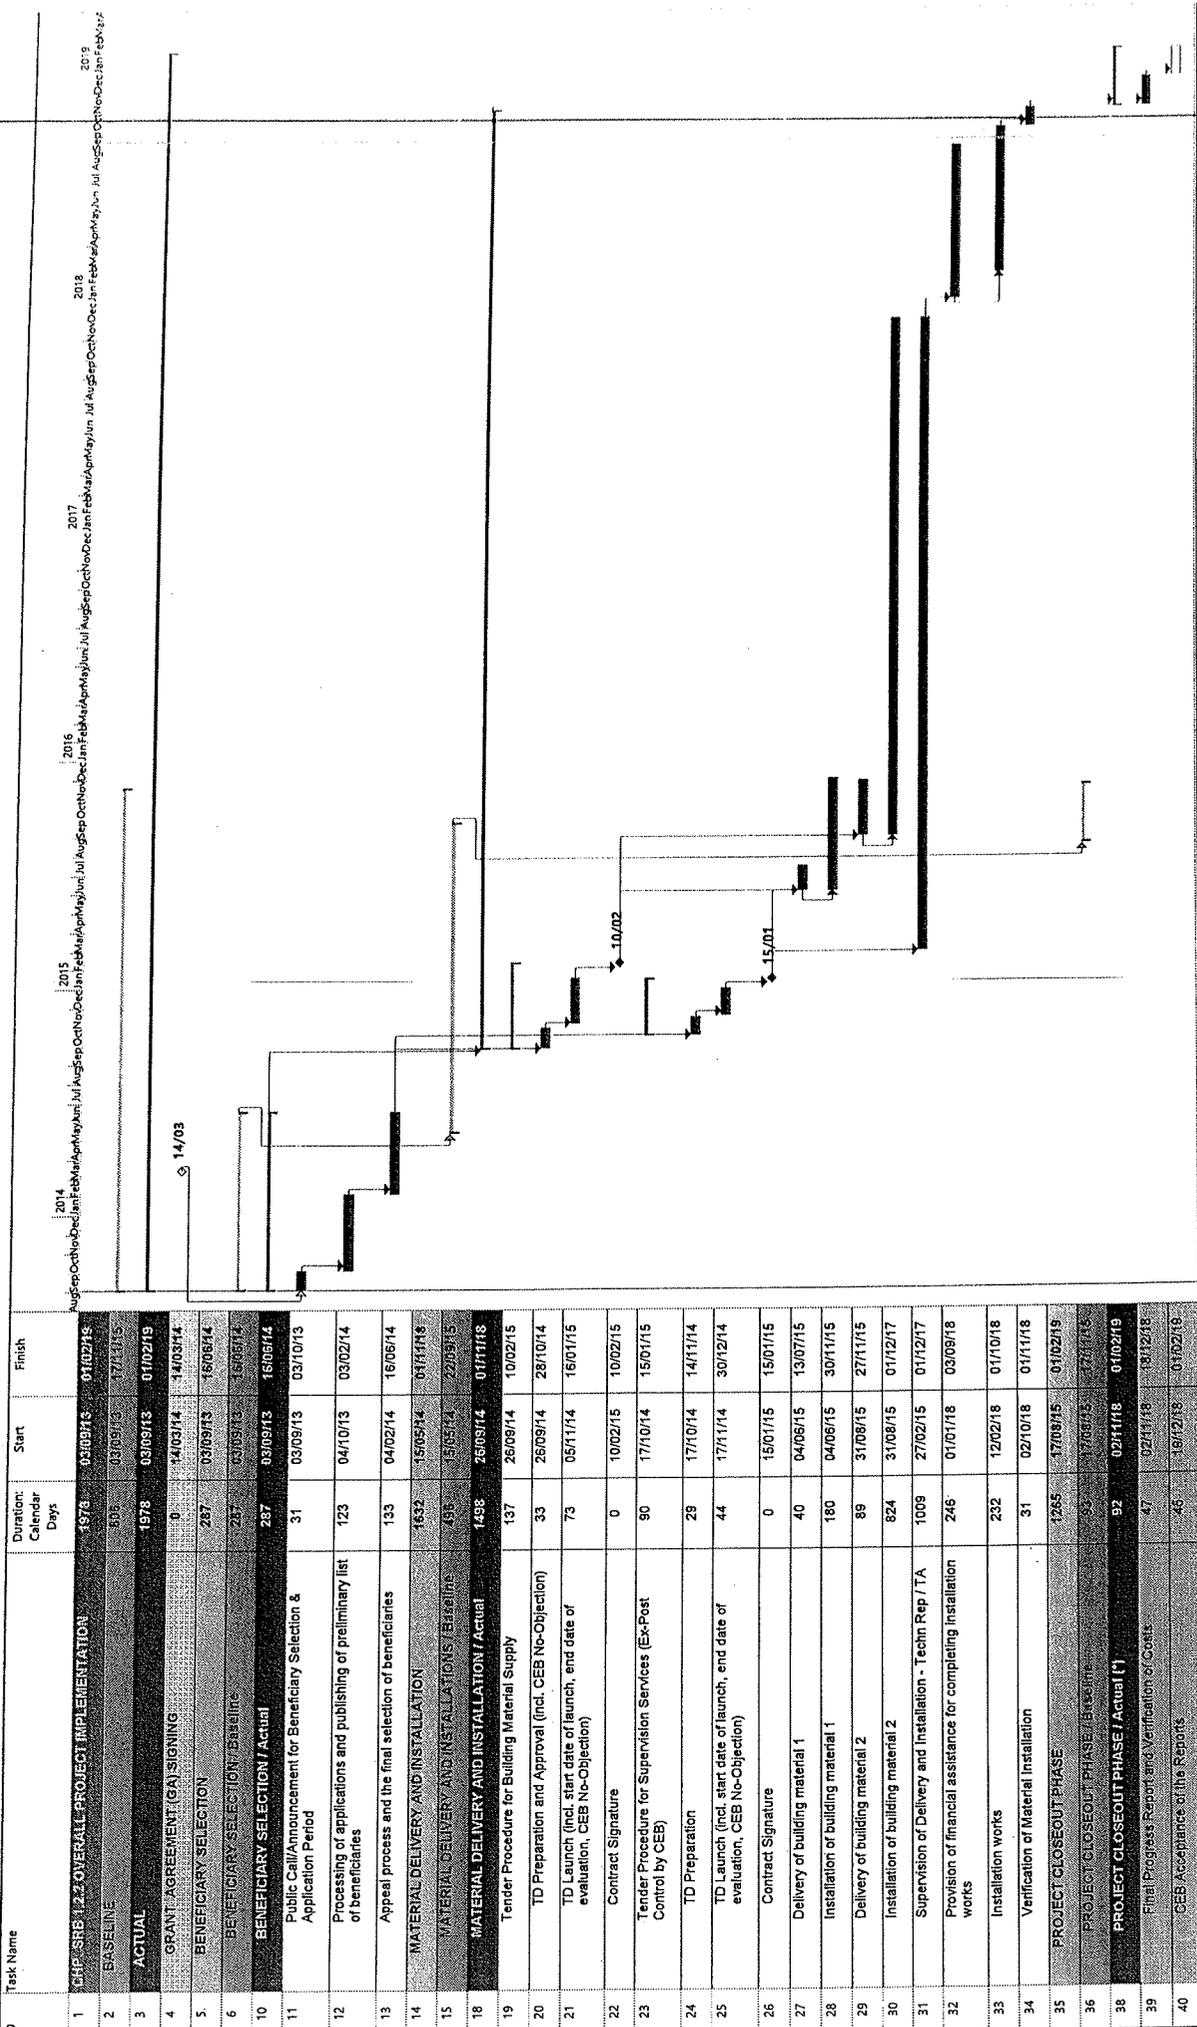

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP: SRB 1.2.2 OVERALL PROJECT IMPLEMENTATION	1876	03/09/13	01/02/19
2	BASELINE	509	03/09/13	17/11/15
3	ACTUAL	1978	03/09/13	01/02/19
4	GRANT AGREEMENT SIGNING	0	14/03/14	14/03/14
5	BENEFICIARY SELECTION	287	03/09/13	16/06/14
6	BENEFICIARY SELECTION / Baseline	25	03/09/13	16/06/14
10	BENEFICIARY SELECTION / Actual	287	03/09/13	16/06/14
11	Public Call/Announcement for Beneficiary Selection & Application Period	31	03/09/13	03/10/13
12	Processing of applications and publishing of preliminary list of beneficiaries	123	04/10/13	03/02/14
13	Appeal process and the final selection of beneficiaries	133	04/02/14	16/06/14
14	MATERIAL DELIVERY AND INSTALLATION	1632	15/05/14	01/11/18
15	MATERIAL DELIVERY AND INSTALLATION / Baseline	493	15/05/14	22/05/15
18	MATERIAL DELIVERY AND INSTALLATION / Actual	1498	26/09/14	01/11/18
19	Tender Procedure for Building Material Supply	137	26/09/14	10/02/15
20	TD Preparation and Approval (incl. CEB No-Objection)	33	26/09/14	28/10/14
21	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	73	05/11/14	16/01/15
22	Contract Signature	0	10/02/15	10/02/15
23	Tender Procedure for Supervision Services (Ex-Post Control by CEB)	80	17/10/14	15/01/15
24	TD Preparation	29	17/10/14	14/11/14
25	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	44	17/11/14	30/12/14
26	Contract Signature	0	15/01/15	15/01/15
27	Delivery of building material 1	40	04/06/15	13/07/15
28	Installation of building material 1	180	04/06/15	30/11/15
29	Delivery of building material 2	89	31/08/15	27/11/15
30	Installation of building material 2	824	31/08/15	01/12/17
31	Supervision of Delivery and Installation - Techn Rep / TA	1009	27/02/15	01/12/17
32	Provision of financial assistance for completing installation works	246	01/01/16	03/09/18
33	Installation works	232	12/02/16	01/10/18
34	Verification of Material Installation	31	02/10/16	01/11/16
35	PROJECT CLOSEOUT PHASE	1255	17/08/15	01/02/19
36	PROJECT CLOSEOUT PHASE / Baseline	93	17/08/15	27/11/15
38	PROJECT CLOSEOUT PHASE / Actual (*)	92	02/11/16	01/02/19
39	Final Progress Report and Verification of Costs	47	02/11/16	13/12/16
40	CEB Acceptance of the Reports	45	16/12/16	01/02/19

Project: SRB 1.2.2  
 Provision of 104 BM  
 Date: 12/9/2018


Actual Task Timeline: [Bar chart showing actual task progress]  
 Grant Agreement Signing: [Bar chart showing grant agreement signing progress]  
 Estimated Project Activities Summary: [Bar chart showing estimated project activities summary]  
 Actual Project Activities Summary: [Bar chart showing actual project activities summary]

Progress: [Bar chart showing progress]  
 Group of Activities: [Bar chart showing group of activities]

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframes within the same Sub-project.

Page 3

RHP: CHP SERBIA - SRB 2.1 - CONSTRUCTION OF BUILDING W/ 200 APARTMENTS  
- BASELINE AND ACTUAL SCHEDULE.

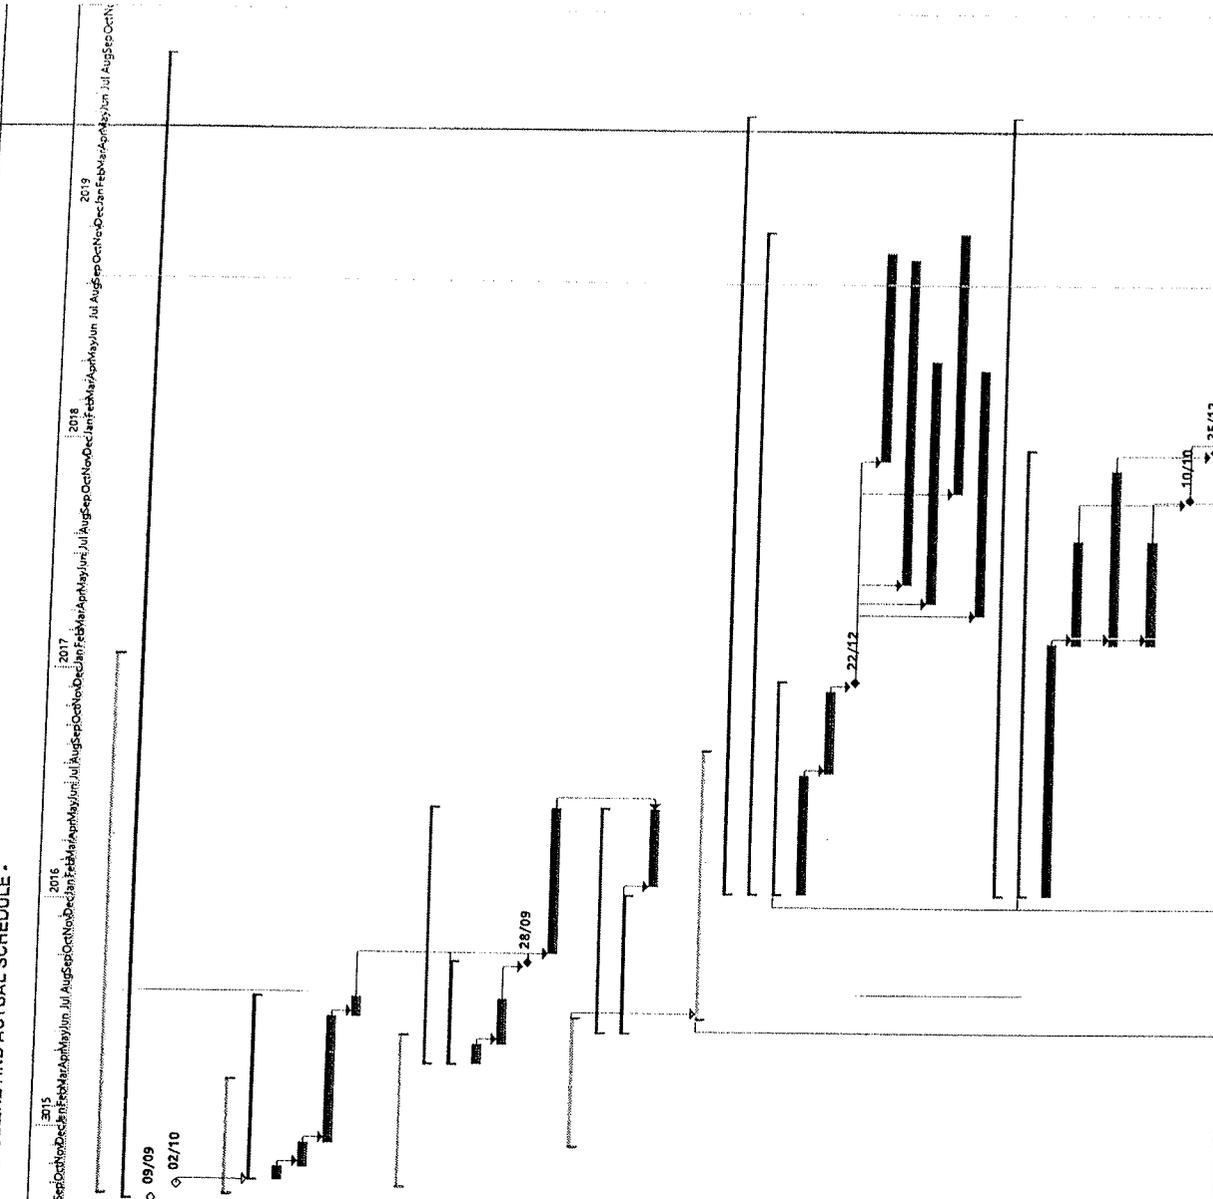

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP: SRB 2.1 OVERALL PROJECT IMPLEMENTATION	1822	09/09/14	04/08/19
2	BASELINE	35	17/09/14	21/09/14
5	ACTUAL	1822	09/09/14	04/08/19
6	GRANT AGREEMENT (GA) SIGNING	0	09/09/14	09/09/14
7	SCRIPULL-IG AGREEMENT SIGNING	0	02/10/14	02/10/14
8	BENEFICIARY SELECTION	318	17/09/14	31/07/15
9	BENEFICIARY SELECTION / Baseline	124	17/09/14	13/09/15
14	BENEFICIARY SELECTION / Actual	235	10/10/14	31/07/15
15	Public Call/Announcement for Beneficiary Selection	22	10/10/14	31/10/14
16	Application Period	40	31/10/14	09/12/14
17	Processing of applications and publishing of preliminary list of beneficiary	203	10/12/14	30/06/15
18	Appeal process and the final selection of beneficiaries	31	01/07/15	31/07/15
19	DESIGN & REVIEW SERVICES	608	01/10/14	30/05/16
20	DESIGN / Baseline	24	01/10/14	01/05/15
23	DESIGN / Actual	410	17/04/15	30/05/16
24	Tender procedure for Design service	164	17/04/15	28/09/15
25	TD Preparation and Approval (incl. CEB No-Objection)	32	17/04/15	18/05/15
26	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	73	19/05/15	30/07/15
27	Contract Signature	0	28/09/15	28/09/15
28	Design service	232	12/10/15	30/05/16
29	REVIEW OF DESIGN / Baseline	205	08/07/15	01/07/15
32	REVIEW OF DESIGN / Actual	358	08/06/15	30/05/16
33	Tender procedure for Review of Design	220	08/06/15	14/01/16
37	Review of design	123	29/07/16	30/05/16
38	CONSTRUCTION WORKS & SUPERVISION SERVICE	1436	02/07/15	05/05/19
39	CONSTRUCTION WORKS / Baseline	177	21/07/15	21/08/16
42	CONSTRUCTION WORKS / Actual	1236	18/01/16	06/08/19
43	CONSTRUCTION WORKS (Actual (Lots: 2.4.5.6.7))	1051	18/01/16	03/12/18
44	Tender procedure for Construction works (Lots: 2.4.5.6.7)	339	18/01/16	22/12/16
45	TD Preparation and Approval (incl. CEB No-Objection)	190	18/01/16	25/07/16
46	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection Lot1)	131	28/07/16	06/12/16
47	Contract Signature	0	22/12/16	22/12/16
48	Construction Works (Lot2 Vrsac)	331	07/12/17	02/11/18
49	Construction Works (Lot4 Knusevac)	515	26/05/17	22/10/18
50	Construction Works (Lot5 Paracin)	384	26/04/17	14/05/18
51	Construction Works (Lot6 Prokuplje)	412	18/10/17	03/12/18
52	Construction Works (Lot7 S.Mitrovice)	389	07/04/17	30/04/18
53	CONSTRUCTION WORKS / Actual (Lots: 1.3.8.9)	1236	18/01/16	06/06/19
54	Tender procedure for Construction works (Lots: 1.3.8.9)	707	18/01/16	25/12/17
55	TD Preparation and Approval (incl. CEB No-Objection)	401	18/01/16	21/02/17
56	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection Lot1)	165	21/02/17	04/08/17
57	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection Lots)	276	21/02/17	23/11/17
58	TD Launch Lot8 (incl. start date of launch, end date of evaluation, CEB No-Objection Lots)	165	21/02/17	04/08/17
59	Contract Signature Lot1	0	10/10/17	10/10/17
60	Contract Signature Lot3	0	25/12/17	25/12/17


Project: SRB 2.1  
 Construction of Buildings w/ 200 Apts  
 Date: 14/9/2018

Legend:  
 Actual Task/Timeframe  
 Grant Agreement Signing  
 Estimated Project Activities Summary  
 Actual Project Activities Summary

Progress  
 Group of Activities

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

RHP: CHP SERBIA - SRB 2.1 - CONSTRUCTION OF BUILDING W/ 200 APARTMENTS  
- BASELINE AND ACTUAL SCHEDULE -

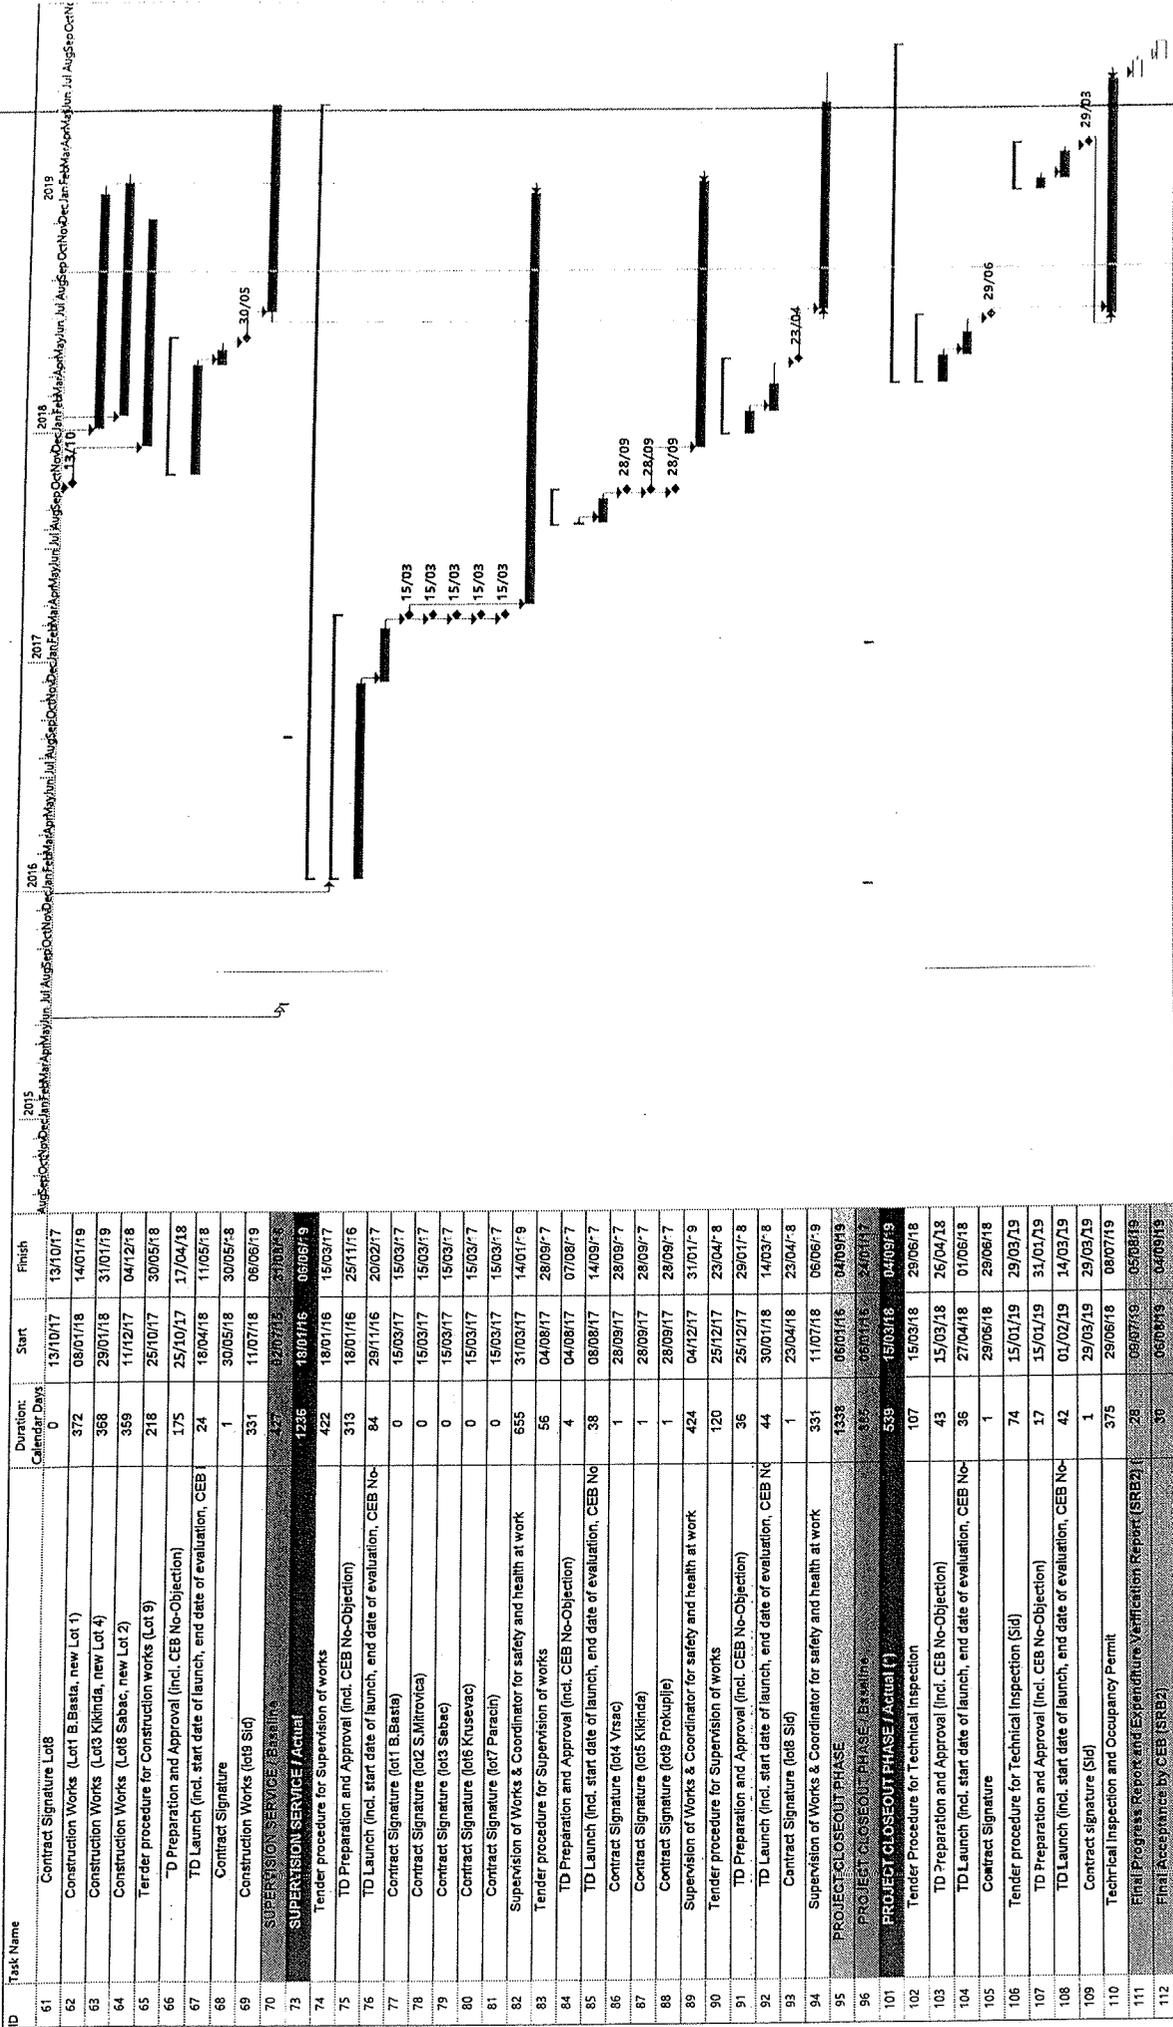

ID	Task Name	Start	Finish	Duration: Calendar Days
61	Contract Signature Lot8	13/10/17	13/10/17	0
62	Construction Works (Lot1 B.Basac, new Lot 1)	08/01/18	14/01/19	372
63	Construction Works (Lot3 Kikinda, new Lot 4)	29/01/18	31/01/19	368
64	Construction Works (Lot8 Sabac, new Lot2)	11/12/17	04/12/18	359
65	Tender procedure for construction works (Lot 9)	25/10/17	30/05/18	218
66	TD Preparation and Approval (incl. CEB No-Objection)	25/10/17	17/04/18	175
67	TD Launch (incl. start date of launch, end date of evaluation, CEB	18/04/18	11/05/18	24
68	Contract Signature	30/05/18	30/05/18	1
69	Construction Works (lot8 Sid)	11/07/18	06/06/19	331
70	<b>SUPERVISION SERVICE (Actual)</b>	<b>18/01/18</b>	<b>08/06/19</b>	<b>422</b>
71	Tender procedure for Supervision of works	18/01/18	15/03/17	422
72	TD Preparation and Approval (incl. CEB No-Objection)	18/01/18	25/11/16	313
73	TD Launch (incl. start date of launch, end date of evaluation, CEB No-	29/11/16	20/02/17	84
74	Contract Signature (lot1 B.Basac)	15/03/17	15/03/17	0
75	Contract Signature (lot2 S.Mitrovica)	15/03/17	15/03/17	0
76	Contract Signature (lot3 Sabac)	15/03/17	15/03/17	0
77	Contract Signature (lot6 Krusevac)	15/03/17	15/03/17	0
78	Contract Signature (lot7 Paracit)	15/03/17	15/03/17	0
79	Supervision of Works & Coordinator for safety and health at work	31/03/17	14/01/19	655
80	Tender procedure for Supervision of works	04/08/17	28/09/17	56
81	TD Preparation and Approval (incl. CEB No-Objection)	04/08/17	07/08/17	4
82	TD Launch (incl. start date of launch, end date of evaluation, CEB No	08/08/17	14/09/17	33
83	Contract Signature (lot4 Vrsac)	28/09/17	28/09/17	1
84	Contract Signature (lot5 Kikinda)	28/09/17	28/09/17	1
85	Contract Signature (lot6 Prokuplje)	28/09/17	28/09/17	1
86	Supervision of Works & Coordinator for safety and health at work	04/12/17	31/01/19	424
87	Tender procedure for Supervision of works	25/12/17	23/04/18	120
88	TD Preparation and Approval (incl. CEB No-Objection)	25/12/17	29/01/18	36
89	TD Launch (incl. start date of launch, end date of evaluation, CEB No	30/01/18	14/03/18	44
90	Contract Signature (lot8 Sid)	23/04/18	23/04/18	1
91	Supervision of Works & Coordinator for safety and health at work	11/07/18	06/05/19	331
92	PROJECT CLOSURE PHASE	06/01/18	04/09/19	1338
93	PROJECT CLOSURE PHASE (Baseline)	06/01/18	24/01/17	332
94	PROJECT CLOSURE PHASE (Actual)	15/03/18	04/09/19	539
95	Tender Procedure for Technical Inspection	107	15/03/18	107
96	TD Preparation and Approval (incl. CEB No-Objection)	15/03/18	29/06/18	43
97	TD Launch (incl. start date of launch, end date of evaluation, CEB No-	27/04/18	01/06/18	36
98	Contract Signature	29/06/18	29/06/18	1
99	Tender procedure for Technical Inspection (Sid)	15/01/19	29/03/19	74
100	TD Preparation and Approval (incl. CEB No-Objection)	15/01/19	31/01/19	17
101	TD Launch (incl. start date of launch, end date of evaluation, CEB No-	01/02/19	14/03/19	42
102	Contract Signature (Sid)	29/03/19	29/03/19	1
103	Technical Inspection and Occupancy Permit	29/06/18	08/07/19	375
104	Final Progress Report and Expenditure Verification Report (SRB2)	09/07/19	05/08/19	28
105	Final Acceptance by CEB (SRB2)	06/08/19	04/09/19	30

Project: SRB 2.1  
Construction of Buildings w/ 200 Apts  
Date: 14/9/2018

Actual Task Timeframe  
Grant Agreement Signing

Estimated Project Activities Summary  
Actual Project Activities Summary

Progress  
Group of Activities

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA - SRB 2.2 - CONSTRUCTION OF 120 PRE-FAB HOUSES - BASELINE AND ACTUAL SCHEDULE.**


ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 2.2 OVERALL PROJECT IMPLEMENTATION	737	01/09/14	03/06/19
2	BASELINE	694	01/09/14	25/07/16
3	ACTUAL	1737	01/09/14	03/06/19
4	GRANT AGREEMENT(S) SIGNING	0	09/09/14	09/09/14
5	BENEFICIARY SELECTION			
6	BENEFICIARY SELECTION / Baseline	246	01/09/14	04/05/16
10	BENEFICIARY SELECTION / Actual	284	06/10/14	16/07/16
11	Public Call/A announcement for Beneficiary Selection & Application Period	74	06/10/14	18/12/14
12	Processing of applications and publishing of preliminary list of beneficiaries	177	22/12/14	18/06/16
13	Appeal process and the final selection of beneficiaries	45	02/06/16	16/07/16
14	DESIGN-BUILD & TECH SUPERVISION			
15	DESIGN-BUILD & TECH SUPERVISION / Baseline	576	27/10/14	24/05/16
18	DESIGN-BUILD & TECH SUPERVISION / Actual	1245	04/12/15	01/05/19
19	Tender Procedure for Design-Build	172	04/12/15	24/05/16
20	TD Preparation and Approval (incl. CEB No-Objection)	51	04/12/15	23/01/16
21	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Ob)	81	26/01/16	15/04/16
22	Contract Signature (Lot #4)	1	16/05/16	16/05/16
23	Contract Signature (Lot #1,2,3)	0	24/05/16	24/05/16
24	Design-Build (Lot #4)	917	28/06/16	31/12/18
25	Design-Build (Lot #1,2,3)	1002	03/08/16	01/05/19
26	Tender for supervision services	122	04/12/15	04/04/16
27	TD Preparation and Approval (incl. CEB No-Objection)	33	04/12/15	05/01/16
28	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Ob)	69	08/01/16	16/03/16
29	Contract Signature	0	04/04/16	04/04/16
30	Technical supervision for Design-Build-Install Coordinator for safety & health	1038	28/06/16	01/05/19
31	PROJECT CLOSEOUT			
32	PROJECT CLOSEOUT PHASE / Baseline	163	21/01/16	23/07/16
35	PROJECT CLOSEOUT PHASE / Actual	655	18/08/17	03/05/19
36	Tender for Technical Inspection	105	18/08/17	30/11/17
37	TD Preparation and Approval (incl. CEB No-Objection)	4	18/08/17	21/08/17
38	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Ob)	67	22/08/17	27/10/17
39	Contract Signature	1	30/11/17	30/11/17
40	Technical Acceptance and Hand Over (incl. Tech. Inspection)	489	31/01/18	09/06/19

Project: SRB 2.2  
 Provision of 120 Pre-Fab H.  
 Date: 14/9/2018

Actual Task Timeframe  
 Grant Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary


Progress  
 Group of Activities



(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-Project.

RHP: CHP SERBIA - SRB 2.3 - PROVISION OF 250 BUILDING MATERIAL PACKAGES (20 LSCG) - BASELINE & ACTUAL SCHEDULE -


ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP: SRB 2.3: OVERALL PROJECT IMPLEMENTATION			
2	BASIS	31	18/09/18	19/10/18
3	ACTUAL	1822	05/09/14	05/09/19
4	GRANT AGREEMENT SIGNING	0	09/09/14	09/09/14
5	PROCUREMENT PLAN (GRANT SCHEME)			
6	PROCUREMENT PLAN (GRANT SCHEME) / Baseline	11	17/09/14	02/10/14
10	PROCUREMENT PLAN (GRANT SCHEME) / Actual	43	31/10/14	12/12/14
12	Review of Draft PAF Procurement Plan (CEB)	5	01/12/14	05/12/14
13	PAF Procurement Plan - No Objection Note #1 (CEB)	5	08/12/14	12/12/14
14	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE			
15	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE / Baseline	120	06/10/14	17/02/15
19	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE / Actual	320	16/12/14	31/10/15
20	Publication of Grant Working Program	0	16/12/14	16/12/14
21	Preparation and publication of Calls for proposals	71	16/12/14	24/02/15
22	Collection of applications	30	24/02/15	26/03/15
23	Processing of applications and signing contracts w/ local government	219	26/03/15	31/10/15
24	MATERIAL DELIVERY AND INSTALLATION			
25	Tender Procedures for Technical Representatives (Ex-Amp Control by CEB) / Baseline	155	05/10/14	09/03/15
27	Tender Procedures for Technical Representative (Ex-Amp Control by CEB) / Actual	134	08/06/15	20/10/15
28	TD Preparation and Approval (incl. CEB No-Objection)	32	08/06/15	09/07/15
29	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	71	10/07/15	18/09/15
30	Contract Signature	0	20/10/15	20/10/15
31	GRANT IMPLEMENTATION (LSGs)			
32	GRANT IMPLEMENTATION (LSGs) / Baseline	264	10/08/15	15/11/15
37	GRANT IMPLEMENTATION (LSGs) / Actual	1516	30/12/15	06/08/19
38	Selection of Beneficiaries (LSGs)	885	30/12/15	14/09/18
39	Secondary Procurement Procedure for Building Material Supply	882	20/07/16	19/12/18
40	Material Delivery and Installations (LSGs)	877	13/03/17	06/08/19
41	Supervision of Material Delivery and Installation	877	13/03/17	06/08/19
42	PROJECT CLOSURE PHASE			
43	PROJECT CLOSURE PHASE / Baseline	112	25/07/15	15/11/15
45	PROJECT CLOSURE PHASE / Actual (*)	30	06/08/19	05/09/19
46	Verification of Material Installation	30	06/08/19	05/09/19

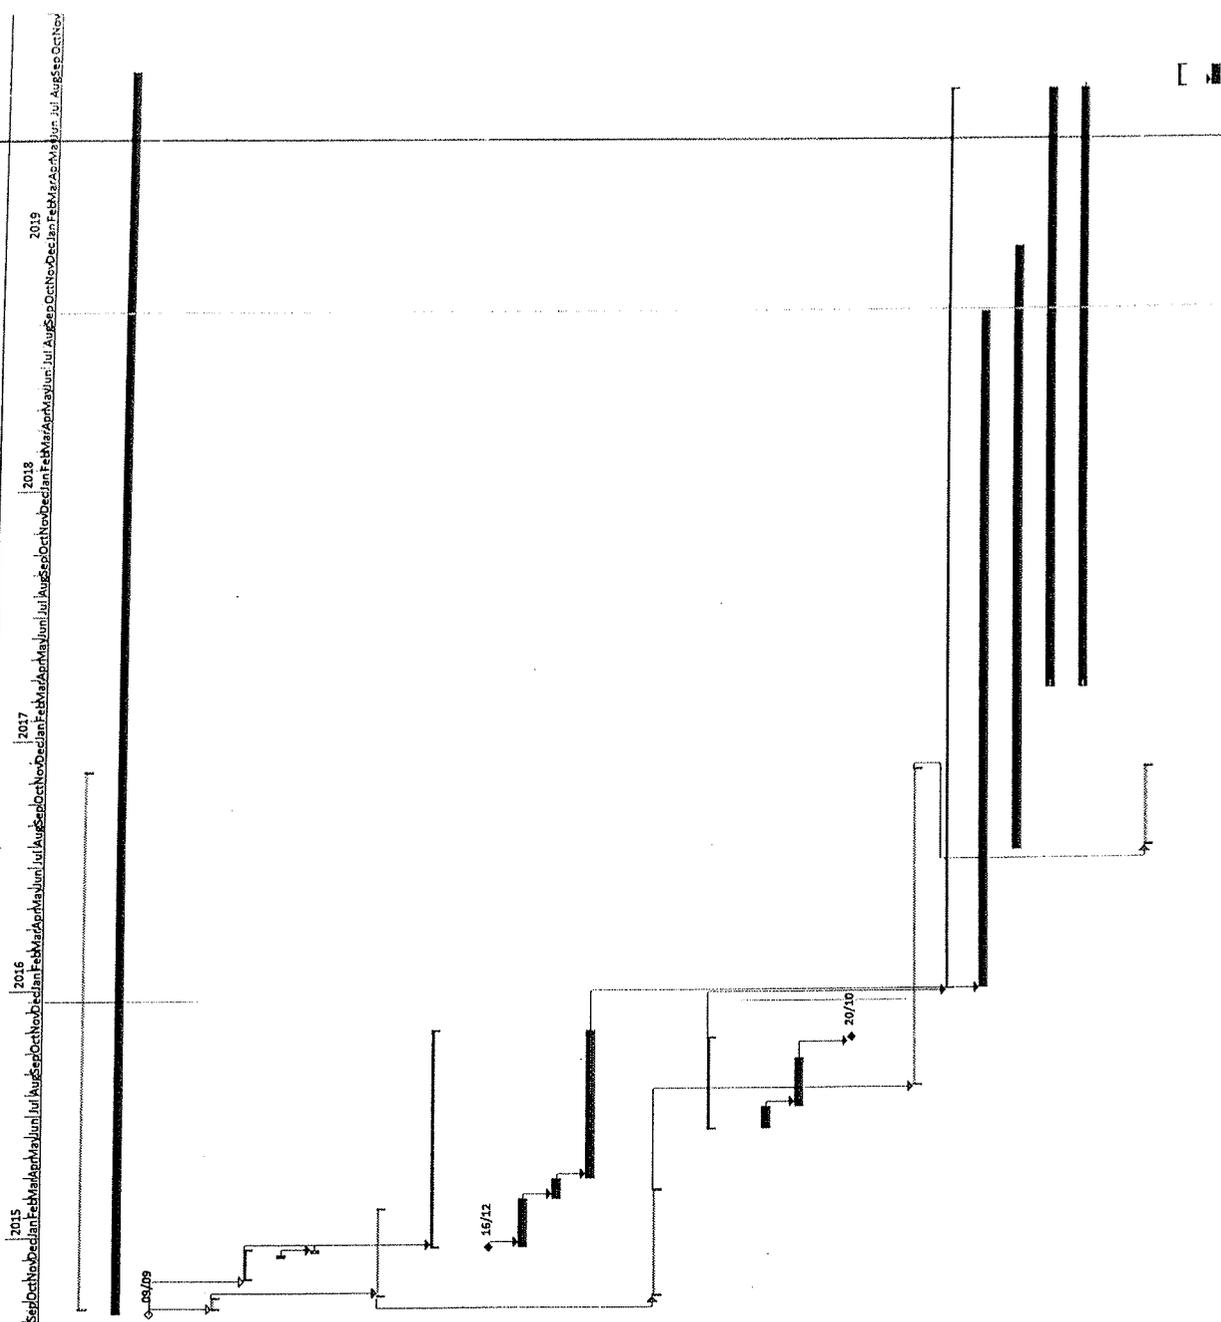

Project: SRB 2.3  
Provision of 250 BM Packages (20 LSCG)  
Date: 14/9/2018

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-Project.

**RHP: CHP SERBIA - SRB 2.4 - PURCHASING OF 250 VILLAGE HOUSES (20 GRANT CONTRACTS)  
- BASELINE & ACTUAL SCHEDULE -**

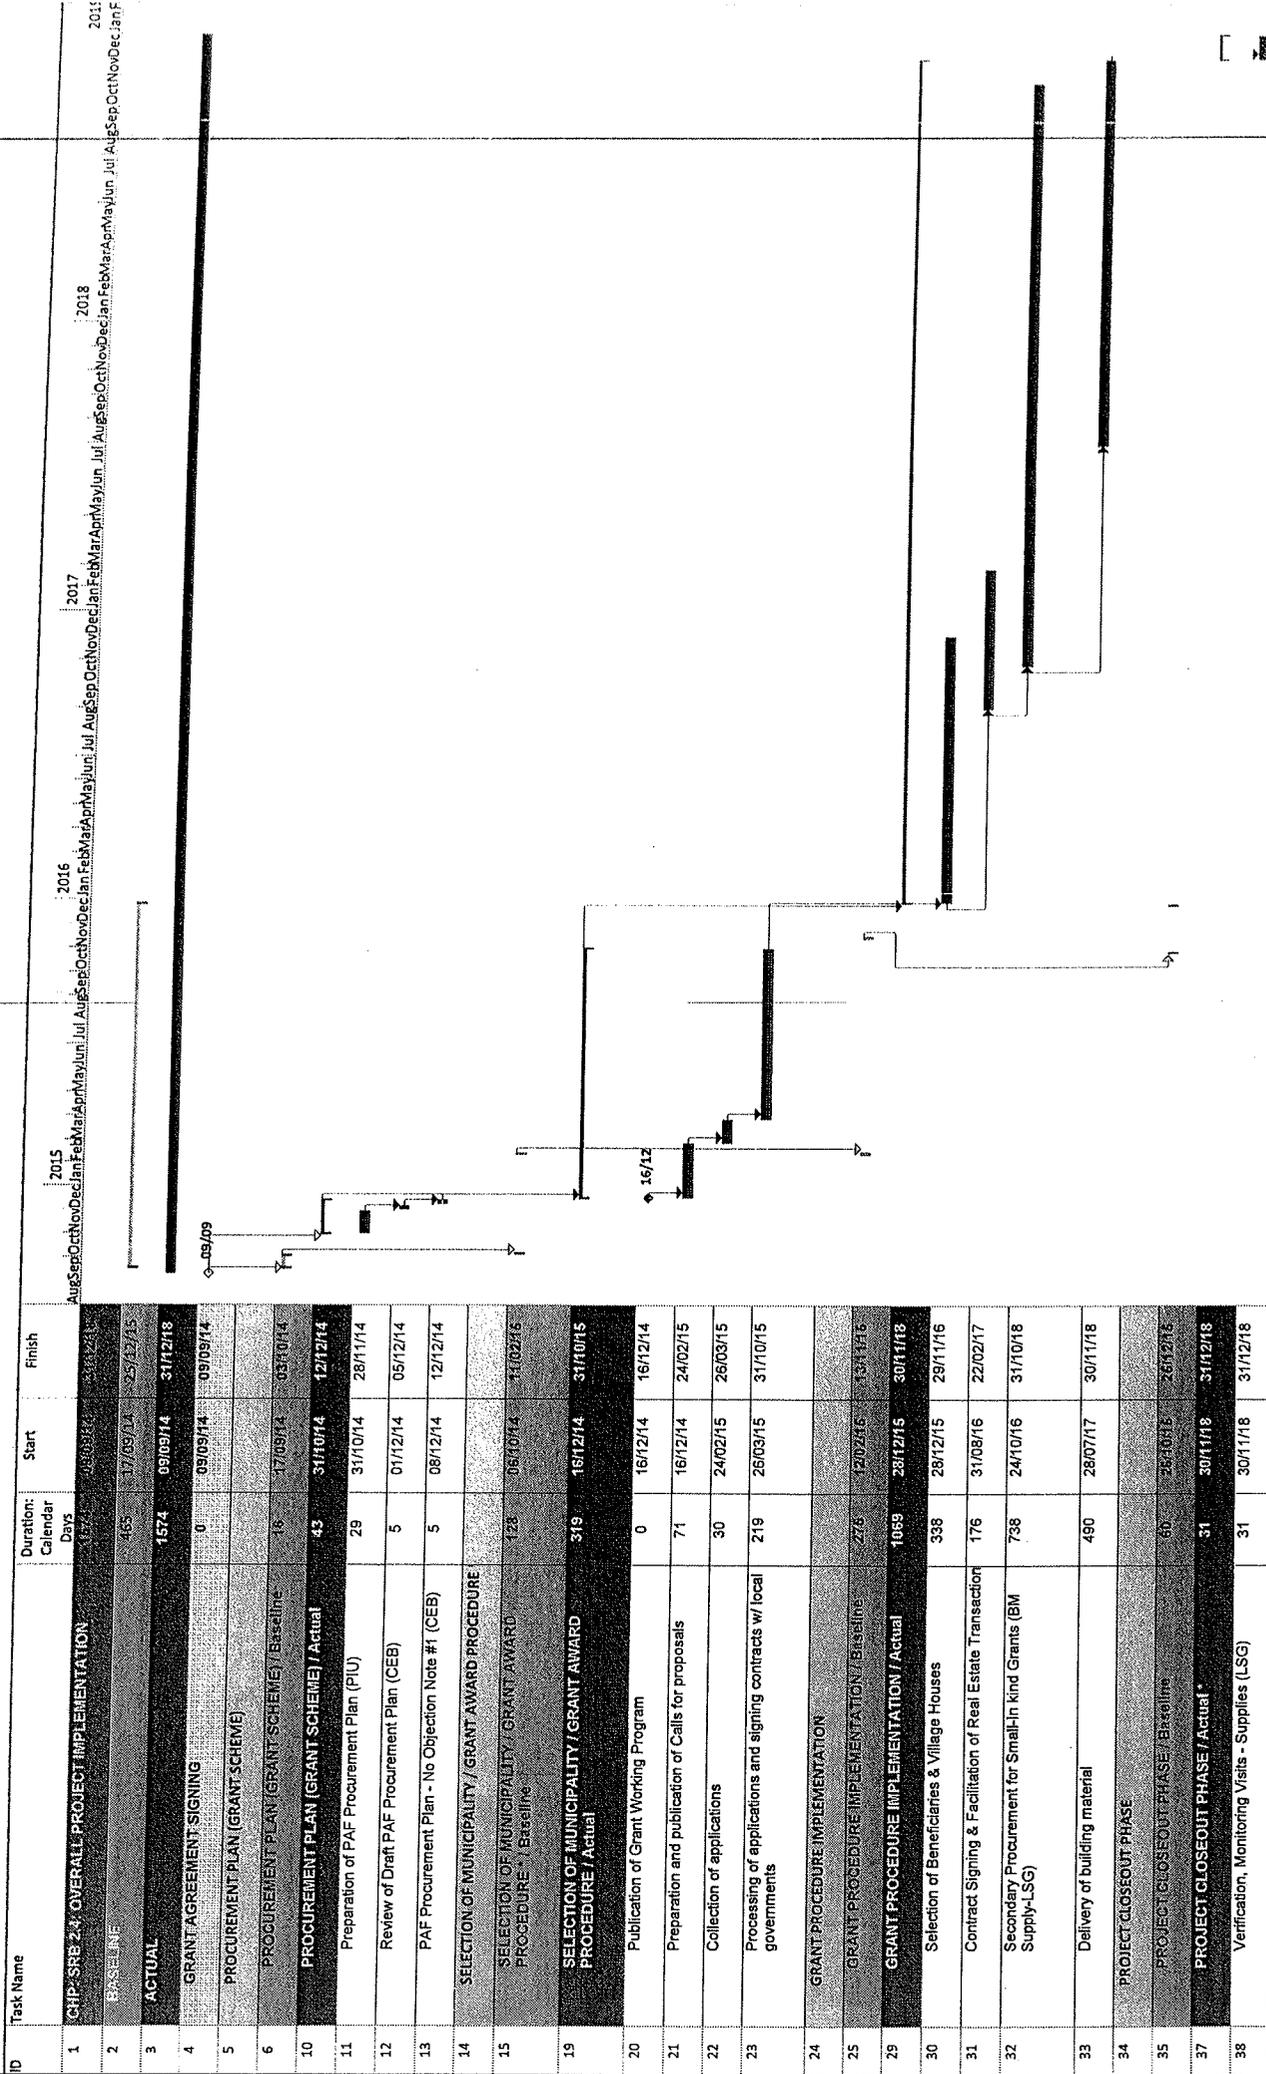


ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 2.4 - OVERALL PROJECT IMPLEMENTATION	165	17/09/14	25/02/15
2	BASELINE			
3	ACTUAL	1574	09/09/14	31/12/18
4	GRANT AGREEMENT SIGNING	0	09/09/14	09/09/14
5	PROCUREMENT PLAN (GRANT SCHEME)			
6	PROCUREMENT PLAN (GRANT SCHEME) / Baseline	16	17/09/14	03/10/14
10	PROCUREMENT PLAN (GRANT SCHEME) / Actual	43	31/10/14	12/12/14
11	Preparation of PAF Procurement Plan (PU)	29	31/10/14	28/11/14
12	Review of Draft PAF Procurement Plan (CEB)	5	01/12/14	05/12/14
13	PAF Procurement Plan - No Objection Note #1 (CEB)	5	08/12/14	12/12/14
14	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE			
15	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE - / Baseline	123	06/10/14	11/02/15
19	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE / Actual	319	16/12/14	31/10/15
20	Publication of Grant Working Program	0	16/12/14	16/12/14
21	Preparation and publication of Calls for proposals	71	16/12/14	24/02/15
22	Collection of applications	30	24/02/15	26/03/15
23	Processing of applications and signing contracts w/ local governments	219	26/03/15	31/10/15
24	GRANT PROCEDURE IMPLEMENTATION			
25	GRANT PROCEDURE IMPLEMENTATION / Baseline	276	17/02/15	13/11/15
29	GRANT PROCEDURE IMPLEMENTATION / Actual	1069	28/12/15	30/11/18
30	Selection of Beneficiaries & Village Houses	338	28/12/15	29/11/16
31	Contract Signing & Facilitation of Real Estate Transaction	176	31/08/16	22/02/17
32	Secondary Procurement for Small-In kind Grants (BM Supply-LSG)	738	24/10/16	31/10/18
33	Delivery of building material	490	28/07/17	30/11/18
34	PROJECT CLOSURE PHASE			
35	PROJECT CLOSURE PHASE / Baseline	60	28/08/15	26/12/15
37	PROJECT CLOSURE PHASE / Actual *	31	30/11/18	31/12/18
38	Verification, Monitoring Visits - Supplies (LSG)	31	30/11/18	31/12/18

Project: SRB 2.4  
250 Village Houses (20 Grant Contracts)  
Date: 14/9/2018

(\* Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframes within the same sub-project.

**RHP: CHP SERBIA - SRB 3.1 - CONSTRUCTION OF 235 APARTMENTS  
- BASELINE AND ACTUAL SCHEDULE -**

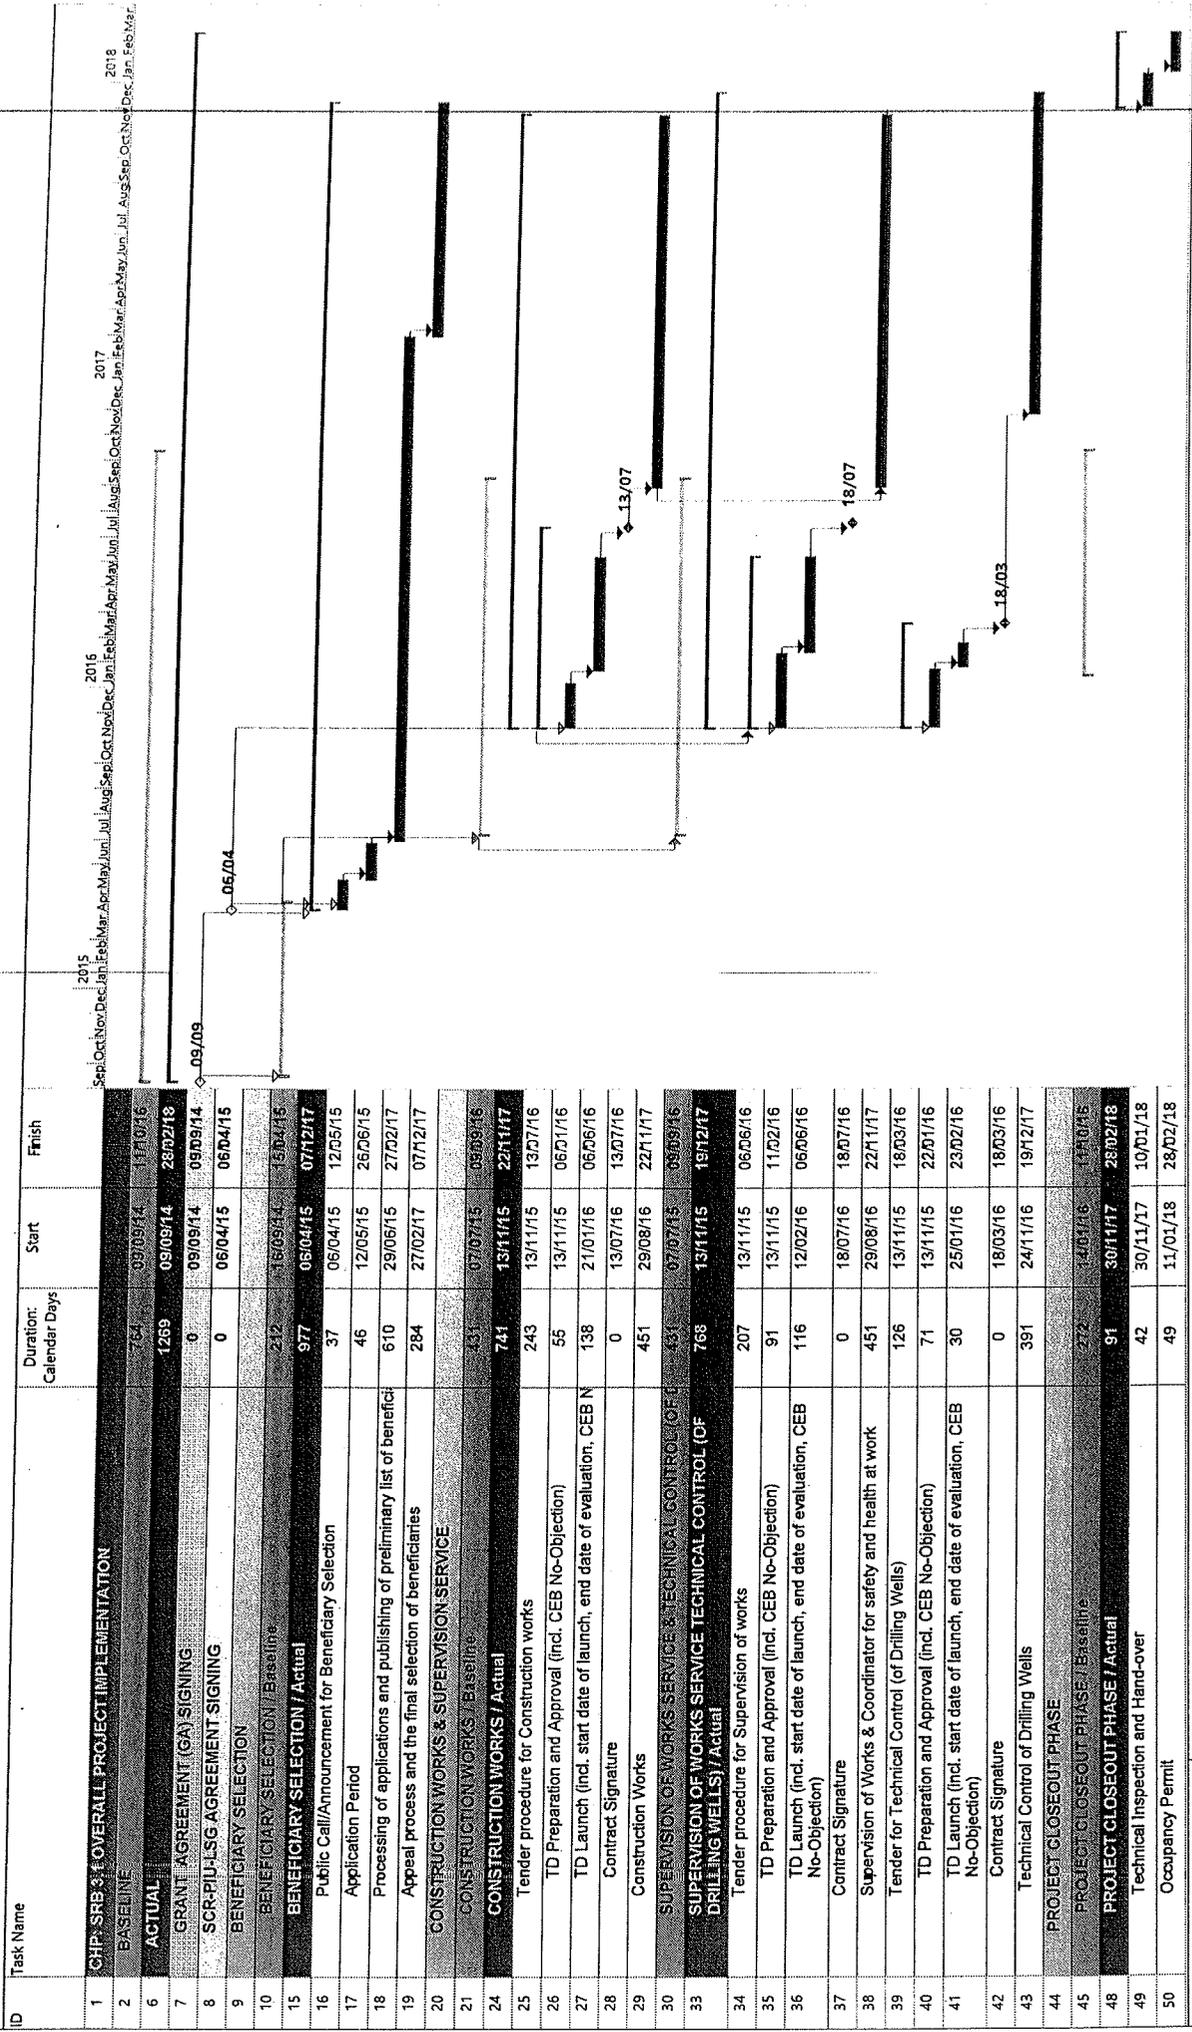


ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 3.1 OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	754	09/09/14	11/07/16
6	ACTUAL	1269	09/09/14	28/02/18
7	GRANT AGREEMENT (GAY) SIGNING	0	09/09/14	09/09/14
8	SCRIPULUSG AGREEMENT SIGNING	0	06/04/15	06/04/15
9	BENEFICIARY SELECTION			
10	BENEFICIARY SELECTION / Baseline	212	18/09/14	15/04/15
15	BENEFICIARY SELECTION / Actual	977	06/04/15	07/12/17
16	Public Call/Announcement for Beneficiary Selection			
17	Application Period	37	06/04/15	12/05/15
18	Processing of applications and publishing of preliminary list of beneficiaries	46	12/05/15	26/06/15
19	Appeal process and the final selection of beneficiaries	610	29/06/15	27/02/17
20	CONSTRUCTION WORKS & SUPERVISION SERVICE			
21	CONSTRUCTION WORKS / Baseline	231	07/07/15	09/09/16
24	CONSTRUCTION WORKS / Actual	741	13/11/15	22/11/17
25	Tender procedure for Construction works	243	13/11/15	13/07/16
26	TD Preparation and Approval (incl. CEB No-Objection)	55	13/11/15	06/01/16
27	TD Launch (incl. start date of launch, end date of evaluation, CEB N	138	21/07/16	06/06/16
28	Contract Signature	0	13/07/16	13/07/16
29	Construction Works	451	29/08/16	22/11/17
30	SUPERVISION OF WORKS SERVICE & TECHNICAL CONTROL OF	631	07/07/15	05/09/16
33	SUPERVISION OF WORKS SERVICE TECHNICAL CONTROL (OF DRILLING WELLS) / Actual	768	13/11/15	19/12/17
34	Tender procedure for Supervision of works	207	13/11/15	06/06/16
35	TD Preparation and Approval (incl. CEB No-Objection)	91	13/11/15	11/02/16
36	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	116	12/02/16	06/06/16
37	Contract Signature	0	18/07/16	18/07/16
38	Supervision of Works & Coordinator for safety and health at work	451	29/08/16	22/11/17
39	Tender for Technical Control (of Drilling Wells)	126	13/11/15	18/03/16
40	TD Preparation and Approval (incl. CEB No-Objection)	71	13/11/15	22/01/16
41	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	30	25/01/16	23/02/16
42	Contract Signature	0	18/03/16	18/03/16
43	Technical Control of Drilling Wells	391	24/11/16	19/12/17
44	PROJECT CLOSEOUT PHASE			
45	PROJECT CLOSEOUT PHASE / Baseline	272	2/05/16	1/06/16
48	PROJECT CLOSEOUT PHASE / Actual	91	30/11/17	28/02/18
49	Technical Inspection and Hand-over	42	30/11/17	10/01/18
50	Occupancy Permit	49	11/01/18	28/02/18

Project SRB 3.1  
Construction of Multi Apt. B. (235 A)  
Date: 12/9/2018

(C) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

RHP: CHP SERBIA - SRB 3.2 - PROVISION OF 49 PRE-FAB HOUSES IN BELGRADE  
- BASELINE AND ACTUAL SCHEDULE -

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 3.2 OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	109	03/02/18	17/03/18
3	ACTUAL	1666	08/09/14	01/04/19
4	GRANT AGREEMENT (GRANTING)	0	09/09/14	09/09/14
5	BENEFICIARY SELECTION			
6	BENEFICIARY SELECTION / Baseline	255	15/09/14	18/05/15
10	BENEFICIARY SELECTION / Actual	470	05/04/15	18/07/15
11	Public Call/Announcement for Beneficiary Selection & Application Period	82	06/04/15	26/06/15
12	Processing of applications and publishing of preliminary list of beneficiaries	298	29/08/15	21/04/16
13	Appeal process and the final selection of beneficiaries	88	21/04/16	18/07/16
14	DESIGN/BUILD & TECH. SUPERVISION			
15	DESIGN/BUILD & TECH. SUPERVISION / Baseline	564	04/07/17	01/04/18
18	DESIGN/BUILD & TECH. SUPERVISION / Actual	1110	18/03/16	01/04/19
19	Tender Procedure for Design-Build	326	18/03/16	07/02/17
20	TD Preparation and Approval (incl. CEB No-Objection)	225	18/03/16	28/10/16
21	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	72	02/11/16	12/01/17
22	Contract Signature	0	07/02/17	07/02/17
23	Design-Build	755	08/03/17	01/04/19
24	Tender for supervision services	321	18/03/16	02/02/17
25	TD Preparation and Approval (incl. CEB No-Objection)	224	18/03/16	27/10/16
26	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	71	31/10/16	08/01/17
27	Contract Signature	0	02/02/17	02/02/17
28	Technical supervision for Design-Build, Coordinator for safety and health at work	763	28/02/17	01/04/19
29	Tender for services EMC elaborate	36	06/09/18	11/10/18
30	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	26	06/09/18	01/10/18
31	Contract Signature	1	11/10/18	11/10/18
32	EMC elaborate (stud)	20	12/10/18	31/10/18
33	PROJECT CLOSEOUT			
34	PROJECT CLOSEOUT / Baseline	166	18/03/18	17/03/18
39	PROJECT CLOSEOUT / Actual	330	07/05/18	01/04/19
40	Tender for Technical Inspection	52	07/05/18	27/06/18
41	TD Preparation and Approval (incl. CEB No-Objection)	8	07/05/18	14/05/18
42	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	31	18/05/18	15/08/18
43	Contract Signature	0	27/06/18	27/06/18
44	Technical Acceptance and Hand Over (incl. Tech. Inspection)	264	12/07/18	01/04/19



Project: SRB 3.2  
Construction of 49 Pre-Fab H. in Bg  
Date: 12/9/2018

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

RHP: CHP SERBIA - SRB 3.3 - PROVISION OF 302 PACKAGES OF BUILDING MATERIAL  
- BASELINE AND ACTUAL SCHEDULE -

ID	Task Name	Duration: Calendar Days	Start	Finish	Preferences Working Days	Duration: Working Days
1	CHP: SRB 3.3 OVERALL PROJECT IMPLEMENTATION	577	05/09/15	07/06/16		433 days
2	BASELINE	577	05/09/15	07/06/16		433 days
3	ACTUAL	1313	03/09/14	10/12/19		1377 days
4	GRANT AGREEMENT (G.A) SIGNING	0	05/09/14	05/09/14		0 days
5	SIGNING OF THE AGREEMENT (SCR, PIU, CITY OF BELGRADE)	0	06/04/15	06/04/15		0 days
6	BENEFICIARY SELECTION	65	05/09/14	27/03/15		119 days
7	BENEFICIARY SELECTION (B) (Actual)	709	05/04/15	14/03/17		512 days
11	Public Call for Beneficiary Selection & Application Period	82	06/04/15	26/06/15	5	61 days
12	Processing of applications and publishing preliminary list of beneficiaries	614	29/06/15	03/03/17	11	444 days
13	Appeal process and the final selection of beneficiaries	12	03/03/17	14/03/17	12FS-23	8 days
14	MATERIAL DELIVERY & INSTALLATIONS SUPERVISION					
15	MATERIAL DELIVERY & INSTALLATIONS SUPERVISION (B) (Actual)	140	16/09/14	01/03/16	7AS	318 days
18	MATERIAL DELIVERY & INSTALLATIONS SUPERVISION (Actual)	1478	05/06/15	24/06/19		1060 days
19	Tender Procedure for Supervision Services	134	08/06/15	20/10/15		96 days
20	TD Preparation and Approval (incl. CEB No-Objection)	32	08/06/15	09/07/15	5	24 days
21	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	71	10/07/15	18/09/15	20	51 days
22	Contract Signature	0	20/10/15	20/10/15	21	0 days
23	Supervision of Material Delivery and Installation (161 + 141)	144	01/02/19	24/06/19	33FF,22	102 days
24	Tender Procedure for Building Material Supply (161)	95	02/10/18	04/01/19		69 days
25	TD Preparation and Approval (incl. CEB No-Objection)	9	02/10/18	10/10/18		7 days
26	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	56	16/10/18	10/12/18	25	40 days
27	Contract Signature	1	04/01/19	04/01/19	26	1 day
28	Delivery and installation of building material (161)	137	01/02/19	17/06/19	27FS+13	97 days
29	Tender Procedure for Building Material Supply (141)	102	02/10/18	11/01/19		74 days
30	TD Preparation and Approval (incl. CEB No-Objection)	9	02/10/18	10/10/18		7 days
31	TD Launch (incl. start date of launch, end date of evaluation, CE)	56	23/10/18	17/12/18	30	40 days
32	Contract Signature	1	11/01/19	11/01/19	31	1 day
33	Delivery and installation of building material (141)	137	08/02/19	24/06/19	32FS+19	97 days
34	PROJECT CLOSURE					
35	PROJECT CLOSURE (B) (Actual)	30	01/03/15	07/03/15	13	22 days
37	PROJECT CLOSURE (Actual)	439	25/07/19	10/12/19		99 days
38	Verification of Material Installation (161 + 141)	62	25/07/19	24/08/19	23,33,28	44 days
39	Final Progress Report and Expenditure Verification Report	45	25/08/19	03/10/19	38	33 days
40	Final Acceptance by CEB (SRES)	30	11/11/19	10/12/19	39	22 days

Actual Task Timeline

Estimated Project Activities Summary


Actual Project Activities Summary

Group of Activities


Project: SRB 3.3  
Provision of 302 BM  
Date: 19/10/2018

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

2015 2016 2017 2018 2019 2020

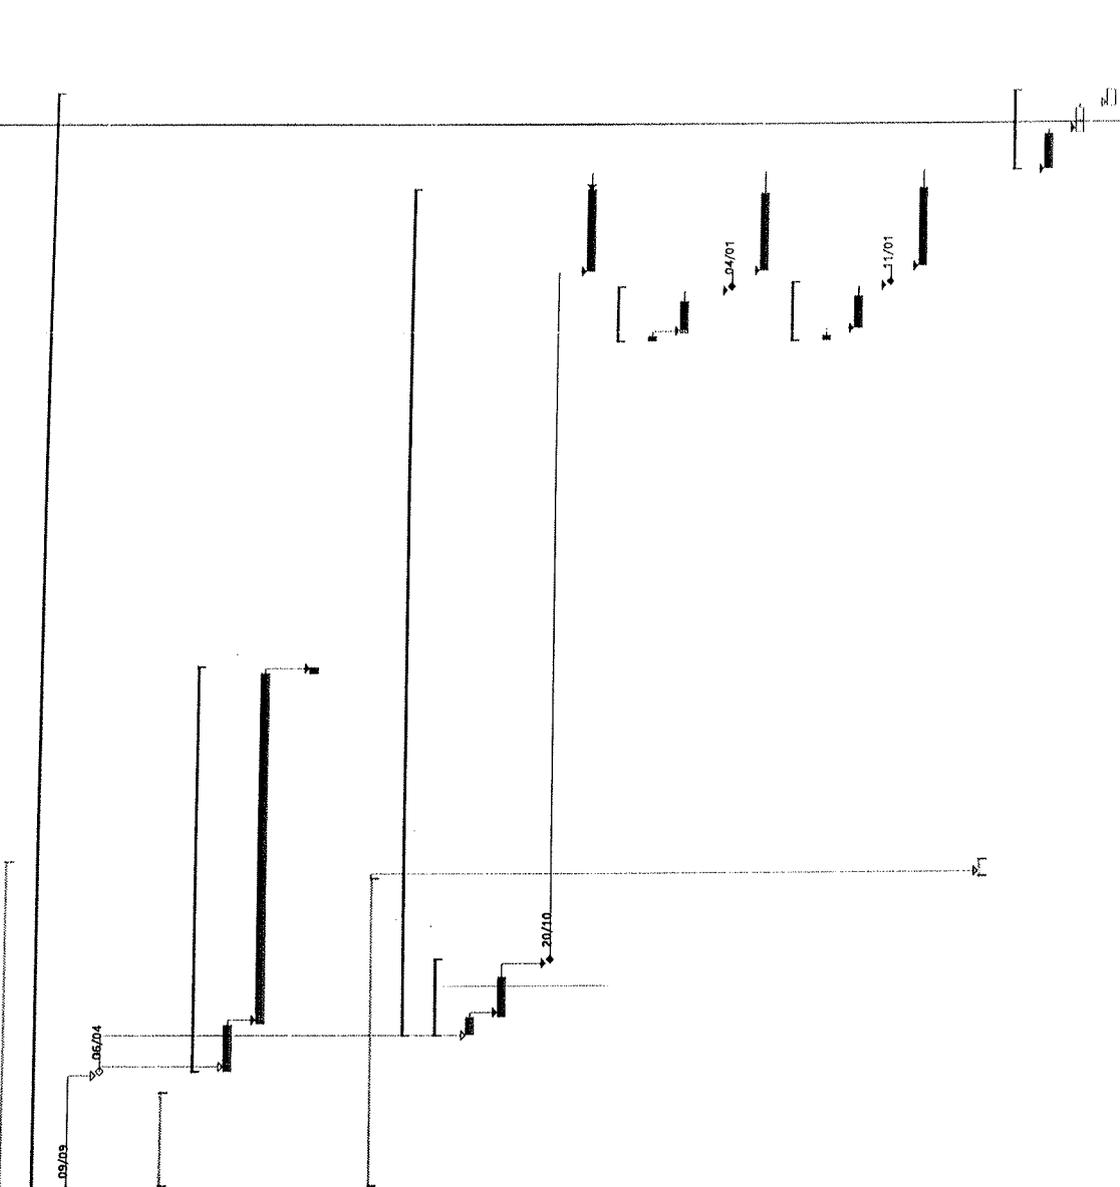

**RHP: CHP SERBIA - SRB 3.4 -PURCHASING OF 68 VILLAGE HOUSES  
- BASELINE & ACTUAL SCHEDULE -**

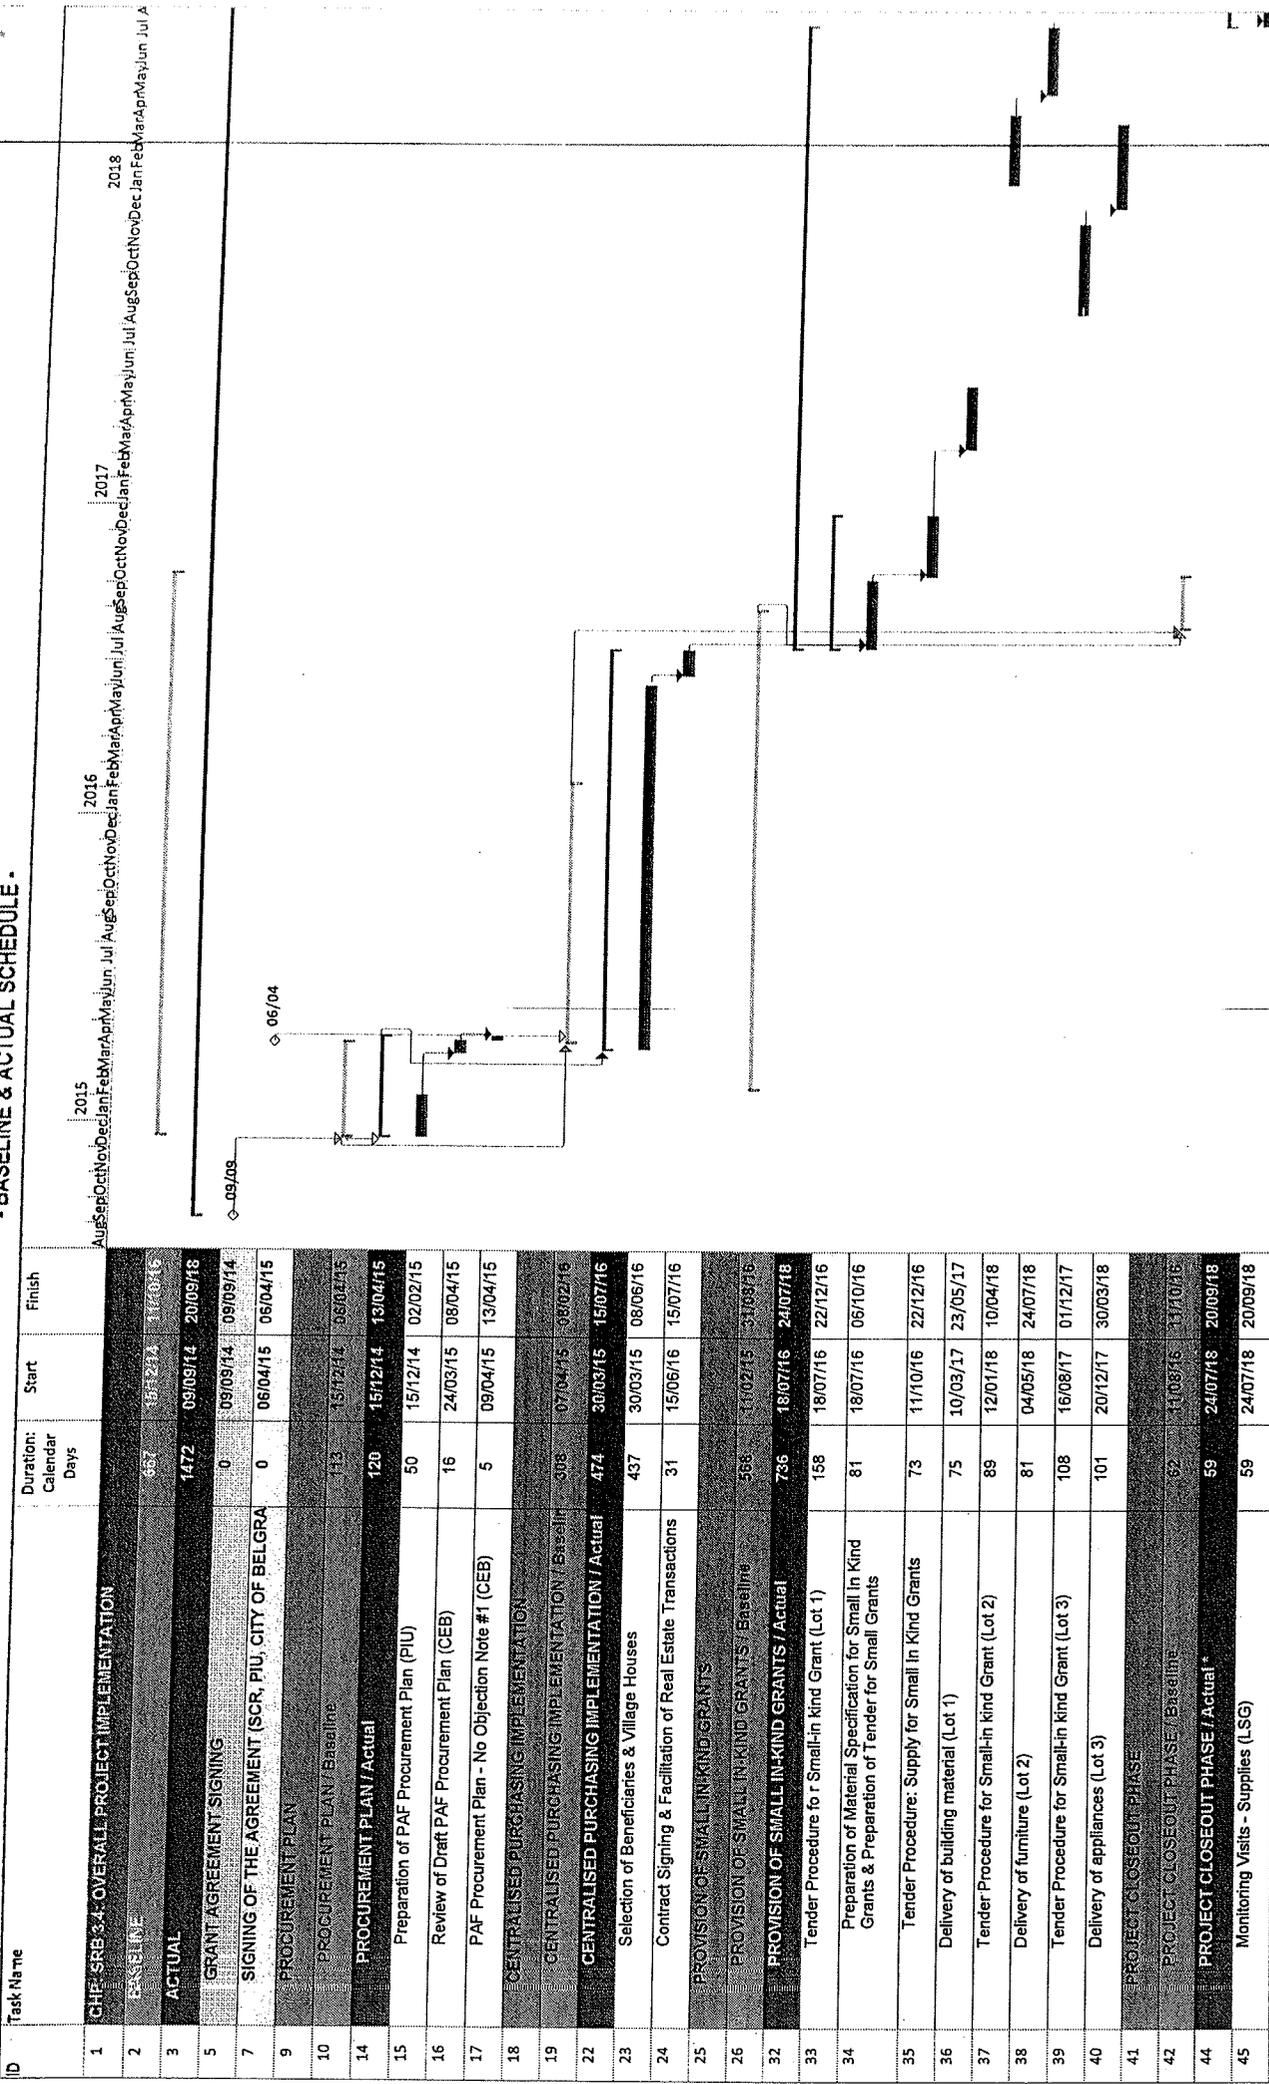

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 3.4- OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	657	15/12/14	11/03/16
3	ACTUAL	1472	09/09/14	20/09/18
5	GRANT AGREEMENT SIGNING	0	09/09/14	09/09/14
7	SIGNING OF THE AGREEMENT (SCR, PIU, CITY OF BELGRA	0	06/04/15	06/04/15
9	PROCUREMENT PLAN			
10	PROCUREMENT PLAN / Baseline	113	15/12/14	06/04/15
14	PROCUREMENT PLAN / Actual	120	15/12/14	13/04/15
15	Preparation of PAF Procurement Plan (PIU)	50	15/12/14	02/02/15
16	Review of Draft PAF Procurement Plan (CEB)	16	24/03/15	08/04/15
17	PAF Procurement Plan - No Objection Note #1 (CEB)	5	09/04/15	13/04/15
18	CENTRALISED PURCHASING IMPLEMENTATION			
19	CENTRALISED PURCHASING IMPLEMENTATION / Baseline	308	07/04/15	08/02/16
22	CENTRALISED PURCHASING IMPLEMENTATION / Actual	474	30/03/15	15/07/16
23	Selection of Beneficiaries & Village Houses	437	30/03/15	08/06/16
24	Contract Signing & Facilitation of Real Estate Transactions	31	15/06/16	15/07/16
25	PROVISION OF SMALL IN-KIND GRANTS			
26	PROVISION OF SMALL IN-KIND GRANTS / Baseline	588	11/02/15	31/03/16
32	PROVISION OF SMALL IN-KIND GRANTS / Actual	736	18/07/16	24/07/18
33	Tender Procedure for Small-in-kind Grant (Lot 1)	158	18/07/16	22/12/16
34	Preparation of Material Specification for Small In Kind Grants & Preparation of Tender for Small Grants	81	18/07/16	06/10/16
35	Tender Procedure: Supply for Small In Kind Grants	73	11/10/16	22/12/16
36	Delivery of building material (Lot 1)	75	10/03/17	23/05/17
37	Tender Procedure for Small-in-kind Grant (Lot 2)	89	12/01/18	10/04/18
38	Delivery of furniture (Lot 2)	81	04/05/18	24/07/18
39	Tender Procedure for Small-in-kind Grant (Lot 3)	108	16/08/17	01/12/17
40	Delivery of appliances (Lot 3)	101	20/12/17	30/03/18
41	PROJECT CLOSEOUT PHASE			
42	PROJECT CLOSEOUT PHASE / Baseline	67	11/03/16	11/10/16
44	PROJECT CLOSEOUT PHASE / Actual *	59	24/07/18	20/09/18
45	Monitoring Visits - Supplies (LSG)	59	24/07/18	20/09/18


Project: SRB 3.4  
Purchase of 63 Village Houses  
Date: 12/9/2018

Actual Task Timeframe  
Grant Agreement Signing  
Estimated Project Activities Summary  
Actual Project Activities Summary

Group of Activities  
Progress

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA - SRB 3.4.1 - PROVISION OF 145 VILLAGE HOUSES (Indicative allocation: 100 centralised + 45 decentralised) - BASELINE AND ACTUAL SCHEDULE.**

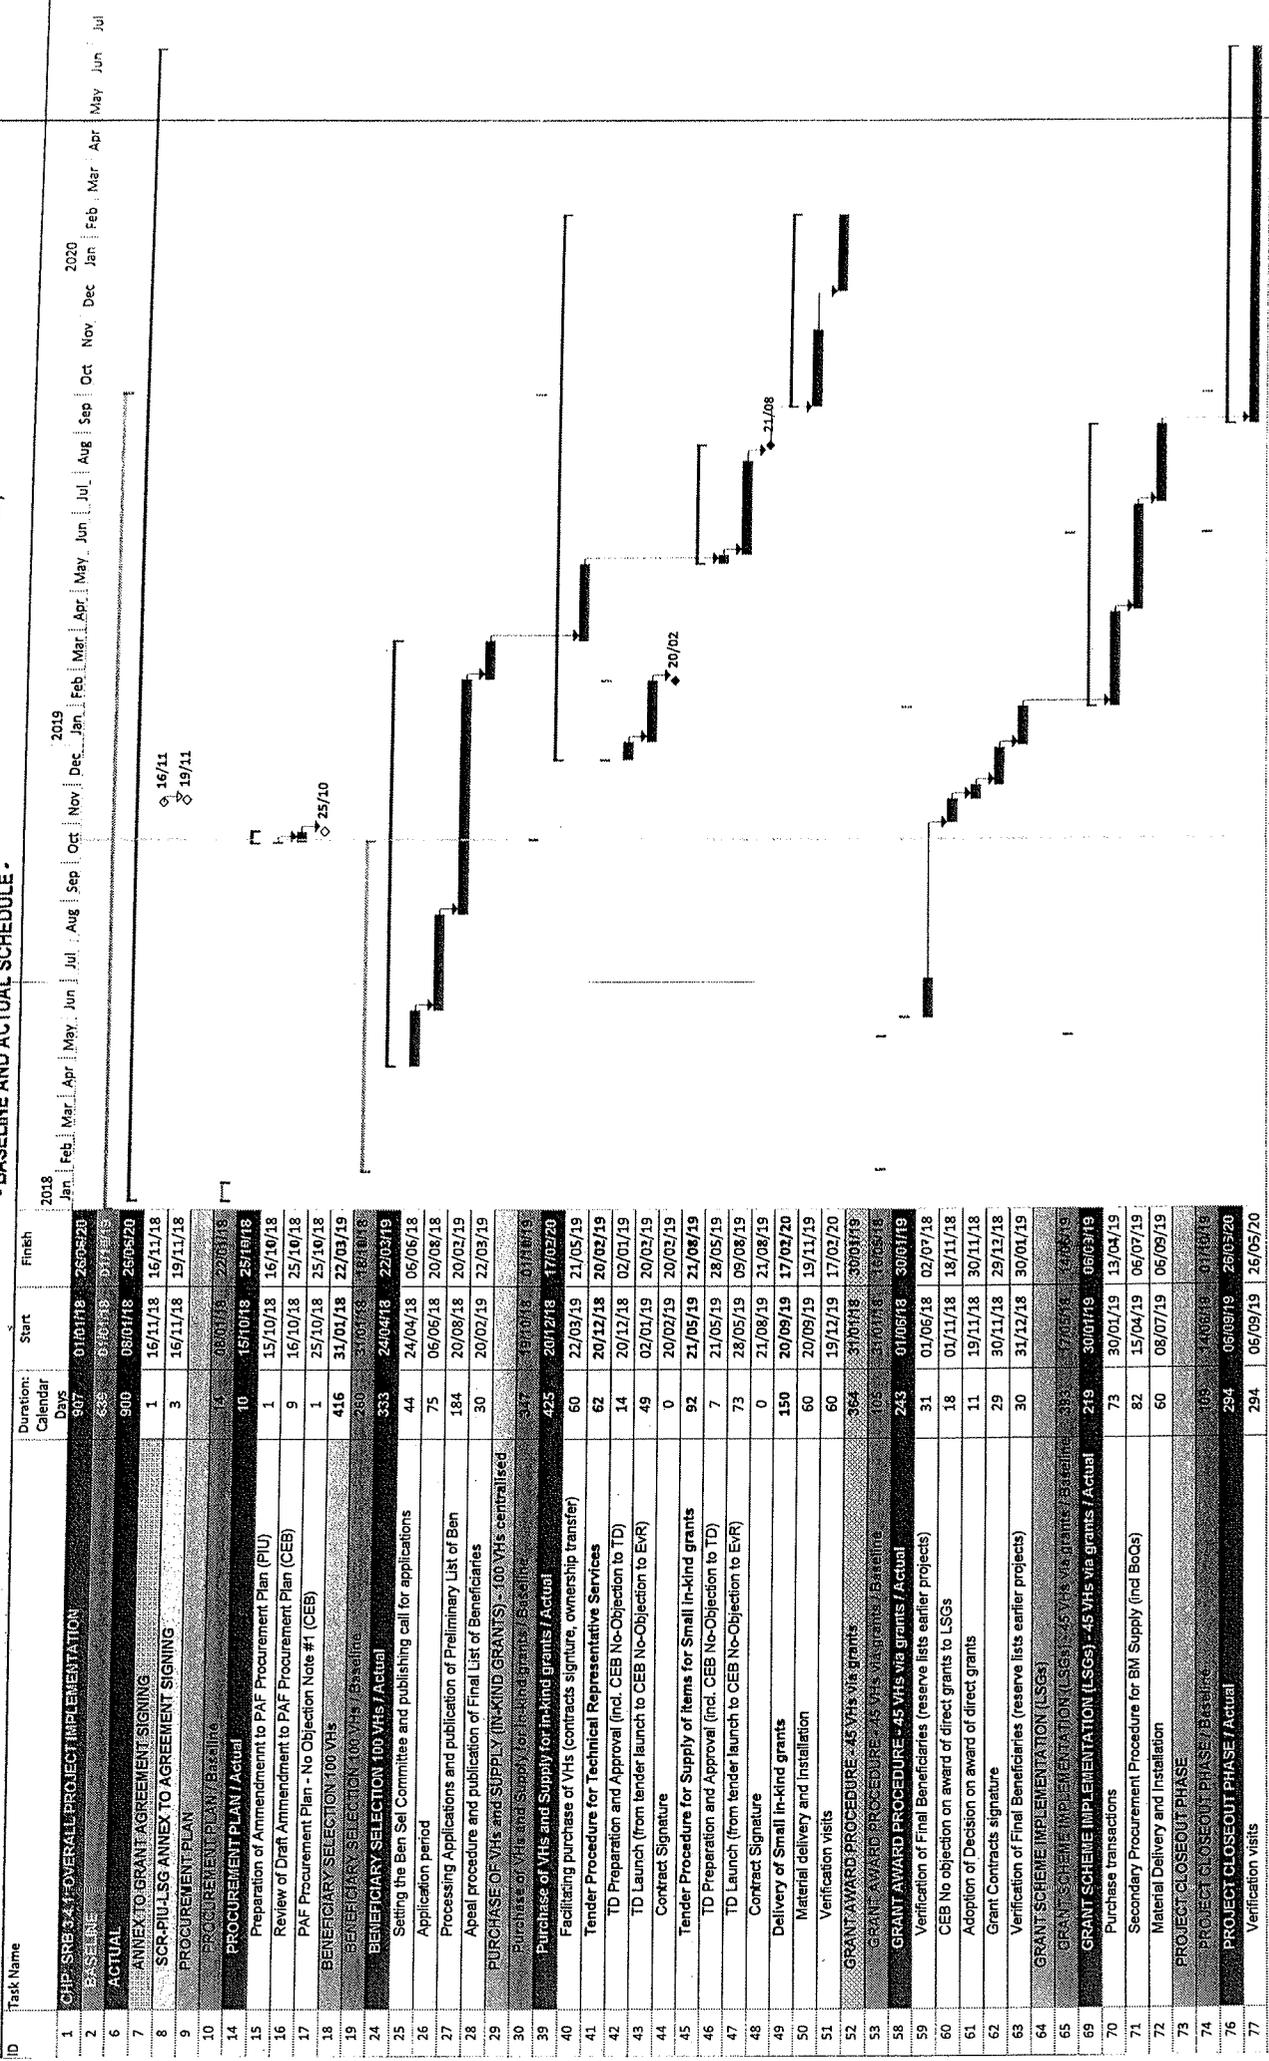

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 3.4.1 FEDERAL PROJECT IMPLEMENTATION	907	01/01/18	26/09/20
2	BASELINE	439	04/01/18	01/01/19
6	ACTUAL	900	05/01/18	26/09/20
7	ANNEX TO GRANT AGREEMENT SIGNING	1	16/11/18	16/11/18
8	SCR-PLUG ANNEX TO AGREEMENT SIGNING	3	16/11/18	19/11/18
9	PROCUREMENT PLAN	14	08/01/18	20/01/18
10	PROCUREMENT PLAN / Actual	10	15/10/18	25/10/18
14	Preparation of Amendment to PAF Procurement Plan (PIU)	1	15/10/18	16/10/18
15	Review of Draft Amendment to PAF Procurement Plan (CEB)	9	16/10/18	25/10/18
16	PAF Procurement Plan - No Objection Note #1 (CEB)	1	25/10/18	25/10/18
17	BENEFICIARY SELECTION 100 VHs	416	31/01/18	22/03/19
18	BENEFICIARY SELECTION 100 VHs / Baseline	380	31/01/18	18/01/19
19	BENEFICIARY SELECTION 100 VHs / Actual	333	24/04/18	22/03/19
20	Setting the Ben Sel Committee and publishing call for applications	44	24/04/18	06/06/18
21	Application period	75	06/06/18	20/08/18
22	Processing Applications and publication of Preliminary List of Ben	184	20/08/18	20/02/19
23	Appeal procedure and publication of Final List of Beneficiaries	30	20/02/19	22/03/19
24	PURCHASE OF VHs and SUPPLY (IN-KIND GRANTS) - 100 VHs centralised	377	19/01/18	01/01/19
25	Purchase of VHs and Supply for in-kind grants / Baseline	425	20/12/18	17/02/20
26	Purchase of VHs and Supply for in-kind grants / Actual	60	22/03/19	21/05/19
27	Facilitating purchase of VHs (contracts signature, ownership transfer)	62	20/12/18	20/02/19
28	Tender Procedure for Technical Representative Services	14	20/12/18	02/01/19
29	TD Preparation and Approval (incl. CEB No-Objection to TD)	49	02/01/19	20/02/19
30	TD Launch (from tender launch to CEB No-Objection to EvR)	0	20/02/19	20/02/19
31	Contract Signature	92	21/05/19	21/08/19
32	Tender Procedure for Supply of items for Small in-kind grants	7	21/05/19	28/05/19
33	TD Preparation and Approval (incl. CEB No-Objection to TD)	73	28/05/19	09/08/19
34	TD Launch (from tender launch to CEB No-Objection to EvR)	0	21/08/19	21/08/19
35	Contract Signature	150	20/09/19	17/02/20
36	Delivery of Small in-kind grants	60	19/12/19	17/02/20
37	Material delivery and installation	60	20/09/19	19/11/19
38	Verification visits	60	19/12/19	17/02/20
39	GRANT AWARDS PROCEDURE - 45 VHs via grants	364	31/01/18	30/01/19
40	GRANT AWARDS PROCEDURE - 45 VHs via grants / Baseline	105	31/01/18	16/09/18
41	GRANT AWARDS PROCEDURE - 45 VHs via grants / Actual	243	01/05/18	30/01/19
42	Verification of Final Beneficiaries (reserve lists earlier projects)	31	01/05/18	02/07/18
43	CEB No objection on award of direct grants to LSGs	18	01/11/18	18/11/18
44	Adoption of Decision on award of direct grants	11	19/11/18	30/11/18
45	Grant Contracts signature	29	30/11/18	29/12/18
46	Verification of Final Beneficiaries (reserve lists earlier projects)	30	31/12/18	30/01/19
47	GRANT SCHEME IMPLEMENTATION (LSGs)	376	01/01/19	06/03/19
48	GRANT SCHEME IMPLEMENTATION (LSGs) - 45 VHs via grants / Baseline	219	30/01/19	06/03/19
49	GRANT SCHEME IMPLEMENTATION (LSGs) - 45 VHs via grants / Actual	73	30/01/19	13/04/19
50	Purchase transactions	82	15/04/19	06/07/19
51	Secondary Procurement Procedure for BM Supply (incl BCoQs)	60	08/07/19	06/09/19
52	Material Delivery and Installation	109	08/07/19	01/09/19
53	PROJECT CLOSOUT PHASE	294	06/09/19	26/03/20
54	PROJECT CLOSOUT PHASE / Baseline	294	06/09/19	26/03/20
55	Verification visits	294	06/09/19	26/03/20


Project: SRB 3.4.1  
 Provision of 145 VHs  
 Date: 19/10/2018

Actual Task Timeframe  
 Grant-Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Group of Activities  
 Progress

RHP: CHP SERBIA - SR3 4.1 - CONSTRUCTION OF 261 APARTMENTS  
 . BASELINE AND ACTUAL SCHEDULE .

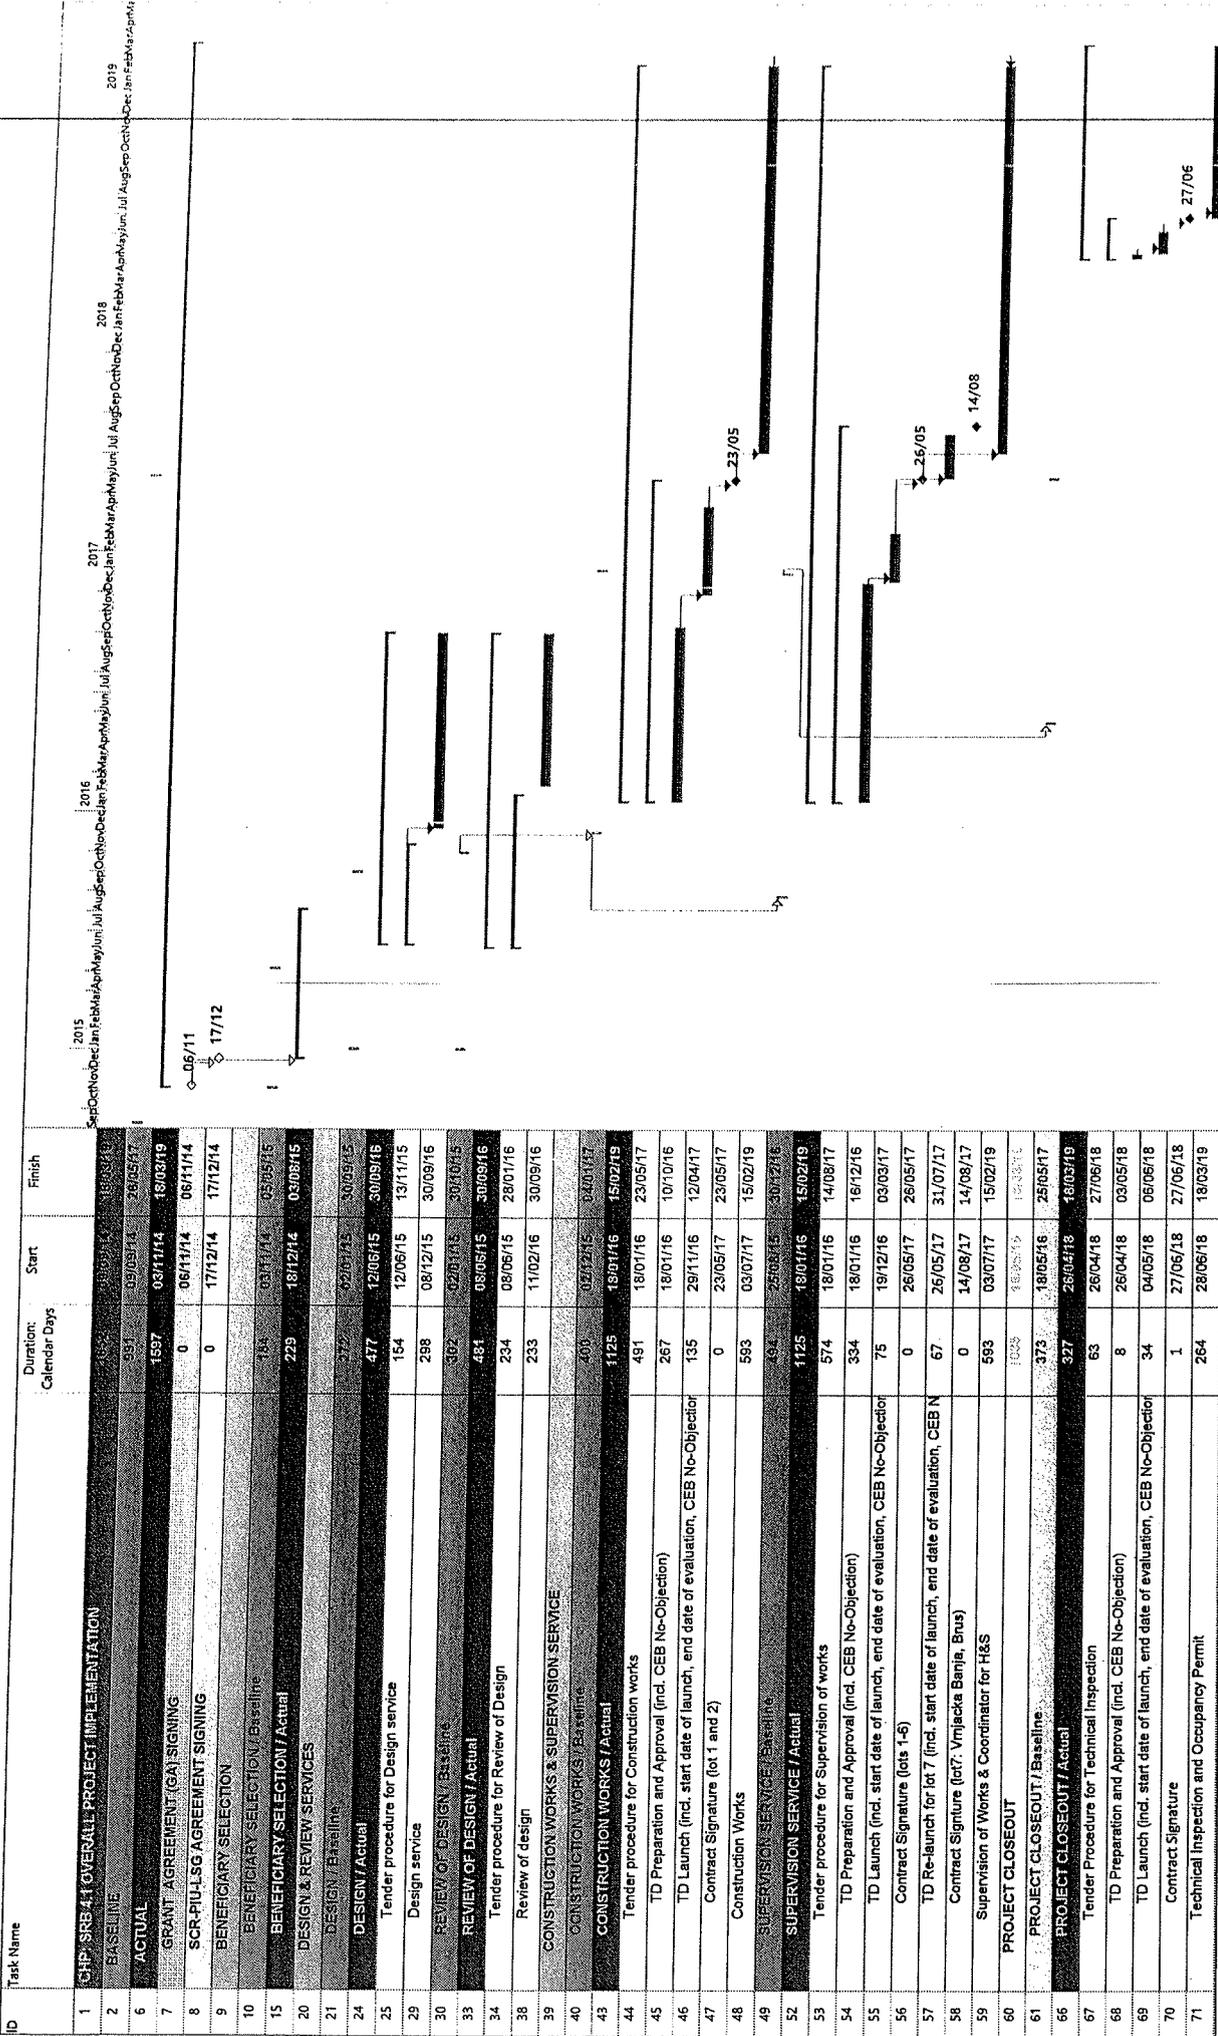

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP SRB 4.1 OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	391	09/09/14	24/05/17
6	ACTUAL	1597	03/11/14	18/03/19
7	GRANT AGREEMENT / SIGNING	0	06/11/14	06/11/14
8	SCR-PIU-LSG AGREEMENT SIGNING	0	17/12/14	17/12/14
9	BENEFICIARY SELECTION			
10	BENEFICIARY SELECTION / Baseline	14	03/11/14	05/05/15
15	BENEFICIARY SELECTION / Actual	229	18/12/14	03/08/15
20	DESIGN & REVIEW SERVICES			
21	DESIGN / Baseline	379	09/09/15	30/09/15
24	DESIGN / Actual	477	12/06/15	30/09/16
25	Tender procedure for Design service	154	12/06/15	13/11/15
29	Design service	298	08/12/15	30/09/16
30	REVIEW OF DESIGN / Baseline	102	02/01/16	30/01/16
33	REVIEW OF DESIGN / Actual	481	08/05/15	30/08/16
34	Tender procedure for Review of Design	234	09/06/15	28/01/16
38	Review of design	233	11/02/16	30/09/16
39	CONSTRUCTION WORKS & SUPERVISION SERVICE			
40	CONSTRUCTION WORKS / Baseline	400	02/02/15	04/01/17
43	CONSTRUCTION WORKS / Actual	1125	18/01/16	15/02/19
44	Tender procedure for Construction works	491	18/01/16	23/05/17
45	TD Preparation and Approval (incl. CEB No-Objection)	267	18/01/16	10/10/16
46	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	135	29/11/16	12/04/17
47	Contract Signature (lot 1 and 2)	0	23/05/17	23/05/17
48	Construction Works	593	03/07/17	15/02/19
49	SUPERVISION SERVICE / Baseline	67	25/02/16	30/12/16
52	SUPERVISION SERVICE / Actual	1125	18/01/16	15/02/19
53	Tender procedure for Supervision of works	574	18/01/16	14/08/17
54	TD Preparation and Approval (incl. CEB No-Objection)	334	18/01/16	16/12/16
55	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	75	18/12/16	03/03/17
56	Contract Signature (lots 1-6)	0	26/05/17	26/05/17
57	TD Re-launch for lot 7 (incl. start date of launch, end date of evaluation, CEB N	67	26/05/17	31/07/17
58	Contract Signature (lot 7: Vrnjacks Banja, Brus)	0	14/08/17	14/08/17
59	Supervision of Works & Coordinator for H&S	593	03/07/17	15/02/19
60	PROJECT CLOSEOUT	1003	18/05/16	12/03/18
61	PROJECT CLOSEOUT / Baseline	373	18/05/16	25/05/17
66	PROJECT CLOSEOUT / Actual	327	26/04/18	18/03/19
67	Tender Procedure for Technical Inspection	63	26/04/18	27/06/18
68	TD Preparation and Approval (incl. CEB No-Objection)	8	26/04/18	03/05/18
69	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	34	04/05/18	06/06/18
70	Contract Signature	1	27/06/18	27/06/18
71	Technical Inspection and Occupancy Permit	264	28/06/18	18/03/19

Project: SRB 4.1  
 Construction of Multi Apts. B. (2)  
 Date: 14/09/2018


Actual Task Timeline  
 Grant Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Progress  
 Group of Activities

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframes within the same Sub-project.

RHP: CHP SERBIA - SRB 4.2 - CONSTRUCTION OF 30 PRE-FAB HOUSES  
- BASELINE AND ACTUAL SCHEDULE -

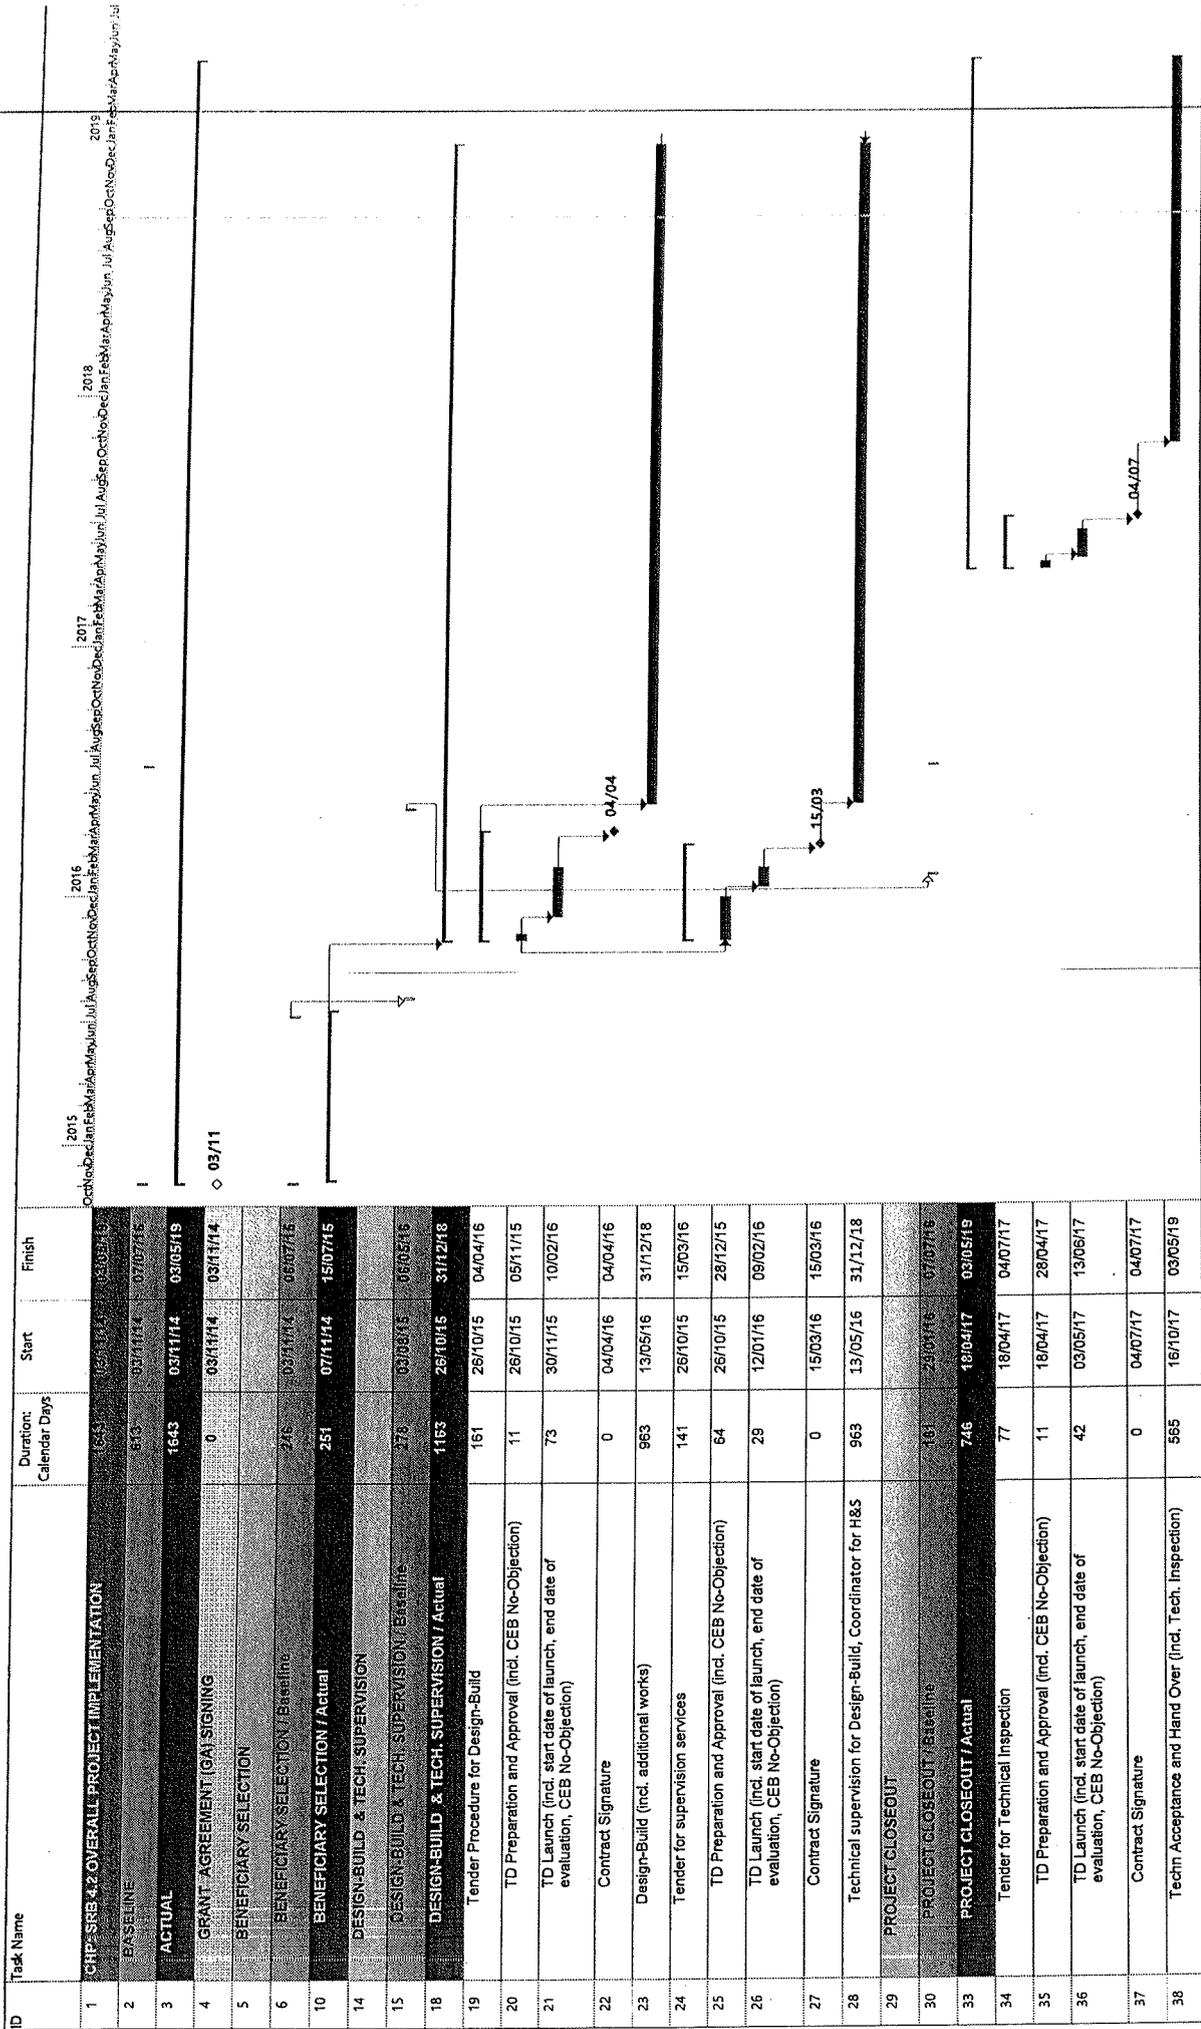


ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP: SRB 4.2 OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	813	03/11/14	07/07/15
3	ACTUAL	1643	03/11/14	03/05/19
4	GRANT AGREEMENT (G.A) SIGNING	0	03/11/14	03/11/14
5	BENEFICIARY SELECTION			
6	BENEFICIARY SELECTION / Baseline	215	03/11/14	05/07/15
10	BENEFICIARY SELECTION / Actual	251	07/11/14	15/07/15
14	DESIGN-BUILD & TECH. SUPERVISION			
15	DESIGN-BUILD & TECH. SUPERVISION / Baseline	275	03/03/15	06/05/16
18	DESIGN-BUILD & TECH. SUPERVISION / Actual	1163	26/10/15	31/12/18
19	Tender Procedure for Design-Build	161	26/10/15	04/04/16
20	TD Preparation and Approval (incl. CEB No-Objection)	11	26/10/15	05/11/15
21	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	73	30/11/15	10/02/16
22	Contract Signature	0	04/04/16	04/04/16
23	Design-Build (incl. additional works)	963	13/05/16	31/12/18
24	Tender for supervision services	141	26/10/15	15/03/16
25	TD Preparation and Approval (incl. CEB No-Objection)	64	26/10/15	28/12/15
26	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	29	12/01/16	09/02/16
27	Contract Signature	0	15/03/16	15/03/16
28	Technical supervision for Design-Build, Coordinator for H&S	963	13/05/16	31/12/18
29	PROJECT CLOSEOUT			
30	PROJECT CLOSEOUT / Baseline	161	29/03/16	07/07/16
33	PROJECT CLOSEOUT / Actual	746	18/04/17	03/05/19
34	Tender for Technical Inspection	77	18/04/17	04/07/17
35	TD Preparation and Approval (incl. CEB No-Objection)	11	18/04/17	28/04/17
36	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	42	09/05/17	13/06/17
37	Contract Signature	0	04/07/17	04/07/17
38	Techn Acceptance and Hand Over (incl. Tech. Inspection)	565	16/10/17	09/05/19

Project: SRB 4.2  
Construction of 30 Pre-Fab H.  
Date: 14/3/2018

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-Project.

**RHP: CHP SERBIA - SRB 4.2.1 - CONSTRUCTION OF 51 PRE-FAB HOUSES (EXTENSION OF SRB4/C2) - BASELINE AND ACTUAL SCHEDULE.**

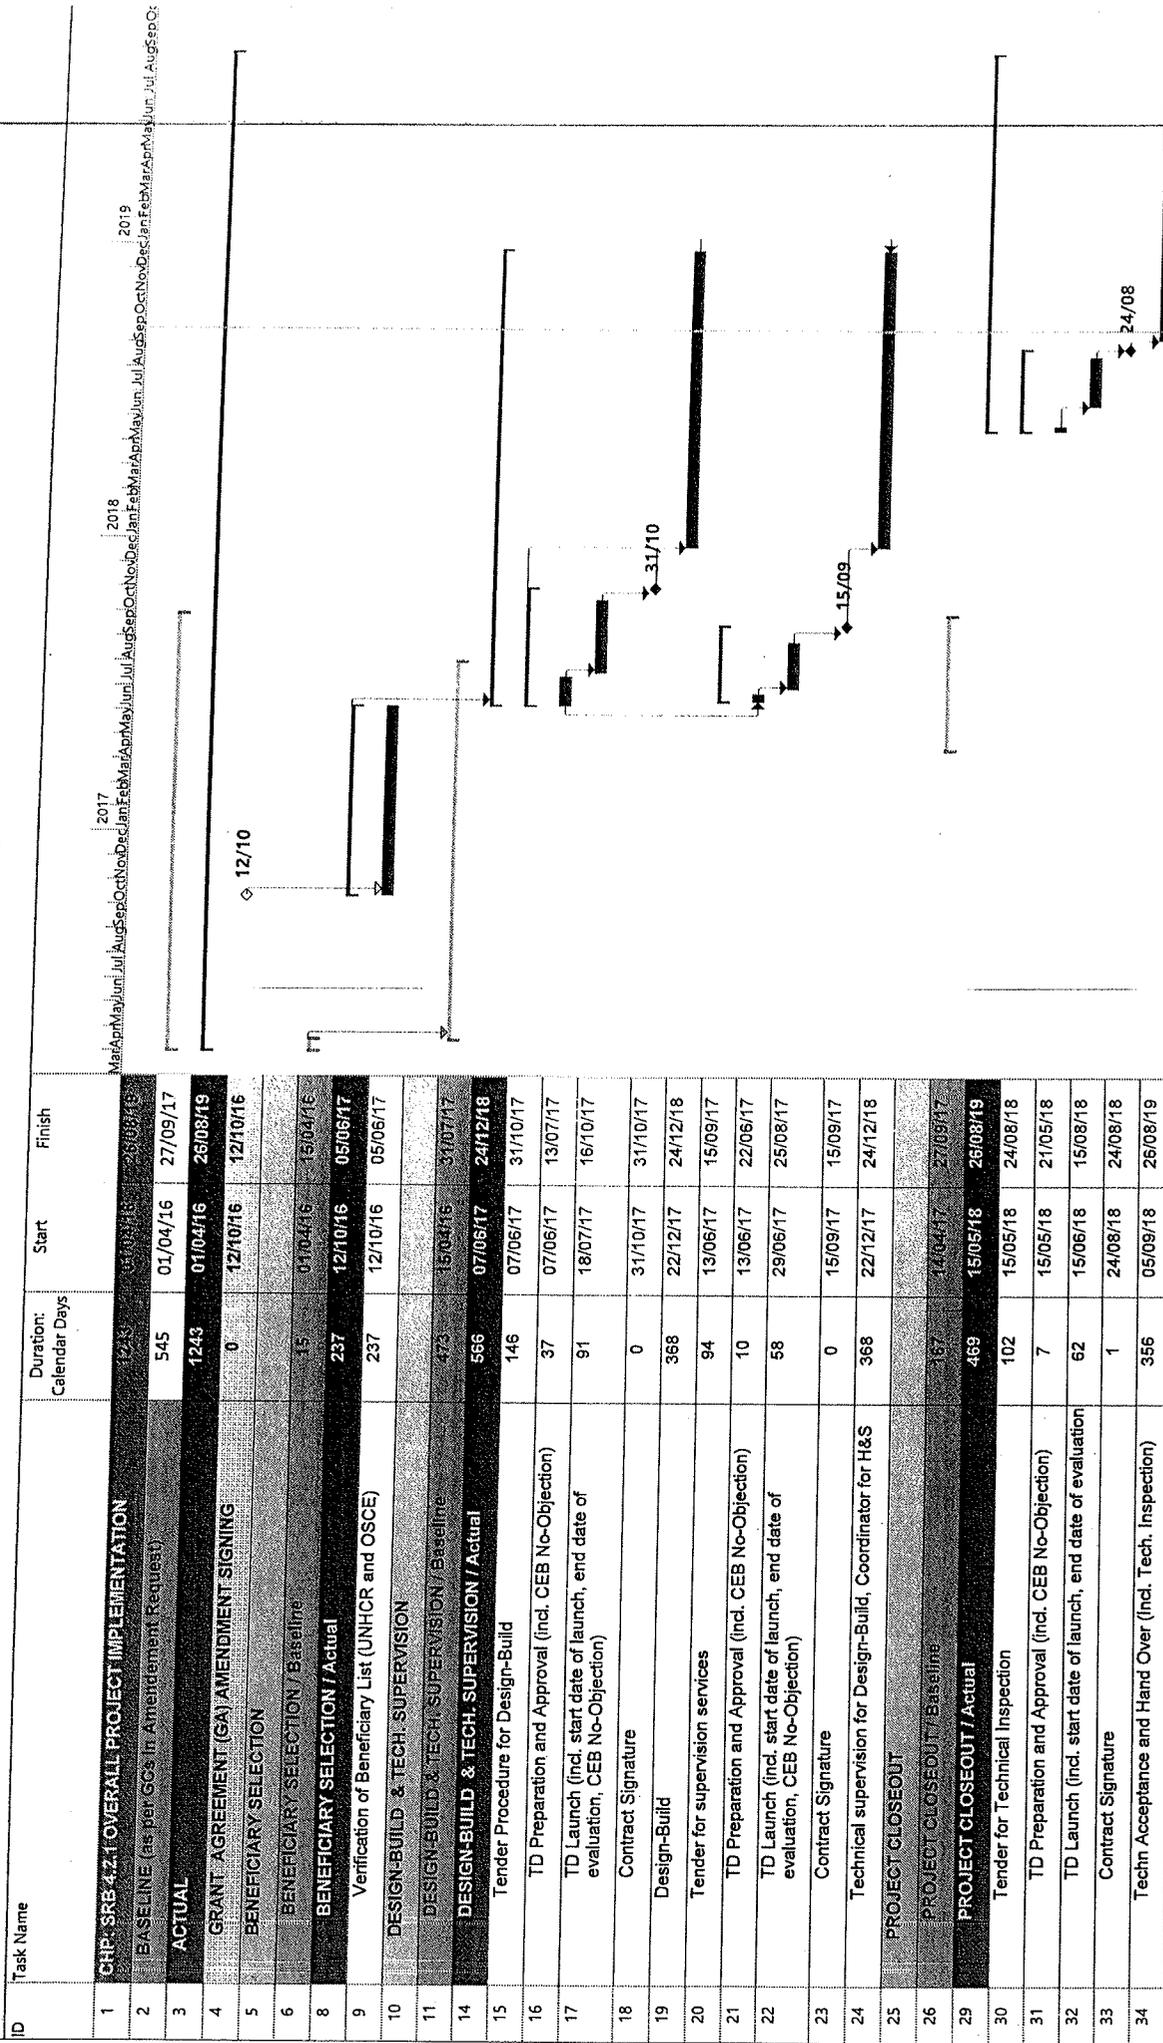

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 4.2.1 OVERALL PROJECT IMPLEMENTATION	243	01/04/16	27/09/17
2	BASELINE (as per GCs in Amendment Request)	545	01/04/16	26/08/19
3	ACTUAL	1243	01/04/16	26/08/19
4	GRANT AGREEMENT (GA) AMENDMENT SIGNING	0	12/10/16	12/10/16
5	BENEFICIARY SELECTION	15	01/04/16	15/04/16
6	BENEFICIARY SELECTION / Baseline	237	12/10/16	05/06/17
8	BENEFICIARY SELECTION / Actual	237	12/10/16	05/06/17
9	Verification of Beneficiary List (UNHCR and OSCE)	473	15/04/16	31/07/17
10	DESIGN-BUILD & TECH. SUPERVISION	566	07/06/17	24/12/18
11	DESIGN-BUILD & TECH. SUPERVISION / Baseline	146	07/06/17	31/10/17
14	DESIGN-BUILD & TECH. SUPERVISION / Actual	37	07/06/17	13/07/17
15	Tender Procedure for Design-Build	91	18/07/17	16/10/17
16	TD Preparation and Approval (incl. CEB No-Objection)	0	31/10/17	31/10/17
17	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	368	22/12/17	24/12/18
18	Contract Signature	94	13/06/17	15/09/17
19	Design-Build	10	13/06/17	22/06/17
20	Tender for supervision services	58	29/06/17	25/08/17
21	TD Preparation and Approval (incl. CEB No-Objection)	0	15/09/17	15/09/17
22	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	368	22/12/17	24/12/18
23	Contract Signature	167	16/04/17	27/09/17
24	Technical supervision for Design-Build, Coordinator for H&S	469	15/05/18	26/08/19
25	PROJECT CLOSEOUT	102	15/05/18	24/08/18
26	PROJECT CLOSEOUT / Baseline	7	15/05/18	21/05/18
29	PROJECT CLOSEOUT / Actual	62	15/06/18	15/08/18
30	Tender for Technical Inspection	1	24/08/18	24/08/18
31	TD Preparation and Approval (incl. CEB No-Objection)	356	05/09/18	26/08/19
32	TD Launch (incl. start date of launch, end date of evaluation)			
33	Contract Signature			
34	Techn Acceptance and Hand Over (incl. Tech. Inspection)			

Project: SRB 4.2.1  
 Construction of 51 Pre-Fab H. (  
 Date: 14/9/2018


Actual Task Timeframe  
 Grant Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Progress  
 Group of Activities

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

RHP: CHP SERBIA - SRB 4.3 - PROVISION OF 300 BUILDING MATERIAL PACKAGES  
- BASELINE & ACTUAL SCHEDULE -

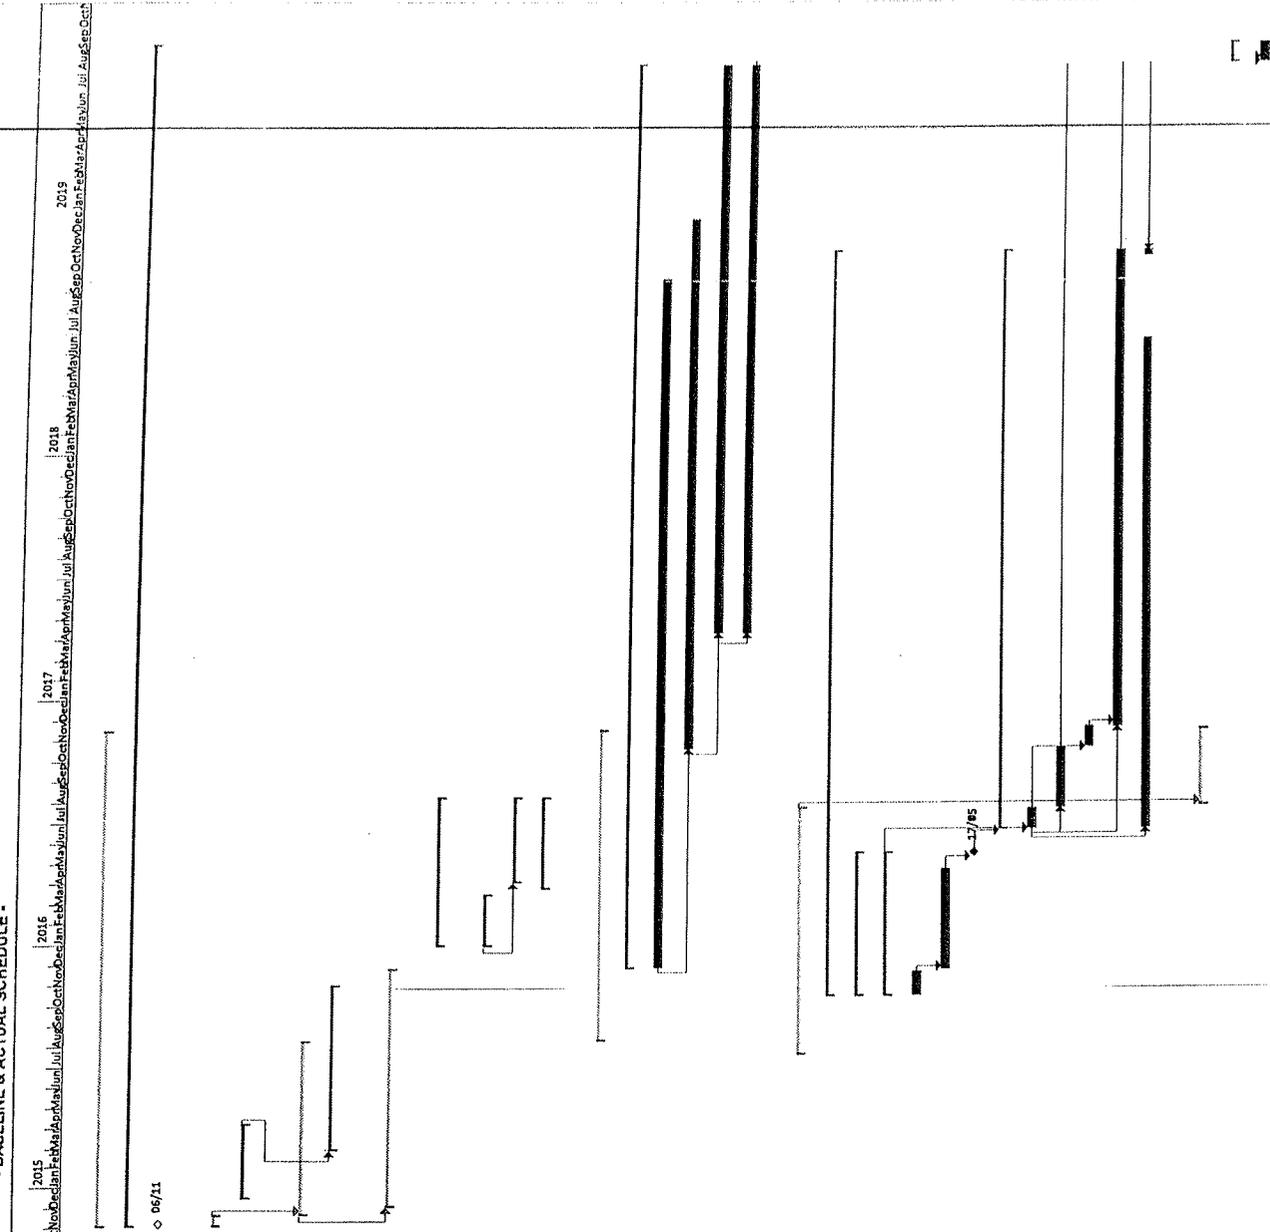

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP SRB 4.3 OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	245	03/11/15	04/14/16
3	ACTUAL			
4	GRANT AGREEMENT SIGNING	1766	03/11/14	04/09/19
5	PROCUREMENT PLAN	0	06/11/14	06/11/14
6	PROCUREMENT PLAN - Baseline	16	03/11/14	03/11/14
10	PROCUREMENT PLAN / Actual	112	15/12/14	06/04/15
14	SELECTION OF MUNICIPALITIES - GRANT (200 PACKAGES)			
15	SELECTION OF MUNICIPALITIES - GRANT (200 PACKAGES) / Actual	26	20/11/14	07/05/15
17	SELECTION OF MUNICIPALITIES - GRANT (200 PACKAGES) / Actual	245	27/02/15	31/10/15
22	TECHNICAL REPRESENTATIVE FOR CENTRALISED PROCEDURE & GRANT (100x200)			
23	TECHNICAL REPRESENTATIVE FOR CENTRALISED PROCEDURE & GRANT (100x200) - Baseline	157	01/12/14	2/13/15
26	TECHNICAL REPRESENTATIVE FOR CENTRALISED PROCEDURE & GRANT (100x200) / Actual	222	30/12/15	03/08/16
27	Tender for Technical Supervision for Provision of Build. Mat. (100)	76	30/12/15	15/03/16
31	Tender for Technical Supervision for Provision of Build. Mat. (200)	126	04/04/16	08/08/16
35	Tender for Technical Supervision for Provision of Build. Mat. (200) - Repeated process	136	25/03/16	08/08/16
39	GRANT IMPLEMENTATION (LSGs) - 200 PACKAGES			
40	GRANT IMPLEMENTATION (LSGs) - 200 PACKAGES / Baseline	143	10/08/15	13/11/16
45	GRANT IMPLEMENTATION (LSGs) - 200 PACKAGES / Actual	1345	27/11/15	06/08/19
46	Selection of Beneficiaries (by LSGs)	1028	27/11/15	20/09/18
47	Secondary Procurement Procedure for Building Material Supply (by LSGs)	791	19/10/16	19/12/18
48	Material Delivery and Installations (by LSGs)	848	10/04/17	06/08/19
49	Supervision of Material Delivery and Installation (200 PACKAGES)	843	10/04/17	06/08/19
50	CENTRALISED PROCUREMENT (100 PACKAGES)			
51	CENTRALISED PROCUREMENT (100 PACKAGES) - Baseline	369	20/07/16	23/07/16
59	CENTRALISED PROCUREMENT (100 PACKAGES) / Actual	1111	16/10/15	31/10/18
60	TENDER PROCEDURE (CENTRALISED 100 packages) / Actual	214	16/10/15	17/05/16
61	Tender Procedure for Building Material	214	16/10/15	17/05/16
62	TD Preparation and Approval (incl. CEB No-Objection)	36	16/10/15	20/11/15
63	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	150	24/11/15	21/04/16
64	Contract Signature	0	17/05/16	17/05/16
65	MATERIAL DELIVERY AND INSTALLATION (CENTRALISED 100 packages) / Act	862	21/06/16	31/10/18
66	Delivery of Building Material 1st Phase	30	21/06/16	21/07/16
67	Installation of Building Material 1 (Final Beneficiaries)	90	22/07/16	19/10/16
68	Delivery of Building Material 2nd Phase	31	20/10/16	19/11/16
69	Installation of Building Material 2 (Final Beneficiaries)	711	19/11/16	31/10/18
70	Technical supervision for Provision of Build. Mat (100)	862	21/06/16	31/10/18
71	PROJECT CLOSEOUT PHASE (100x200)			
72	PROJECT CLOSEOUT PHASE (100x200) / Baseline	13	21/07/16	07/11/16
74	PROJECT CLOSEOUT PHASE (100x200) / Actual	23	08/03/19	04/09/19
75	Verification of Material Installation	29	06/06/19	04/09/19

Actual Task Timeframe  
PIU Milestone

Estimated Project Activities Summary  
Actual Project Activities Summary


CEB Milestone  
Manual Summary

Progress

Project: SRB 4.3  
Provision of 300 BM  
Date: 14/9/2018

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown. In components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA - SRB 4.3.1 - PROVISION OF 264 BUILDING MATERIAL PACKAGES (62+202, EXTENSION OF SRB4(C3) - BASELINE & ACTUAL SCHEDULE .**

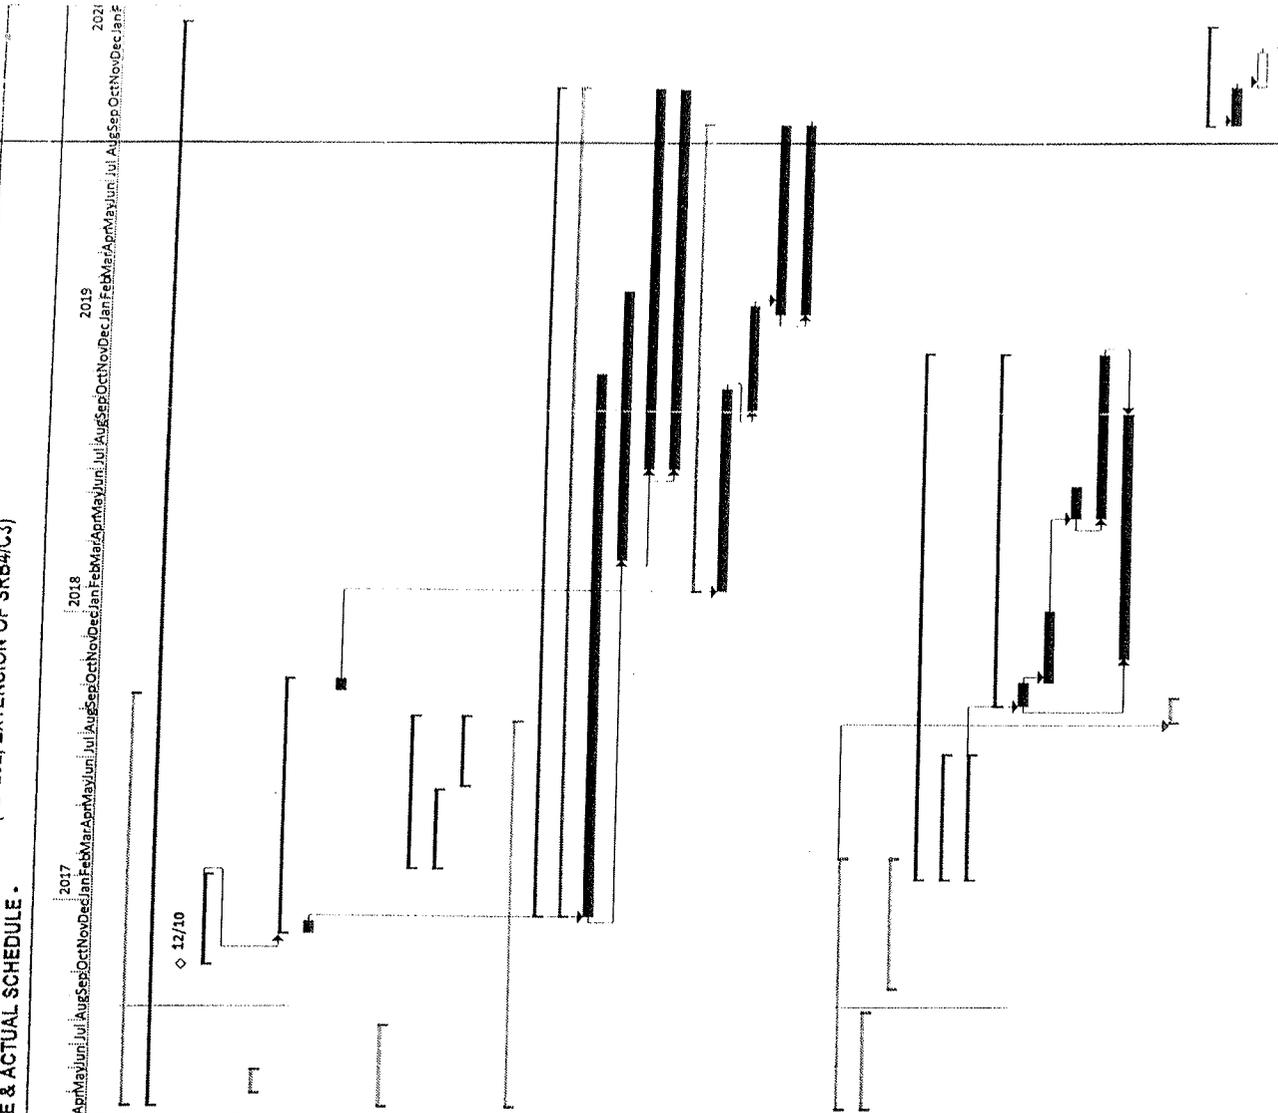

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP SRB 4.3.1: OVERALL PROJECT IMPLEMENTATION	524	15/04/16	20/01/20
2	BASELINE	0	12/10/15	12/10/15
3	ACTUAL	115	12/10/16	03/02/17
4	GRANT AGREEMENT SIGNING	10	01/05/16	31/05/16
5	PROCUREMENT PLAN / Actual	324	21/11/16	16/01/17
9	SELECTION OF MUNICIPALITIES - GRANT (202 PACKAGES)	15	21/11/16	05/12/16
10	SELECTION OF MUNICIPALITIES - GRANT (202 PACKAGES) / Actual	15	26/09/17	10/10/17
11	TECHNICAL REPRESENTATIVE FOR CENTRALISED PROCEDURE & GRANT (62+202)	104	08/04/17	27/07/17
12	TECHNICAL REPRESENTATIVE FOR CENTRALISED PROCEDURE & GRANT (62+202)	184	13/02/17	28/08/17
13	Grant Contracts Signature with LSGs placed on reserve list (166BM)	100	13/02/17	23/05/17
14	Grant Contracts Signature with LSGs placed on reserve list (36BM)	89	29/05/17	25/08/17
15	TECHNICAL REPRESENTATIVE FOR CENTRALISED PROCEDURE & GRANT (62+202)	31	13/04/18	18/05/18
16	TECHNICAL REPRESENTATIVE FOR CENTRALISED PROCEDURE & GRANT (62+202)	1051	14/12/18	30/01/19
17	Tender for Technical Supervision for Provision of Build. Mat. (62BM)	688	14/12/18	30/01/19
18	Tender for Technical Supervision for Provision of Build. Mat. (202BM)	257	01/02/18	16/10/18
19	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES	132	19/09/18	28/01/19
20	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES / Actual	241	18/01/19	16/09/19
21	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES / Actual	241	18/01/19	16/09/19
22	Selection of Beneficiaries (by LSGs)	483	05/07/18	30/10/19
23	Secondary Procurement Procedure for Building Material Supply (by LSGs)	482	05/07/18	30/10/19
24	Material Delivery and Installation (by LSGs)	557	07/07/18	30/10/19
25	Supervision of Material Delivery and Installation	257	01/02/18	16/10/18
26	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES	132	19/09/18	28/01/19
27	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES / Actual	241	18/01/19	16/09/19
28	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES / Actual	241	18/01/19	16/09/19
29	Selection of Beneficiaries (by LSGs)	370	15/04/16	23/02/17
30	Secondary Procurement Procedure for Building Material Supply (by LSGs)	124	15/04/16	19/08/16
31	Material Delivery and Installation (by LSGs)	186	15/09/16	29/02/17
32	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES	685	02/02/17	30/11/18
33	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES / Actual	159	02/02/17	11/07/17
34	GRANT IMPLEMENTATION (LSGs) - 202 PACKAGES / Actual	159	02/02/17	11/07/17
35	Tender Procedure for Building Material	445	11/09/17	30/11/18
36	MATERIAL DELIVERY AND INSTALLATION (CENTRALISED 62 packages) / Actual	30	11/09/17	11/10/17
37	Delivery of Building Material 1st Phase	90	11/10/17	08/01/18
38	Installation of Building Material 1 (Final Beneficiaries)	40	07/05/18	15/06/18
39	Delivery of Building Material 2nd Phase	207	07/05/18	30/11/18
40	Installation of Building Material 2 (Final Beneficiaries)	311	10/11/17	17/09/18
41	Technical supervision for Provision of Build. Mat	41	10/08/17	20/09/17
42	PROJECT CLOSEOUT PHASE	125	16/09/19	20/01/20
43	PROJECT CLOSEOUT PHASE / Actual	49	16/09/19	04/11/19
44	Verification of Material Installation	45	04/11/19	19/12/19
45	Final Progress Report and Expenditure Verification Report	32	13/12/19	20/01/20
46	Final Acceptance by the CEB			

Project: SRB 4.3.1  
 Provision of 219 BM (62+157, Etc)  
 Date: 14/9/2018


Actual Task Timeframe  
 PIU Milestone

Estimated Project Activities Summary  
 Actual Project Activities Summary

CEB Milestone  
 Manual Summary  
 Progress

(\* Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA - SRB 4.3.2 - PROVISION OF 115 BUILDING MATERIAL PACKAGES  
- BASELINE AND ACTUAL SCHEDULE -**

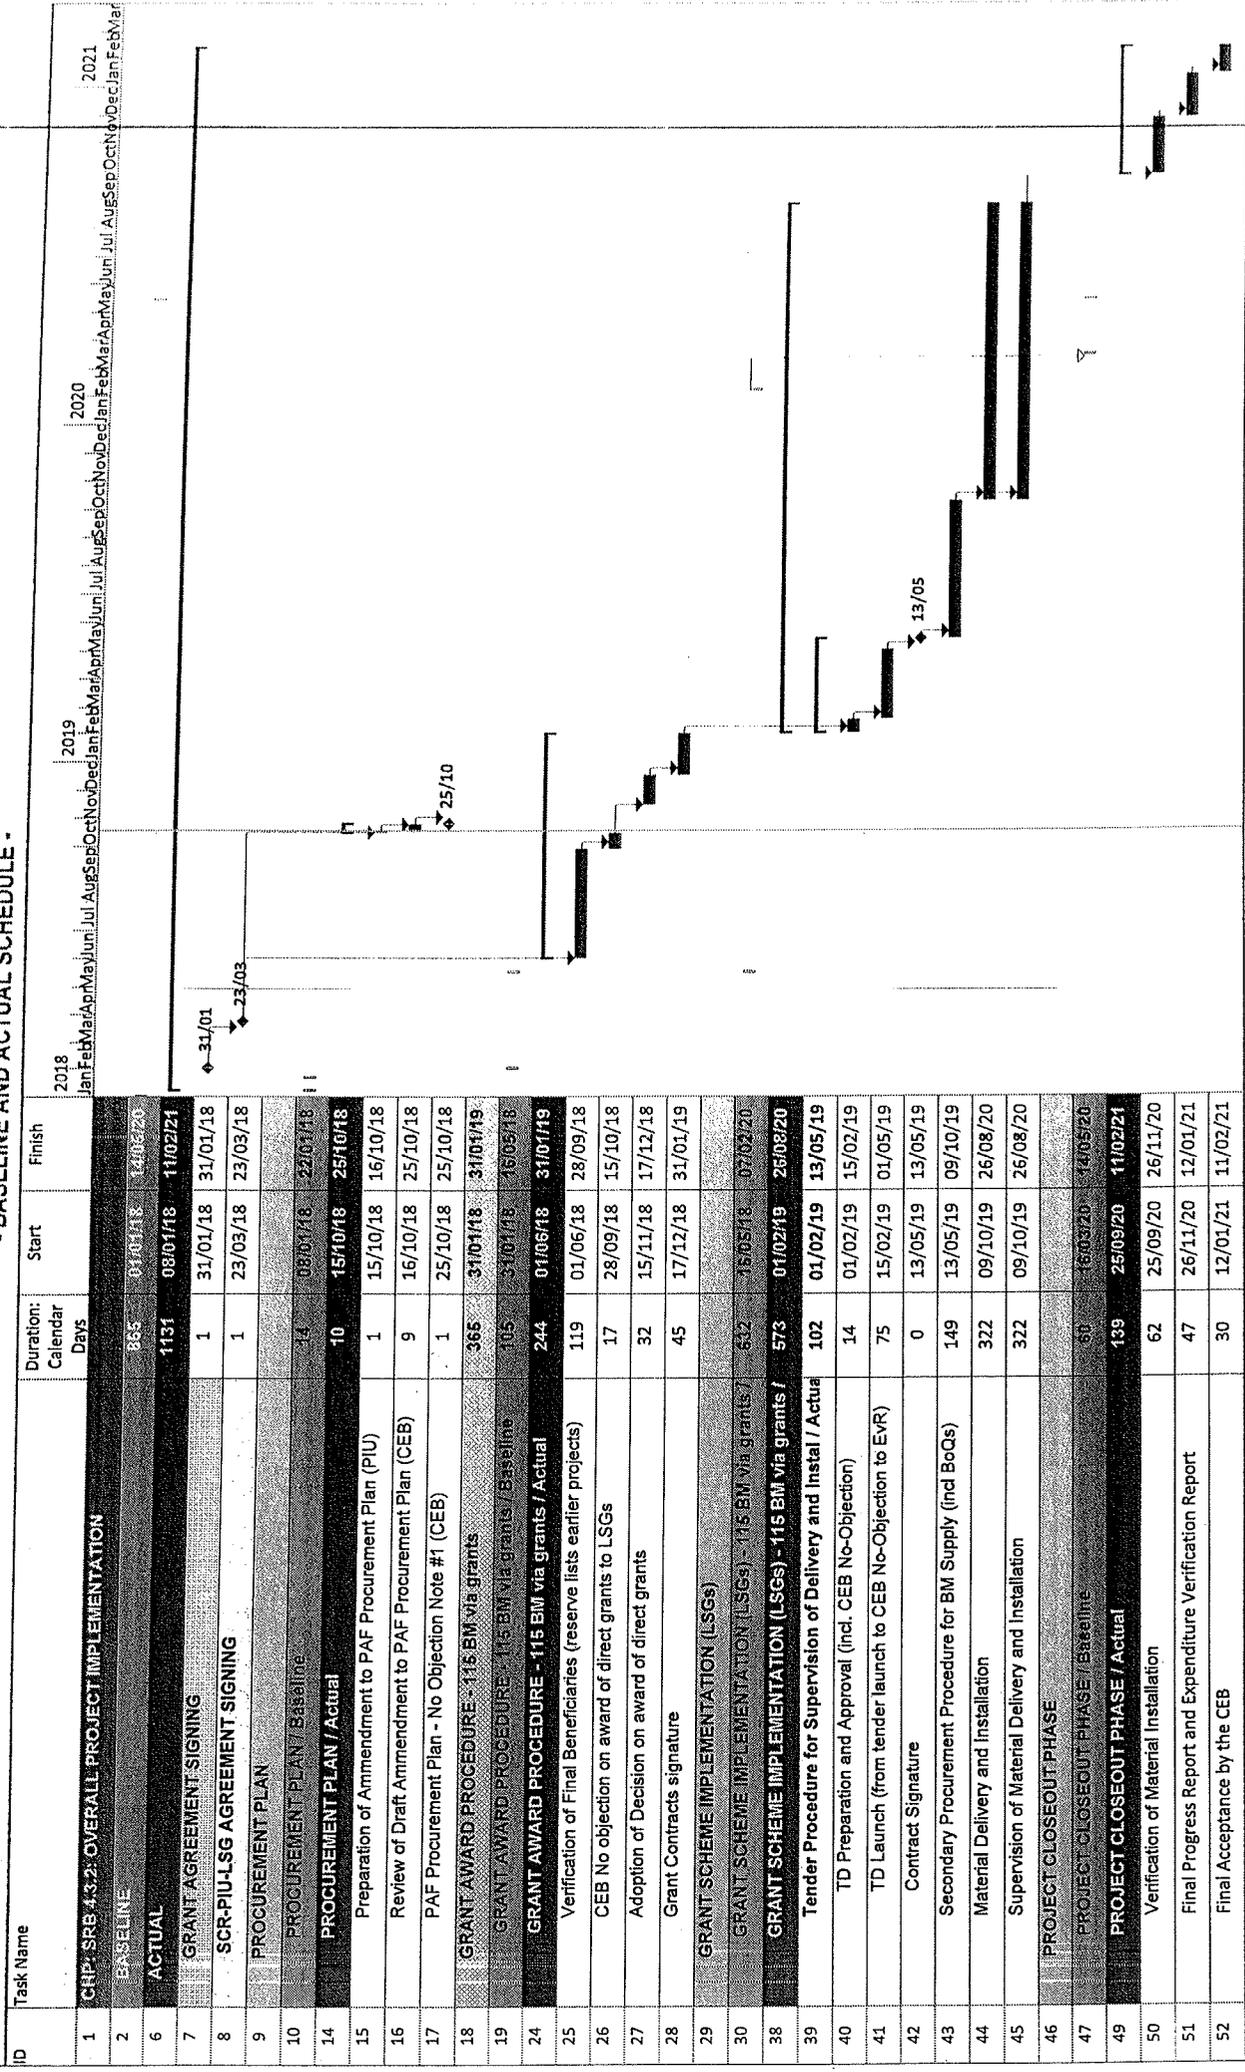


Project: SRB 4.3.2  
Provision of 115 BM Packages  
Date: 16/10/2018

Actual Task Timeframe: \_\_\_\_\_  
Grant Agreement Signing: \_\_\_\_\_

Estimated Project Activities Summary: \_\_\_\_\_  
Actual Project Activities Summary: \_\_\_\_\_

Group of Activities: \_\_\_\_\_  
Progress: \_\_\_\_\_


**RHP: CHP SERBIA - SRB 4.4 -PURCHASING OF 70 VILLAGE HOUSES  
- BASELINE & ACTUAL SCHEDULE .**

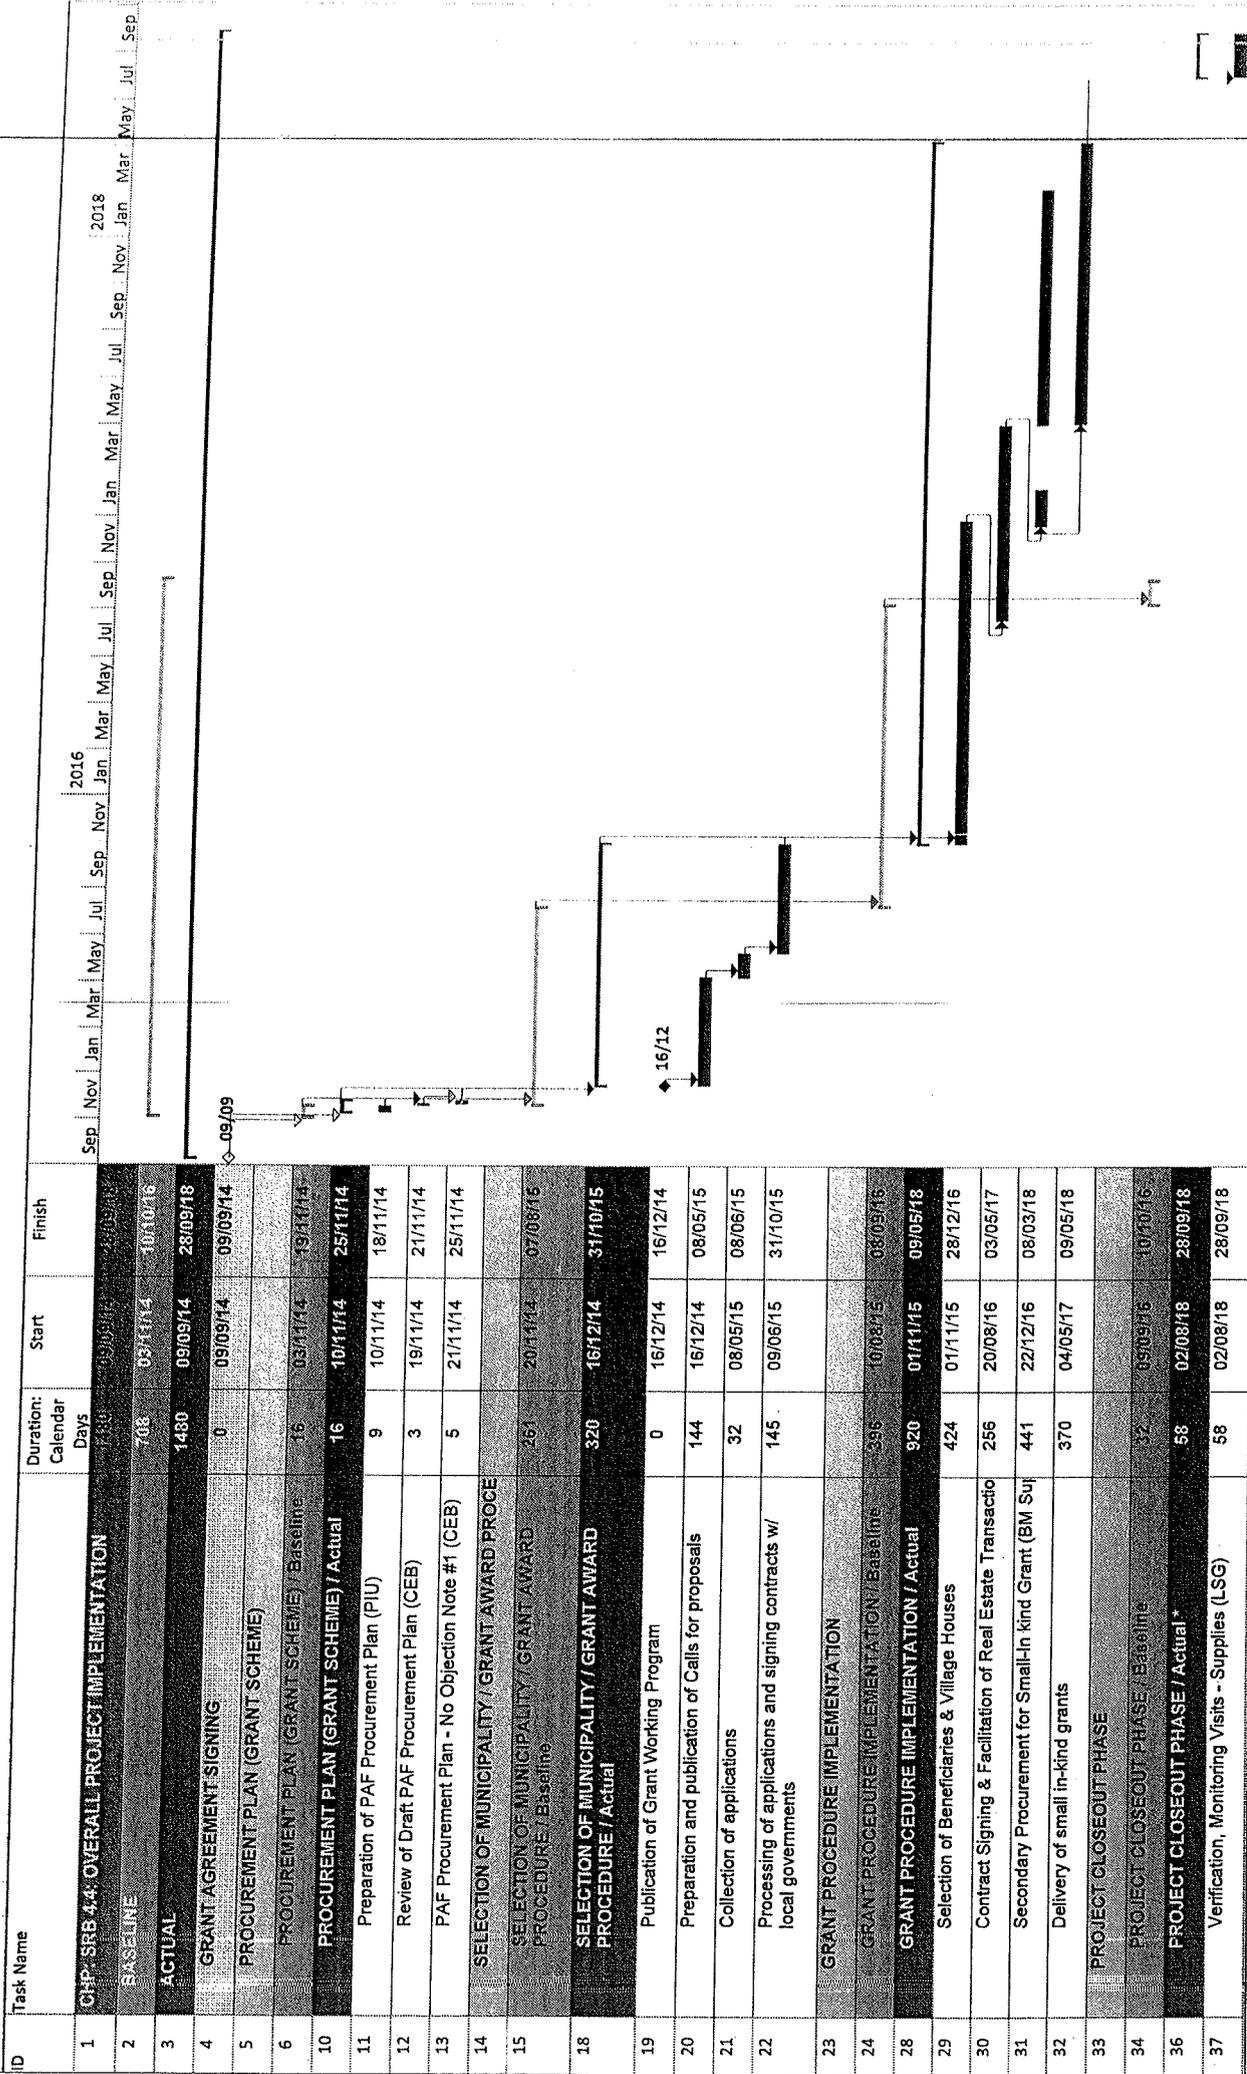

Project: SRB 4.4  
70 Village Houses  
Date: 14/9/2018

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA - SRB 4.4.1 -PURCHASING OF 200 VILLAGE HOUSES (EXTENSION OF SRB4/IC4) - BASELINE & ACTUAL SCHEDULE.**

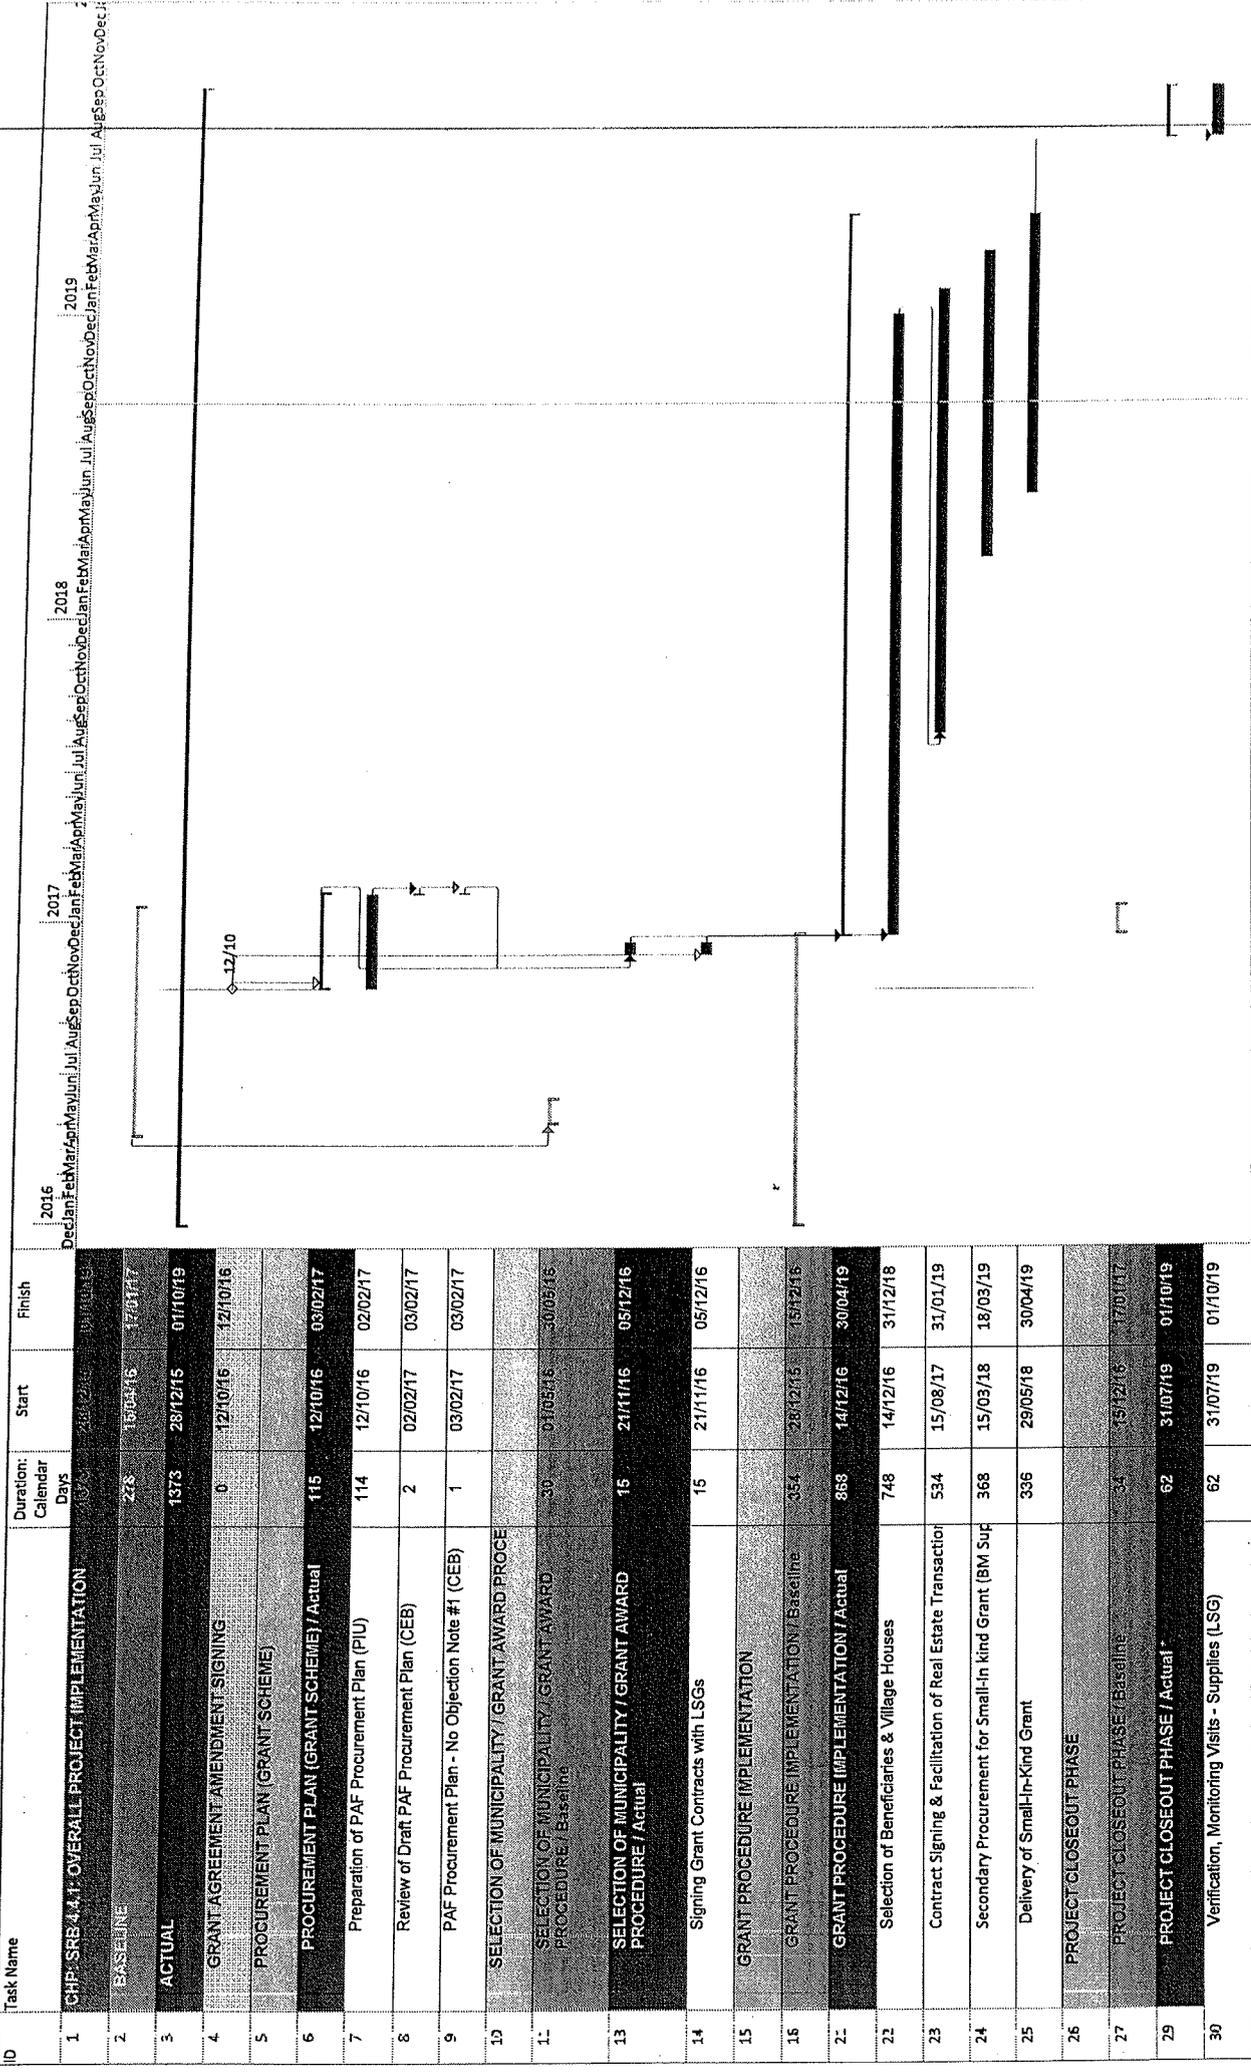

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP - SRB 4.4.1: OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	228	16/04/16	17/01/17
3	ACTUAL	1373	28/12/15	01/10/19
4	GRANT AGREEMENT AMENDMENT/ SIGNING	0	12/10/16	12/10/16
5	PROCUREMENT PLAN (GRANT SCHEME)			
6	PROCUREMENT PLAN (GRANT SCHEME) / Actual	115	12/10/16	03/02/17
7	Preparation of PAF Procurement Plan (PIU)	114	12/10/16	02/02/17
8	Review of Draft PAF Procurement Plan (CEB)	2	02/02/17	03/02/17
9	PAF Procurement Plan - No Objection Note #1 (CEB)	1	03/02/17	03/02/17
10	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE			
11	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE / Baseline	30	01/05/16	30/05/16
13	SELECTION OF MUNICIPALITY / GRANT AWARD PROCEDURE / Actual	15	21/11/16	05/12/16
14	Signing Grant Contracts with LSGs	15	21/11/16	05/12/16
15	GRANT PROCEDURE IMPLEMENTATION			
16	GRANT PROCEDURE IMPLEMENTATION / Baseline	354	28/12/15	15/12/16
21	GRANT PROCEDURE IMPLEMENTATION / Actual	868	14/12/16	30/04/19
22	Selection of Beneficiaries & Village Houses	748	14/12/16	31/12/18
23	Contract Signing & Facilitation of Real Estate Transaction	534	15/08/17	31/01/19
24	Secondary Procurement for Small-In kind Grant (BM Sup	368	15/03/18	18/03/19
25	Delivery of Small-In-Kind Grant	336	29/05/18	30/04/19
26	PROJECT CLOSEOUT PHASE			
27	PROJECT CLOSEOUT PHASE / Baseline	34	15/12/16	17/01/17
29	PROJECT CLOSEOUT PHASE / Actual *	62	31/07/19	01/10/19
30	Verification, Monitoring Visits - Supplies (LSG)	62	31/07/19	01/10/19

Project: SRB 4.4.1  
 Purchase of 129 Village Houses  
 Date: 14/9/2018


Actual Task Timeframe  
 Grant Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Group of Activities  
 Progress

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same sub-project.

**RHP: CHP SERBIA - SRB 4.4.2 -PROVISION OF 76 VILLAGE HOUSES decentralised - BASELINE AND ACTUAL SCHEDULE .**

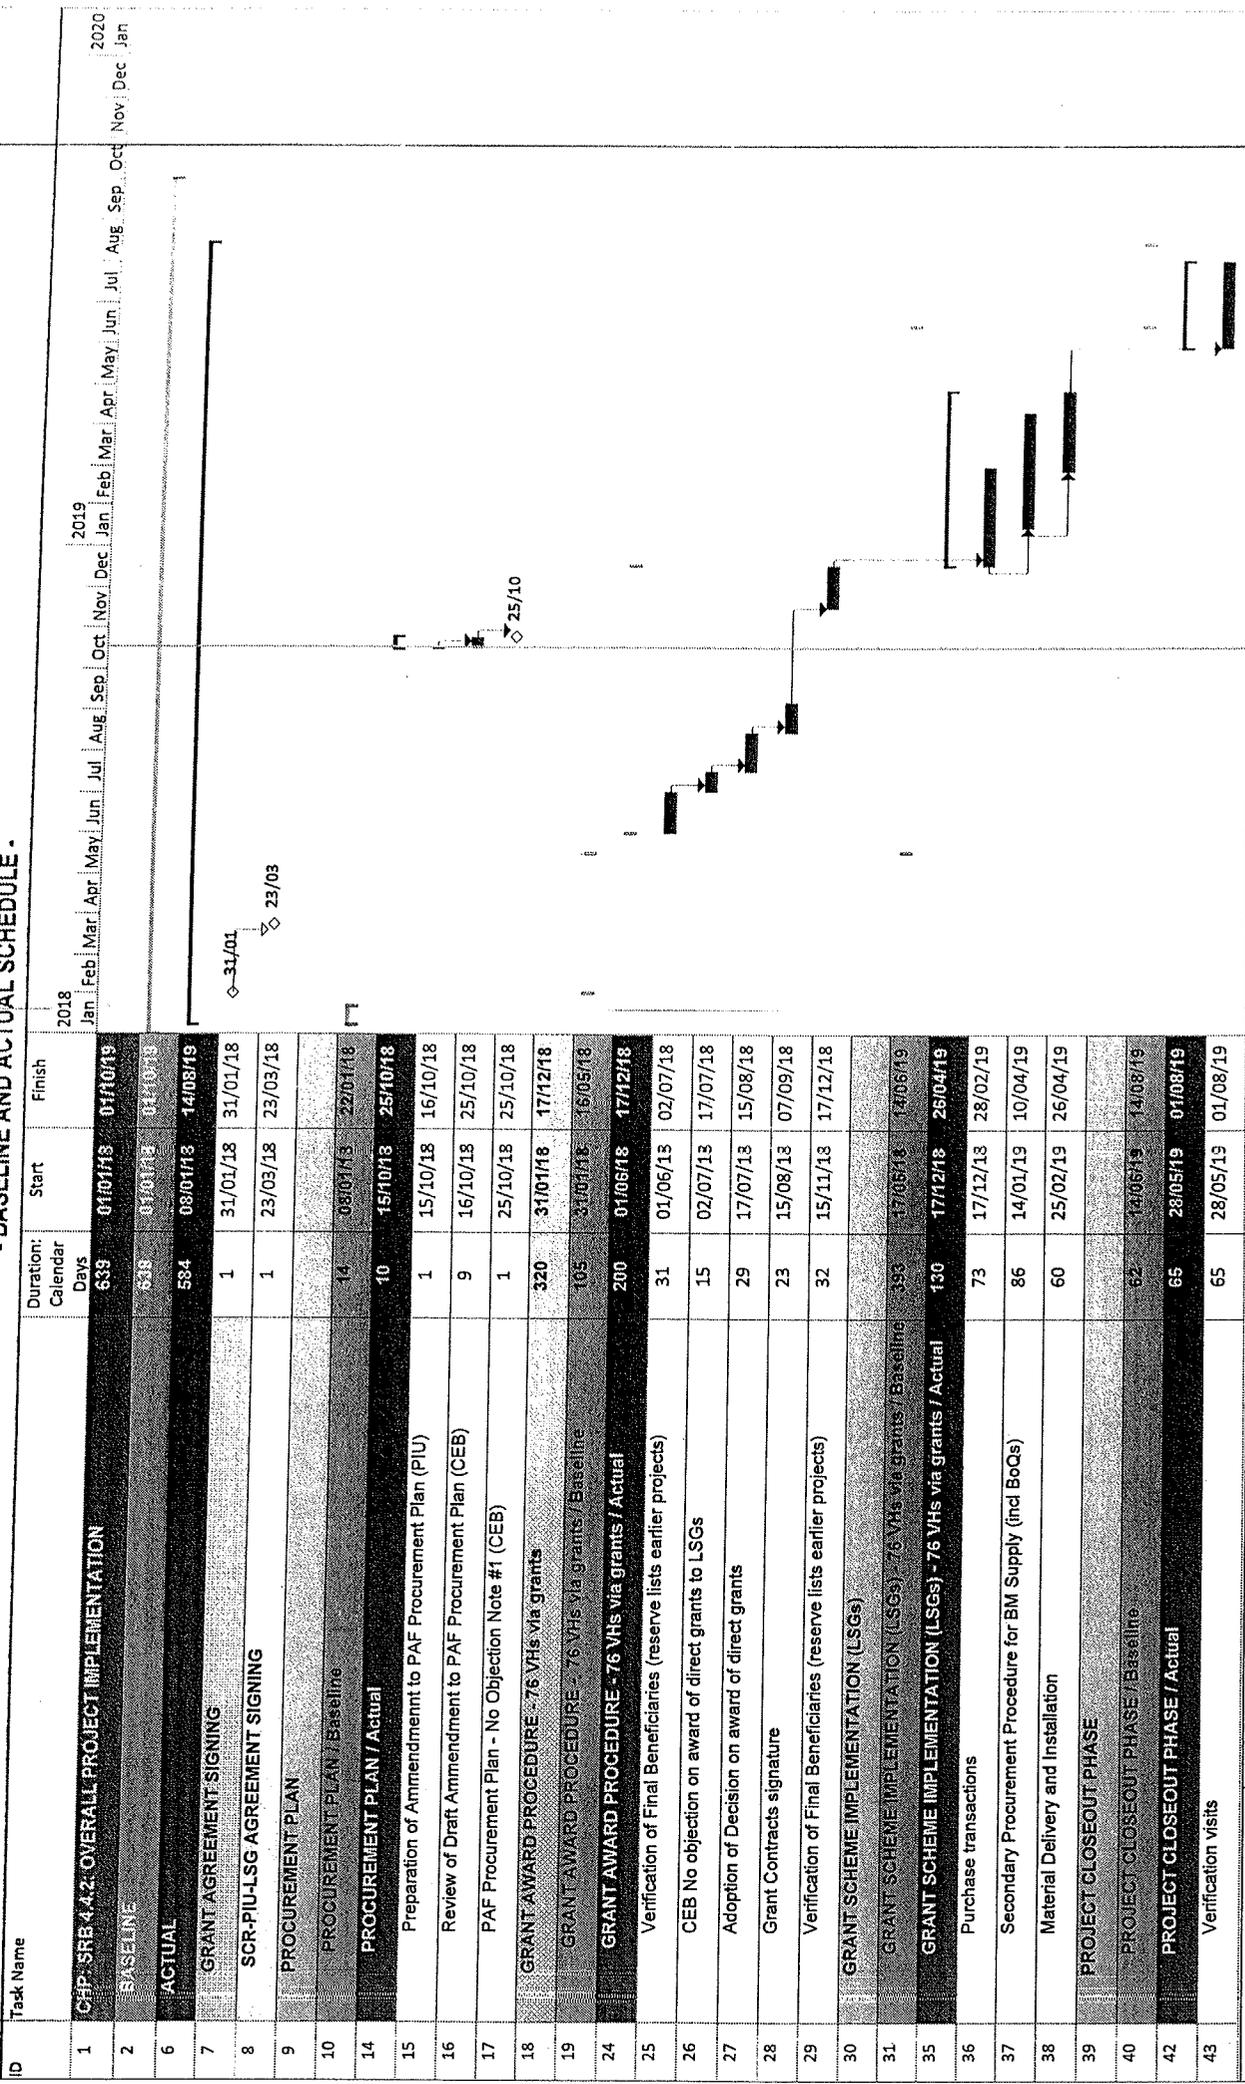

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 4.4.2- OVERALL PROJECT IMPLEMENTATION	639	01/01/18	01/10/19
2	BASELINE	638	01/01/18	01/10/18
6	ACTUAL	584	08/01/18	14/08/19
7	GRANT AGREEMENT SIGNING	1	31/01/18	31/01/18
8	SCR-PIU-LSG AGREEMENT SIGNING	1	23/03/18	23/03/18
9	PROCUREMENT PLAN			
10	PROCUREMENT PLAN / Baseline	14	08/01/18	22/01/18
14	PROCUREMENT PLAN / Actual	10	15/10/18	25/10/18
15	Preparation of Amendment to PAF Procurement Plan (PIU)	1	15/10/18	16/10/18
16	Review of Draft Amendment to PAF Procurement Plan (CEB)	9	16/10/18	25/10/18
17	PAF Procurement Plan - No Objection Note #1 (CEB)	1	25/10/18	25/10/18
18	GRANT AWARD PROCEDURE - 76 VHS via grants	320	31/01/18	17/12/18
19	GRANT AWARD PROCEDURE - 76 VHS via grants / Baseline	105	31/01/18	16/05/18
24	GRANT AWARD PROCEDURE - 76 VHS via grants / Actual	200	01/06/18	17/12/18
25	Verification of Final Beneficiaries (reserve lists earlier projects)	31	01/06/18	02/07/18
26	CEB No objection on award of direct grants to LSGs	15	02/07/18	17/07/18
27	Adoption of Decision on award of direct grants	29	17/07/18	15/08/18
28	Grant Contracts signature	23	15/08/18	07/09/18
29	Verification of Final Beneficiaries (reserve lists earlier projects)	32	15/11/18	17/12/18
30	GRANT SCHEME IMPLEMENTATION (LSGs)			
31	GRANT SCHEME IMPLEMENTATION (LSGs) - 76 VHS via grants / Baseline	393	17/06/18	14/05/19
35	GRANT SCHEME IMPLEMENTATION (LSGs) - 76 VHS via grants / Actual	130	17/12/18	26/04/19
36	Purchase transactions	73	17/12/18	28/02/19
37	Secondary Procurement Procedure for BM Supply (incl BoQs)	86	14/01/19	10/04/19
38	Material Delivery and Installation	60	25/02/19	26/04/19
39	PROJECT CLOSEOUT PHASE			
40	PROJECT CLOSEOUT PHASE / Baseline	62	13/06/18	14/08/19
42	PROJECT CLOSEOUT PHASE / Actual	65	28/05/19	01/08/19
43	Verification visits	65	28/05/19	01/08/19


Project: SRB 4.4.2  
 Provision of 76 VHS  
 Date: 16/10/2018

Actual Task Timeframe  
 Grant Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Group of Activities  
 Progress

RHP: CHP SERBIA - SRB 5.1 - CONSTRUCTION OF 827 APARTMENTS

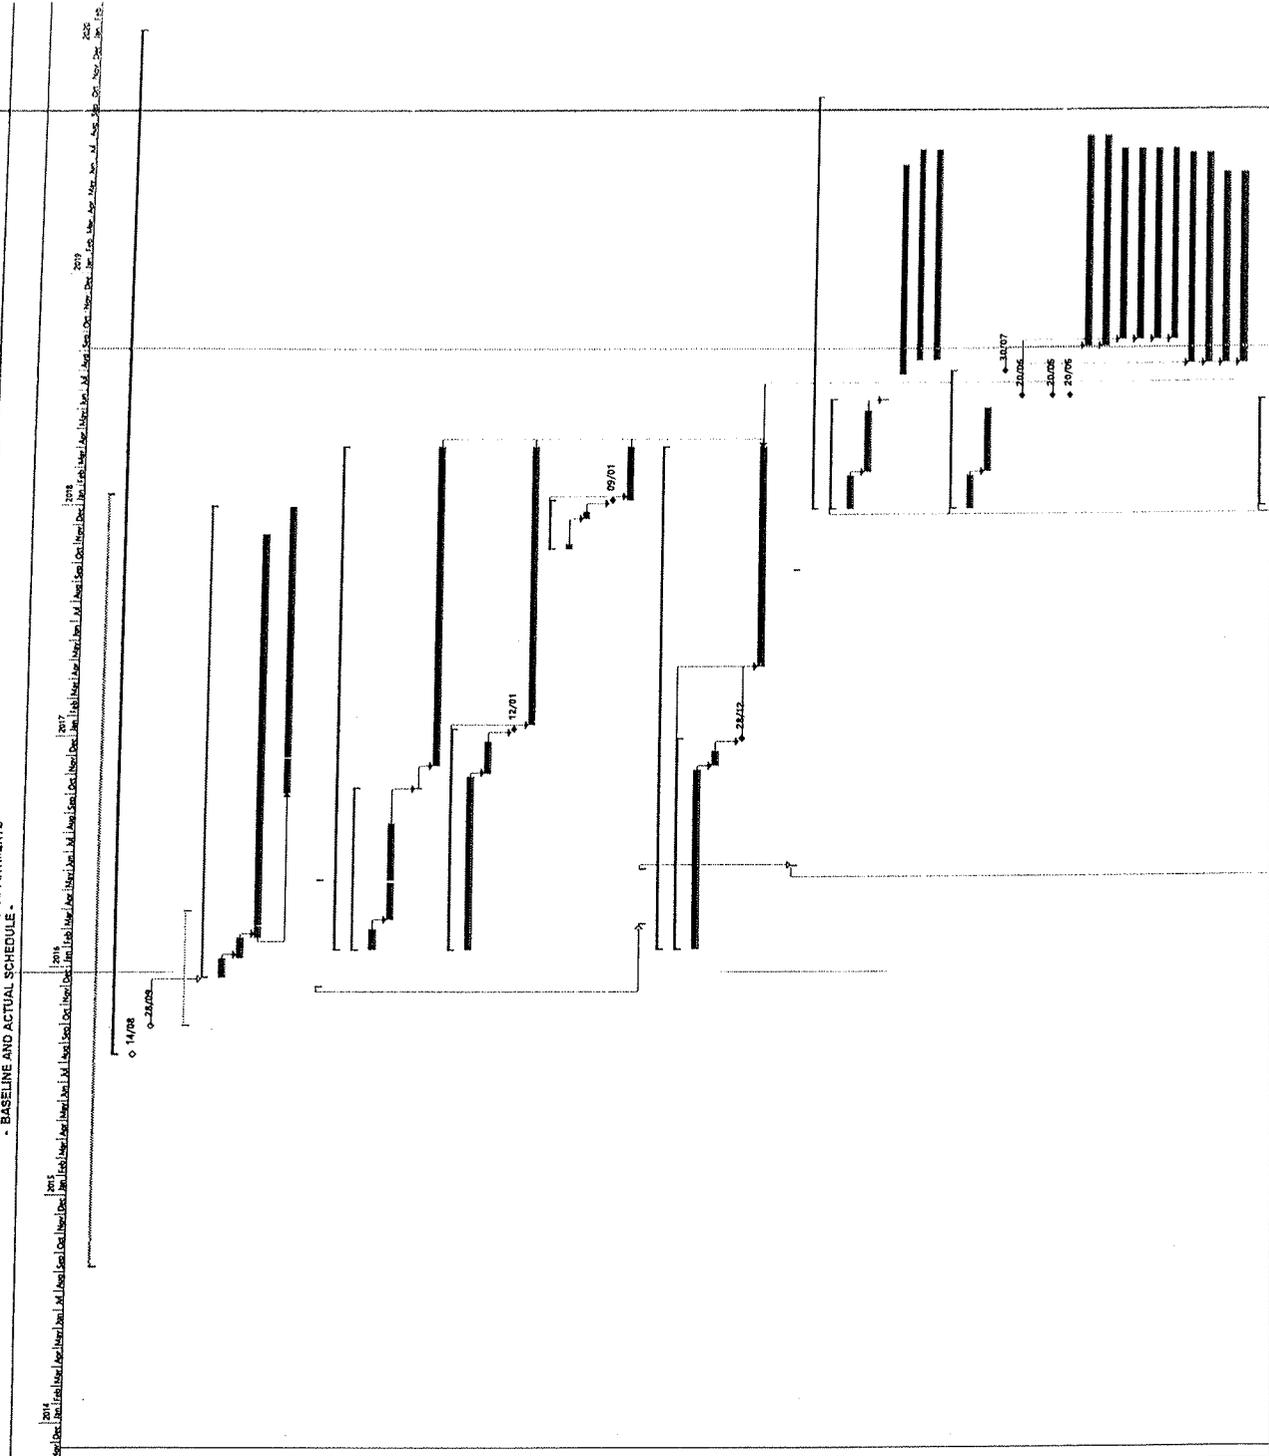

ID	Task Name	Duration (Calendar Days)	Start	Finish
1	START OF THE OFFICIAL PROCESS IMPLEMENTATION	1	2015-01-01	2015-01-01
2	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
3	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
4	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
5	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
6	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
7	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
8	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
9	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
10	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
11	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
12	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
13	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
14	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
15	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
16	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
17	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
18	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
19	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
20	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
21	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
22	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
23	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
24	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
25	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
26	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
27	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
28	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
29	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
30	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
31	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
32	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
33	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
34	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
35	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
36	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
37	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
38	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
39	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
40	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
41	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
42	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
43	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
44	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
45	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
46	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
47	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
48	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
49	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
50	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
51	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
52	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
53	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
54	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
55	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
56	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
57	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
58	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
59	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
60	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
61	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
62	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
63	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
64	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
65	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
66	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
67	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
68	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
69	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
70	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
71	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
72	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
73	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
74	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
75	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
76	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
77	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01
78	GRANT AGREEMENT SIGNING	1	2015-01-01	2015-01-01

Project SRB 5.1  
 827 Apartments  
 Date: 30/03/2018

Actual Task Timeline

Estimated Project Activities Summary


Actual Project Activities Summary

Group of Activities

17. This Program Report is Esercizio's Verification Report and Final Acceptance by CEB as shown in components that have the largest project implementation duration within the same Subproject.


RHP - CHP SERBIA - SRB 5.1 - CONSTRUCTION OF B27 APARTMENTS - BASELINE AND ACTUAL SCHEDULE -

ID	Task Name	Duration Calendar Days	Start	Finish
80	TD Launch (incl. start date of launch, and date of evaluation, CEB No-Ob)	113	01/02/18	24/05/18
81	Contract Signature	1	13/05/18	13/05/18
82	Construction Works Non-Safe	452	13/07/18	07/10/19
83	Tender procedure for Construction works 11 LSG	102	21/06/18	30/09/18
84	TD Preparation and Approval (incl. CEB No-Objection)	6	21/06/18	26/06/18
85	TD Launch (incl. start date of launch, and date of evaluation, CEB No-Ob)	78	04/07/18	17/09/18
86	Contract Signature TLESG	3	28/08/18	30/08/18
87	Construction Works KIRINDA	331	30/10/18	25/09/19
88	Construction Works PANCEVO	331	30/10/18	25/09/19
89	Construction Works ZRENJANIN	331	30/10/18	25/09/19
90	Construction Works TEMERIN	331	30/10/18	25/09/19
91	Construction Works B. PETROVAC	331	30/10/18	25/09/19
92	Construction Works B. PALANKA	331	30/10/18	25/09/19
93	Construction Works S. MITROVICA	331	30/10/18	25/09/19
94	Construction Works IRIG	331	30/10/18	25/09/19
95	Construction Works S. KARLOVCI	331	30/10/18	25/09/19
96	Construction Works N. PAZAR	331	30/10/18	25/09/19
97	Construction Works LUCANI	331	30/10/18	25/09/19
98	Construction Works KIKINDA	331	30/10/18	25/09/19
99	Construction Works ZEMUN	331	30/10/18	25/09/19
100	Construction Works ZEMUNJANIN	331	30/10/18	25/09/19
101	SUPERVISION SERBIA / Actual	645	28/07/18	04/11/19
102	Tender procedure for Supervision of Works	183	28/07/18	30/07/18
103	TD Preparation and Approval (incl. CEB No-Objection)	39	28/07/18	06/08/18
104	TD Launch (incl. start date of launch, and date of evaluation, CEB No-Ob)	72	20/08/18	30/09/18
105	Contract Signature Valjevo, Uzen, Cajalina, Hg. S. Karlovi, Pancevo, Zl	1	14/08/18	14/08/18
106	Contract Signature Novi Sad	1	18/08/18	18/08/18
107	Contract Signature Hg. Kosevare	1	30/07/18	30/07/18
108	Supervision of Works & Coordinator for safety and health at work NOVMI SAJ	452	10/09/18	04/11/19
109	Supervision of Works & Coordinator for safety and health at work VALJEVO	333	17/09/18	15/07/19
110	Supervision of Works & Coordinator for safety and health at work UZEN	333	17/09/18	15/07/19
111	Supervision of Works & Coordinator for safety and health at work CAJETIN	333	17/09/18	15/07/19
112	Supervision of Works & Coordinator for safety and health at work NIŠ	333	07/09/18	05/08/19
113	Supervision of Works & Coordinator for safety and health at work KRUSEVA	333	07/09/18	05/08/19
114	Supervision of Works & Coordinator for safety and health at work IRIG	331	30/10/18	25/09/19
115	Supervision of Works & Coordinator for safety and health at work S. KARLOVCI	331	30/10/18	25/09/19
116	Supervision of Works & Coordinator for safety and health at work PANCEVO	331	30/10/18	25/09/19
117	Supervision of Works & Coordinator for safety and health at work ZEMUN	331	30/10/18	25/09/19
118	Supervision of Works & Coordinator for safety and health at work TEMERIN	331	30/10/18	25/09/19
119	Supervision of Works & Coordinator for safety and health at work UB	302	10/08/18	07/06/19
120	Supervision of Works & Coordinator for safety and health at work MIONICA	302	10/08/18	07/06/19
121	Supervision of Works & Coordinator for safety and health at work LOZNICA	333	10/08/18	08/07/19
122	Supervision of Works & Coordinator for safety and health at work KRUPANJ	333	10/08/18	08/07/19
123	Tender procedure for Supervision of Works	89	21/06/18	17/08/18
124	TD Preparation and Approval (incl. CEB No-Objection)	9	21/06/18	28/06/18
125	TD Launch (incl. start date of launch, and date of evaluation, CEB No-Ob)	74	29/06/18	10/09/18
126	Contract Signature	1	17/09/18	17/09/18
127	Supervision of Works & Coordinator for safety and health at work KIRINDA	331	30/10/18	25/09/19
128	Supervision of Works & Coordinator for safety and health at work B. PETROVAC	331	30/10/18	25/09/19
129	Supervision of Works & Coordinator for safety and health at work B. PALANKA	331	30/10/18	25/09/19
130	Supervision of Works & Coordinator for safety and health at work S. MITROVICA	331	30/10/18	25/09/19
131	Supervision of Works & Coordinator for safety and health at work N. PAZAR	331	30/10/18	25/09/19
132	Supervision of Works & Coordinator for safety and health at work LUCANI	331	30/10/18	25/09/19
133	Supervision of Works & Coordinator for safety and health at work SVILJANA	302	17/09/18	15/07/19
134	Supervision of Works & Coordinator for safety and health at work ZABAR	302	17/09/18	15/07/19
135	Supervision of Works & Coordinator for safety and health at work M. CRNIĆ	302	17/09/18	15/07/19
136	Supervision of Works & Coordinator for safety and health at work ROZAR	302	17/09/18	15/07/19
137	PROJECT CLOSEOUT			
138	PROJECT CLOSEOUT ACTUAL	276	03/04/19	20/12/20
139	Tender procedure for Technical Inspection	66	10/07/18	05/04/19
140	TD Preparation and Approval (incl. CEB No-Objection)	15	10/07/18	24/07/18
141	TD Launch (incl. start date of launch, and date of evaluation, CEB No-Ob)	81	31/07/18	07/04/19
142	Contract Signature	1	05/04/19	05/04/19
143	Technical Inspection and Occupancy Permit	183	06/05/19	04/11/19
144	Final Project Closeout and Acceptance by CEB	2	04/11/19	06/11/19



RHP: CHP SERBIA - SRB 5.1.1 - CONSTRUCTION OF 270 APARTMENTS IN KAMENDIN, CITY OF BELGRADE  
 - BASELINE AND ACTUAL SCHEDULE -

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP: SRB 5.1.1 OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	145	03/09/14	27/10/17
7	ACTUAL	1337	14/08/15	17/04/19
8	GRANT AGREEMENT (GA) SIGNING	0	14/08/15	14/08/15
9	SCR-PIU-LSG AGREEMENT SIGNING	0	28/09/15	28/09/15
10	BENEFICIARY SELECTION			
11	BENEFICIARY SELECTION / Baseline	182	29/09/15	28/03/16
16	BENEFICIARY SELECTION / Actual	724	15/12/15	07/12/17
17	Public Call/Announcement for Beneficiary Selection	31	15/12/15	14/01/16
18	Application Period	32	15/01/16	15/02/16
19	Processing of applications and publishing of preliminary list of beneficiaries	378	16/02/16	27/02/17
20	Appeal process and the final selection of beneficiaries	284	27/02/17	07/12/17
21	DESIGN & REVIEW SERVICES (City of Belgrade)			
22	DESIGN / Baseline	183	01/12/15	16/05/16
25	DESIGN / Actual (City of Belgrade)	416	16/11/15	04/01/17
31				
32	REVIEW OF DESIGN / Baseline	37	09/03/16	05/03/16
35	REVIEW OF DESIGN / Actual (City of Belgrade)	412	20/11/15	08/01/17
41				
42	CONSTRUCTION WORKS & SUPERVISION SERVICE			
43	CONSTRUCTION WORKS / Baseline	471	05/03/16	19/09/17
46	CONSTRUCTION WORKS / Actual	682	27/03/17	05/02/19
47	Tender procedure for Construction works (PIU)	185	27/03/17	28/09/17
48	TD Preparation and Approval (incl. CEB No-Objection)	73	27/03/17	07/06/17
49	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	89	16/06/17	12/09/17
50	Contract Signature	0	28/09/17	28/09/17
51	Construction Works	451	13/11/17	05/02/19
52	SUPERVISION SERVICE / Baseline	265	05/03/16	13/05/17
55	SUPERVISION SERVICE / Actual (City of Belgrade)	451	13/11/17	05/02/19
56	Supervision of Works & HS Coordinator (external task)	451	13/11/17	05/02/19
57	PROJECT CLOSEOUT			
58	PROJECT CLOSEOUT / Baseline	134	17/02/17	27/10/17
61	PROJECT CLOSEOUT / Actual (City of Belgrade)	64	07/02/19	17/04/19
62	Technical Inspection and Occupancy Permit (external task)	64	07/02/19	11/04/19

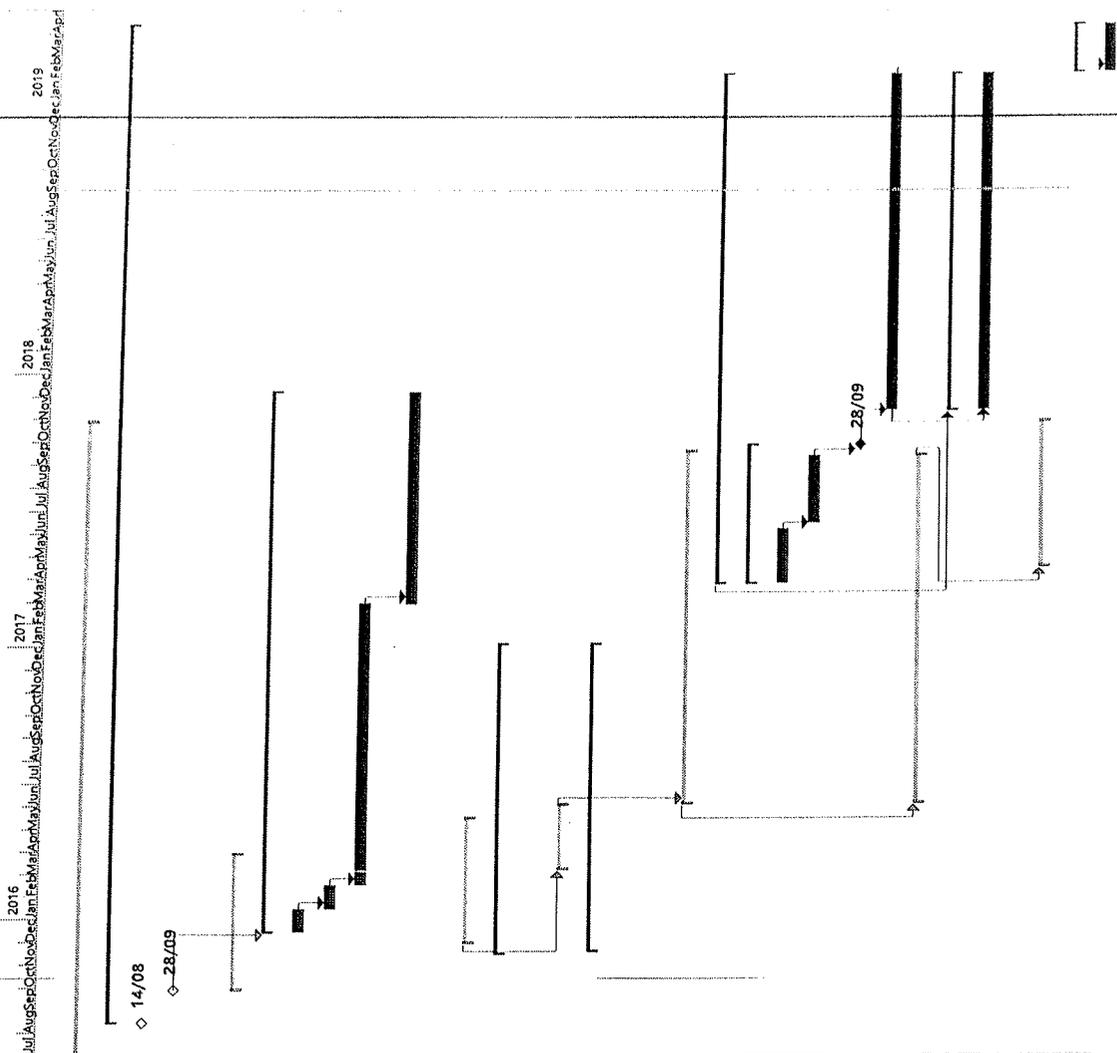

Project: SRB 5.1.1  
 C1.1 - MultiApts Buildings  
 270 Apts.-Kamendin, City of BG  
 Date: 3/9/2018

Actual Task Timeframe  
 Grant Agreement Signing


Estimated Project Activities Summary  
 Actual Project Activities Summary

Progress  
 Group of Activities

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

RHP: CHP SERBIA - SRB 5.1.2 - CONSTRUCTION OF 165 APARTMENTS IN MUNICIPALITY OF STARA PAZOVA  
- BASELINE AND ACTUAL SCHEDULE -

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 5.1.2 OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	1075	09/09/14	18/08/17
6	ACTUAL	1420	14/08/15	03/07/19
7	GRANT AGREEMENT (GA) SIGNING	0	14/08/15	14/08/15
8	SCR-PIU-LSG AGREEMENT SIGNING	0	28/09/15	28/09/15
9	BENEFICIARY SELECTION			
10	BENEFICIARY SELECTION - Baseline	162	29/09/15	28/03/16
15	BENEFICIARY SELECTION / Actual	183	15/12/15	14/06/16
16	Public Call/Announcement for Beneficiary Selection			
17	Application Period	30	15/12/15	13/01/16
18	Processing of applications and publishing of preliminary list of beneficiaries	32	15/01/16	15/02/16
19	Appeal process and the final selection of beneficiaries	30	16/02/16	16/03/16
20	CONSTRUCTION WORKS & SUPERVISION SERVICE			
21	CONSTRUCTION WORKS / Baseline	442	15/02/16	07/05/17
24	CONSTRUCTION WORKS / Actual	582	27/11/17	01/07/19
25	Tender procedure for Construction works	197	27/11/17	11/06/18
26	TD Preparation and Approval (incl. CEB No-Objection)	47	27/11/17	12/01/18
27	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	106	15/01/18	30/04/18
28	Contract Signature	1	11/06/18	11/06/18
29	Construction Works	333	03/08/18	01/07/19
30	SUPERVISION SERVICE / Baseline	428	16/02/16	17/03/17
33	SUPERVISION SERVICE / Actual	572	07/12/17	01/07/19
34	Tender procedure for Supervision of works	132	07/12/17	17/04/18
35	TD Preparation and Approval (incl. CEB No-Objection)	2	07/12/17	08/12/17
36	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	91	08/12/17	08/03/18
37	Contract Signature	1	17/04/18	17/04/18
38	Supervision of Works & Coordinator for safety and health at work	333	03/08/18	01/07/19
39	PROJECT CLOSEOUT			
40	PROJECT CLOSEOUT / Baseline	247	15/12/16	18/08/17
45	PROJECT CLOSEOUT / Actual	175	10/07/19	03/07/19
46	Tender Procedure for Technical Inspection	41	10/07/19	19/02/19
47	TD Preparation and Approval (incl. CEB No-Objection)	6	10/07/19	15/01/19
48	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	28	15/01/19	11/02/19
49	Contract Signature	1	19/02/19	19/02/19
50	Technical Inspection and Occupancy Permit	120	06/03/19	03/07/19

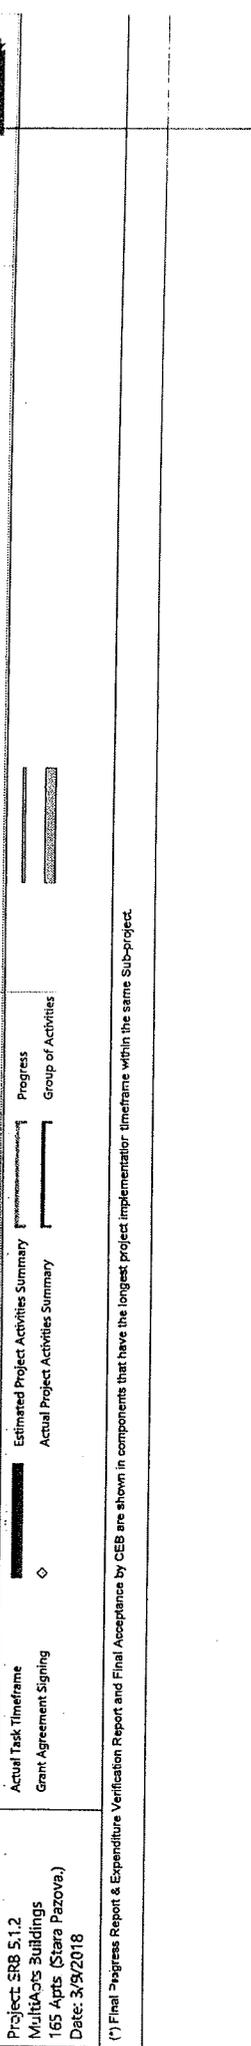

Project: SRB 5.1.2  
 Multi-apartment Buildings  
 165 Apts (Stara Pazova)  
 Date: 3/9/2018


Actual Task Timeframe  
 Grant Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Progress  
 Group of Activities

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same sub-project.

**RHP: CHP SERBIA - SRB 5.2 - PROVISION OF 200 BUILDING MATERIAL PACKAGES - BASELINE & ACTUAL SCHEDULE -**

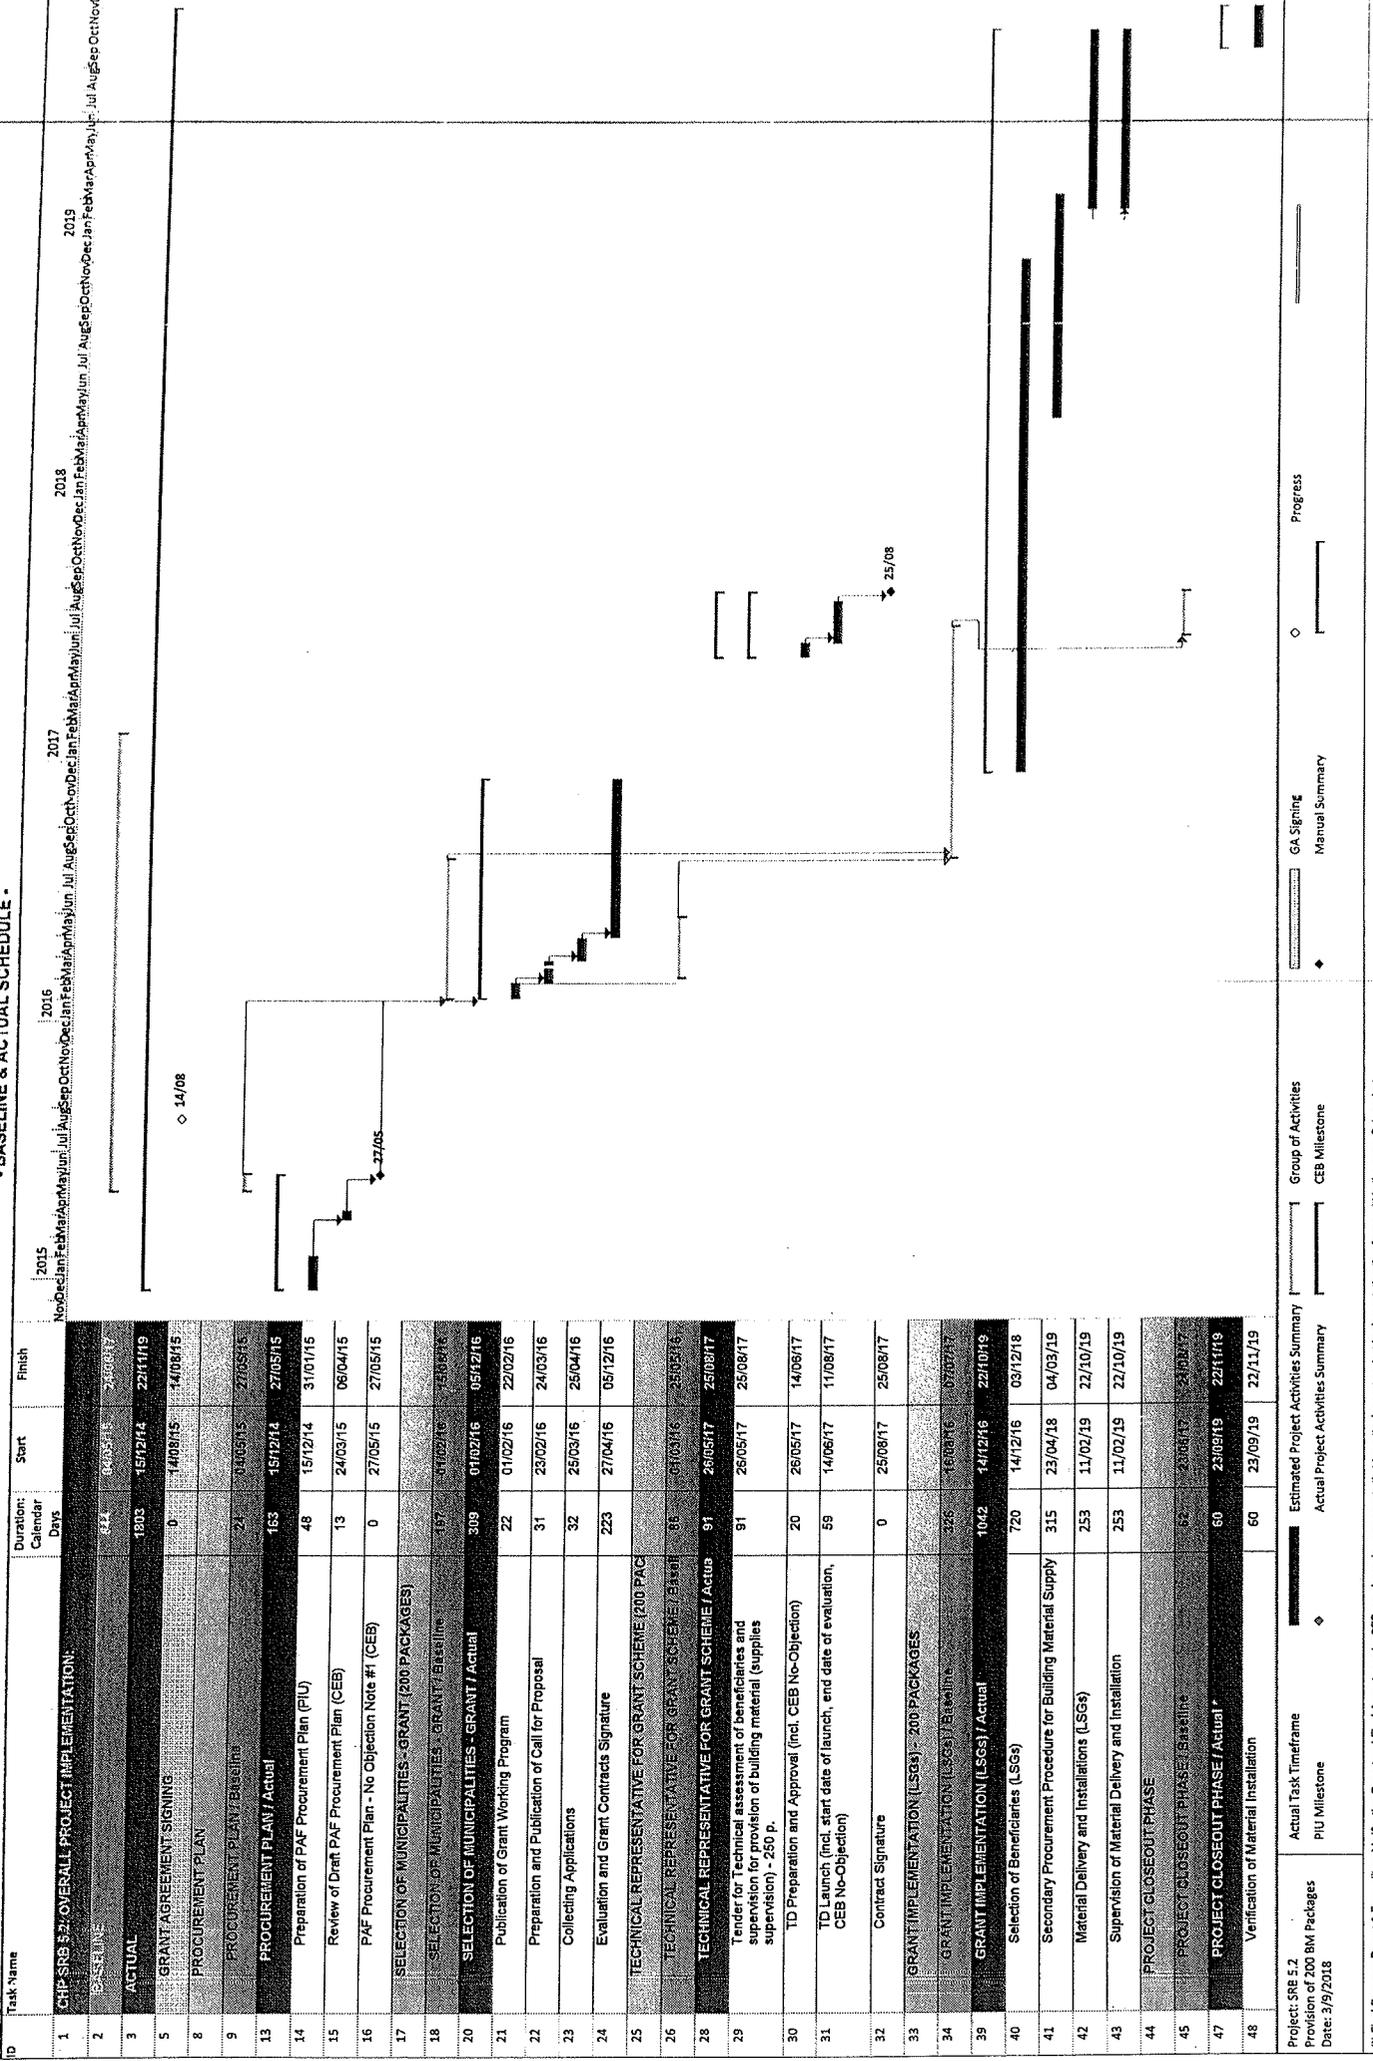


ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 5.2-OVERALL PROJECT IMPLEMENTATION	444	04/05/17	25/08/19
2	BASELINE	1803	15/12/14	22/11/19
3	ACTUAL	0	14/08/15	14/08/15
5	GRANT AGREEMENT SIGNING	21	31/05/15	27/05/15
8	PROCUREMENT PLAN	163	15/12/14	27/05/15
9	PROCUREMENT PLAN / Baseline	48	15/12/14	31/01/15
13	PROCUREMENT PLAN / Actual	13	24/03/15	06/04/15
14	Preparation of PAF Procurement Plan (PIU)	0	27/05/15	27/05/15
15	Review of Draft PAF Procurement Plan (CEB)			
16	PAF Procurement Plan - No Objection Note #1 (CEB)			
17	SELECTION OF MUNICIPALITIES - GRANT (200 PACKAGES)			
18	SELECTION OF MUNICIPALITIES - GRANT / Baseline	157	07/02/16	23/08/16
20	SELECTION OF MUNICIPALITIES - GRANT / Actual	309	01/02/16	05/12/16
21	Publication of Grant Working Program	22	01/02/16	22/02/16
22	Preparation and Publication of Call for Proposal	31	23/02/16	24/03/16
23	Collecting Applications	32	25/03/16	25/04/16
24	Evaluation and Grant Contracts Signature	223	27/04/16	05/12/16
25	TECHNICAL REPRESENTATIVE FOR GRANT SCHEME (200 PAC)			
26	TECHNICAL REPRESENTATIVE FOR GRANT SCHEME / Baseline	65	01/03/16	25/03/16
28	TECHNICAL REPRESENTATIVE FOR GRANT SCHEME / Actual	91	28/03/17	25/08/17
29	Tender for Technical assessment of beneficiaries and supervision for provision of building material (supplies supervision) - 250 p.	81	28/03/17	25/08/17
30	TD Preparation and Approval (incl. CEB No-Objection)	20	26/05/17	14/06/17
31	TD Launch (incl. start date of launch, end date of evaluation, CEB No-Objection)	59	14/06/17	11/08/17
32	Contract Signature	0	25/08/17	25/08/17
33	GRANT IMPLEMENTATION (LSGs) - 200 PACKAGES			
34	GRANT IMPLEMENTATION (LSGs) / Baseline	125	14/08/16	07/07/17
39	GRANT IMPLEMENTATION (LSGs) / Actual	1042	14/12/16	22/10/19
40	Selection of Beneficiaries (LSGs)	720	14/12/16	03/12/18
41	Secondary Procurement Procedure for Building Material Supply	315	23/04/18	04/03/19
42	Material Delivery and Installations (LSGs)	253	11/02/19	22/10/19
43	Supervision of Material Delivery and Installation	253	11/02/19	22/10/19
44	PROJECT CLOSEOUT PHASE			
45	PROJECT CLOSEOUT PHASE / Baseline	60	23/09/19	22/11/19
47	PROJECT CLOSEOUT PHASE / Actual	60	23/09/19	22/11/19
48	Verification of Material Installation	60	23/09/19	22/11/19

Project: SRB 5.2 Provision of 200 BM Packages  
 Date: 3/9/2018  
 Estimated Project Activities Summary  
 Actual Project Activities Summary  
 Group of Activities  
 CEB Milestone  
 GA Signing  
 Manual Summary  
 Progress

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

RHP: CHP SERBIA - SRB 5.3 - PROVISION OF 241 VILLAGE HOUSES (+ 139 VH Nat. Contrib.)  
 - BASELINE & ACTUAL SCHEDULE.

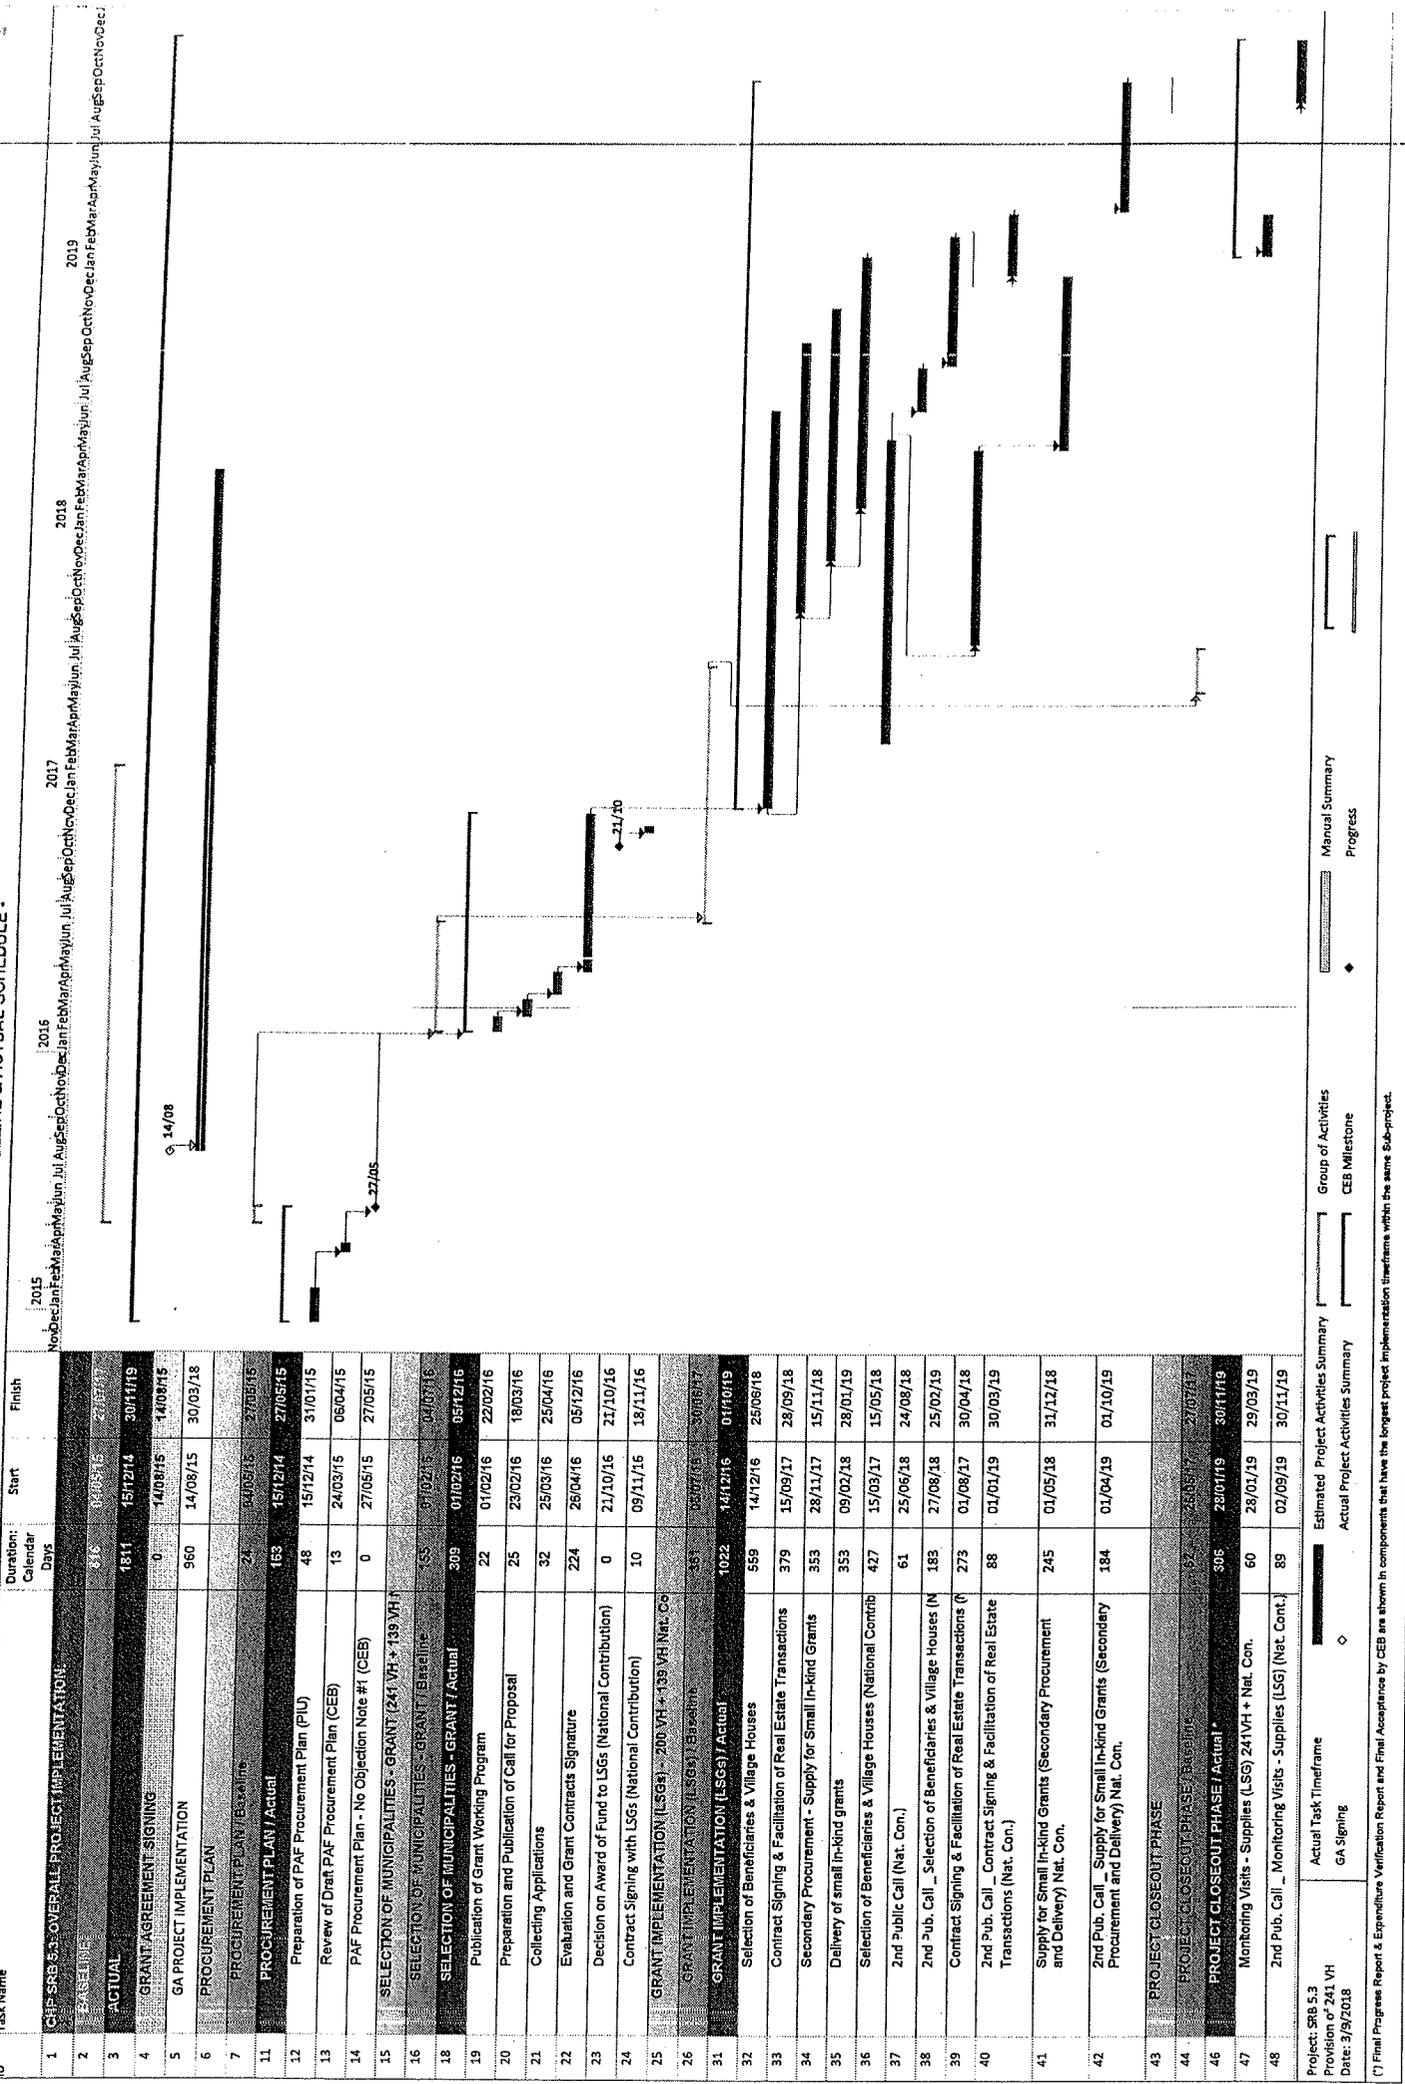

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP SRB 5.3 - OVERALL PROJECT IMPLEMENTATION	516	15/12/14	30/11/19
2	BASELINE	0	14/08/15	14/08/15
3	ACTUAL	960	14/08/15	30/03/18
4	GRANT AGREEMENT SIGNING	24	15/12/14	27/05/15
5	GA PROJECT IMPLEMENTATION	48	15/12/14	31/01/15
6	PROCUREMENT PLAN	13	24/03/15	06/04/15
7	PROUREMENT PLAN / Actual	0	27/05/15	27/05/15
8	PROUREMENT PLAN / Baseline	309	01/02/16	05/12/16
9	Preparation of PAF Procurement Plan (PIU)	22	01/02/16	22/02/16
10	Review of Draft PAF Procurement Plan (CEB)	25	23/02/16	18/03/16
11	PAF Procurement Plan - No Objection Note #1 (CEB)	32	25/03/16	25/04/16
12	PAF Procurement Plan - No Objection Note #2 (CEB)	224	28/04/16	05/12/16
13	Decision on Award of Fund to LSGs (National Contribution)	0	21/10/16	21/10/16
14	Contract Signing with LSGs (National Contribution)	10	09/11/16	18/11/16
15	GRANT IMPLEMENTATION (LSGs) - 200 VH + 139 VH Nat. Con.	15	09/11/16	24/06/17
16	GRANT IMPLEMENTATION (LSGs) - Baseline	1022	14/12/16	01/10/19
17	GRANT IMPLEMENTATION (LSGs) / Actual	559	14/12/16	25/06/18
18	Selection of Beneficiaries & Village Houses	379	15/09/17	28/09/18
19	Contract Signing & Facilitation of Real Estate Transactions	353	28/11/17	15/11/18
20	Secondary Procurement - Supply for Small In-kind Grants	353	09/02/18	28/01/19
21	Delivery of small in-kind grants	427	15/03/17	15/05/18
22	Selection of Beneficiaries & Village Houses (National Contrib)	61	25/06/18	24/08/18
23	2nd Public Call (Nat. Con.)	183	27/08/18	25/02/19
24	2nd Pub. Call - Selection of Beneficiaries & Village Houses (N	273	01/08/17	30/04/18
25	Contract Signing & Facilitation of Real Estate Transactions (P	88	01/04/19	30/03/19
26	2nd Pub. Call - Contract Signing & Facilitation of Real Estate Transactions (Nat. Con.)	245	01/05/18	31/12/18
27	Supply for Small In-kind Grants (Secondary Procurement and Delivery) Nat. Con.	184	01/04/19	01/10/19
28	2nd Pub. Call - Supply for Small In-kind Grants (Secondary Procurement and Delivery) Nat. Con.	306	28/01/19	29/03/19
29	PROJECT CLOSURE PHASE	89	02/09/19	30/11/19
30	Monitoring Visits - Supplies (LSG) 241VH + Nat. Con.	60	28/01/19	29/03/19
31	2nd Pub. Call - Monitoring Visits - Supplies (LSG) (Nat. Con.)	89	02/09/19	30/11/19

Project: SRB 5.3  
 Provision of 241 VH  
 Date: 3/9/2018

Actual Task timeframe  
 GA signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Group of Activities  
 CEB Milestone

Manual Summary  
 Progress

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA - SRB 7.1 - PURCHASE OF 130 APARTMENTS  
- BASELINE AND ACTUAL SCHEDULE -**


ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB7.1 OVERALL PROJECT IMPLEMENTATION	297	02/10/17	02/11/18
2	BASELINE	697	02/10/17	02/11/18
3	ACTUAL	687	02/10/17	19/08/19
4	GRANT AGREEMENT (GA) AMENDMENT SIGNING	1	02/10/17	02/10/17
5	PREPARATORY ACTIVITIES			
6	PREPARATORY ACTIVITIES / Baseline	30	03/10/17	07/11/17
8	PREPARATORY ACTIVITIES / Actual	31	30/01/18	01/03/18
9	Preparatory activities	31	30/01/18	01/03/18
10	BENEFICIARY SELECTION			
11	BENEFICIARY SELECTION / Baseline	33	02/11/17	04/12/17
13	BENEFICIARY SELECTION / Actual	211	02/03/18	28/09/18
14	Verification of Beneficiary List (UNHCR and OSCE)	211	02/03/18	28/09/18
15	PURCHASE			
16	PURCHASE / Baseline	303	05/12/17	03/10/18
18	PURCHASE / Actual	329	03/07/18	27/05/19
19	Tender procedure for Services of Independent Appraisers	65	03/07/18	05/09/18
20	TD Preparation and Approval (Including CEB No-Objection)	2	03/07/18	04/07/18
21	TD Launch (incl. start date of launch, end date of evaluation, C	48	05/07/18	21/08/18
22	Contract signature	1	05/09/18	05/09/18
23	Independent Appraising Services	90	06/09/18	04/12/18
24	Selection of apartments in competitive process	142	01/10/18	19/02/19
25	Govt Decision on purchase of apartments	59	20/02/19	19/04/19
26	Award of apartments to beneficiaries	36	22/04/19	27/05/19
27	PROJECT CLOSEOUT			
28	PROJECT CLOSEOUT / Baseline	30	04/10/18	02/11/18
30	PROJECT CLOSEOUT / Actual	84	28/05/19	19/08/19
31	Final Progress Report and Verification of Costs	42	28/05/19	08/07/19
32	CEB Acceptance of Progress Report	42	09/07/19	19/08/19



Project: SRB7.1	Actual Task Timeframe	Progress
Purchase of 130 Apartments	Grant Agreement Signing	Group of Activities
Date: 14/9/2018	Estimated Project Activities Summary	
	Actual Project Activities Summary	

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA - SRB 7.2 -PURCHASING OF 180 VILLAGE HOUSES  
- BASELINE & ACTUAL SCHEDULE .**

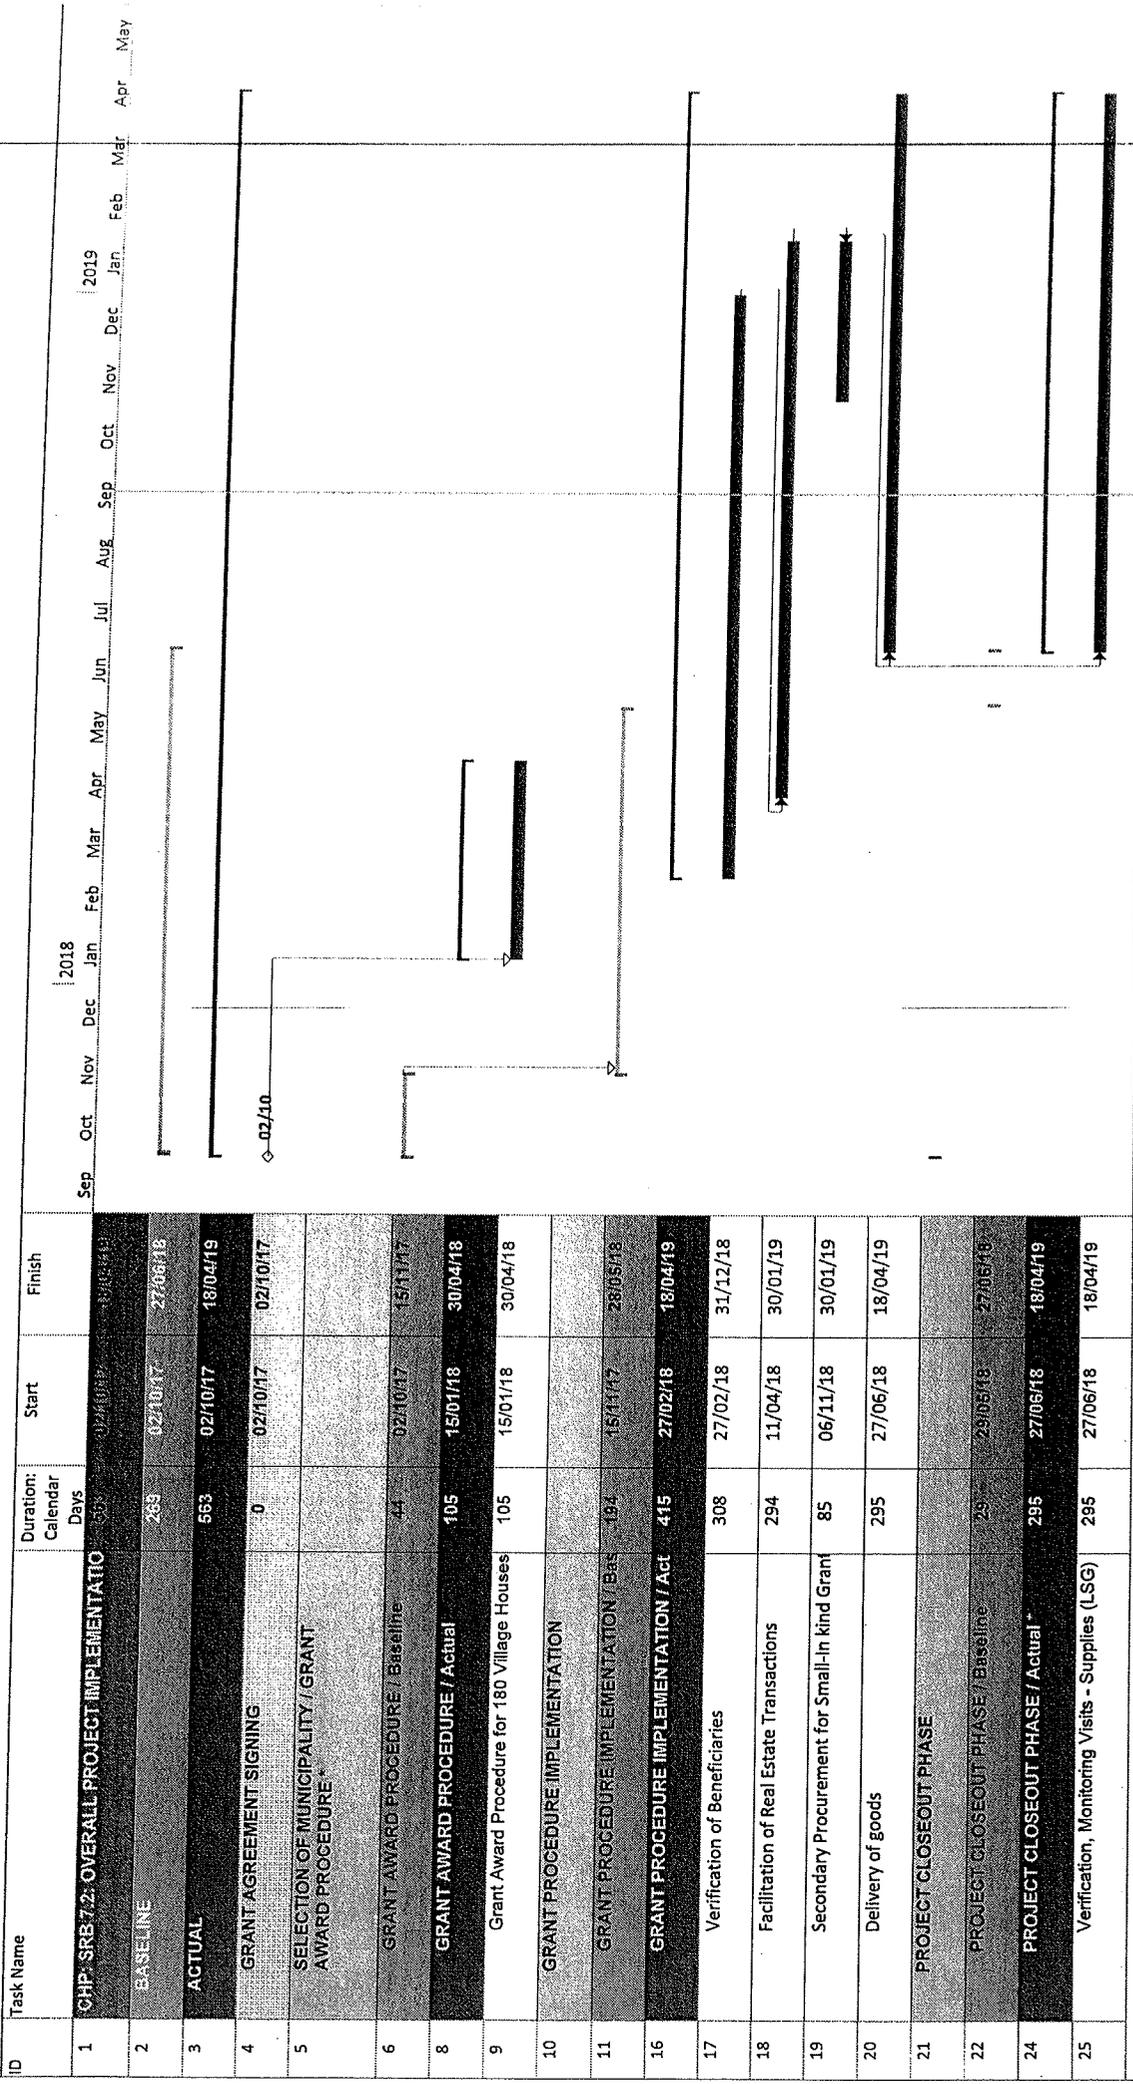

Project: SRB 7.2  
Purchasing of 180 VH  
Date: 14/9/2018


Actual Task Timeframe  
Grant Agreement Signing

Estimated Project Activities Summary  
Actual Project Activities Summary  
Group of Activities  
Progress

(\* ) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA - SRB 7.3 - PROVISION OF 180 PACKAGES OF BUILDING MATERIAL  
- BASELINE AND ACTUAL SCHEDULE -**


ID	Task Name	Duration: Calendar Days	Start	Finish
1	<b>CHP: SRB 7.3 OVERALL PROJECT IMPLEMENTATION</b>	321	02/10/17	08/02/20
2	<b>BASELINE</b>	505	02/10/17	22/02/19
3	<b>ACTUAL</b>	870	02/10/17	18/02/20
4	<b>GRANT AGREEMENT (GA) SIGNING</b>	0	02/10/17	02/10/17
5	<b>BENEFICIARY SELECTION</b>			
6	<b>BENEFICIARY SELECTION / Baseline</b>	30	02/10/17	31/10/17
8	<b>BENEFICIARY SELECTION / Actual</b>	28	01/02/18	28/02/18
9	Verification of Beneficiaries	28	01/02/18	28/02/18
10	<b>MATERIAL DELIVERY &amp; INSTALLATIONS SUPERVISION</b>			
11	<b>MATERIAL DELIVERY &amp; INSTALLATIONS SUPERVISION / Baseline</b>	449	01/11/17	23/01/19
14	<b>MATERIAL DELIVERY &amp; INSTALLATIONS, SUPERVISION/ Actual</b>	748	01/02/18	18/02/20
15	Preparation of BoQs for 347 beneficiaries	149	01/02/18	29/06/18
16	Tender Procedure for Technical Representative	98	19/10/18	24/01/19
17	TD Preparation and Approval (incl. CEB No-Objection)	8	19/10/18	26/10/18
18	TD Launch (from tender launch to EVR No-objection)	73	29/10/18	09/01/19
19	Contract Signature	1	24/01/19	24/01/19
20	Provision of Services of Technical Representative	359	25/02/19	18/02/20
21	Tender Procedure for Building Material Supply	113	19/10/18	08/02/19
22	TD Preparation and Approval (incl. CEB No-Objection)	11	19/10/18	29/10/18
23	TD Launch (from tender launch to EVR No-objection)	81	05/11/18	24/01/19
24	Contract Signature	1	08/02/19	08/02/19
25	Delivery of building material 1	32	11/03/19	11/04/19
26	Installation of building material 1 (Final Beneficiaries)	135	11/03/19	23/07/19
27	Delivery of building material 2	34	24/07/19	26/08/19
28	Installation of building material 2 (Final Beneficiaries)	135	24/07/19	05/12/19
29	<b>PROJECT CLOSEOUT</b>			
30	<b>PROJECT CLOSEOUT / Baseline</b>	30	24/01/19	23/02/19
32	<b>PROJECT CLOSEOUT / Actual</b>	30	09/12/19	07/01/20
33	Verification of Material Installation	30	09/12/19	07/01/20

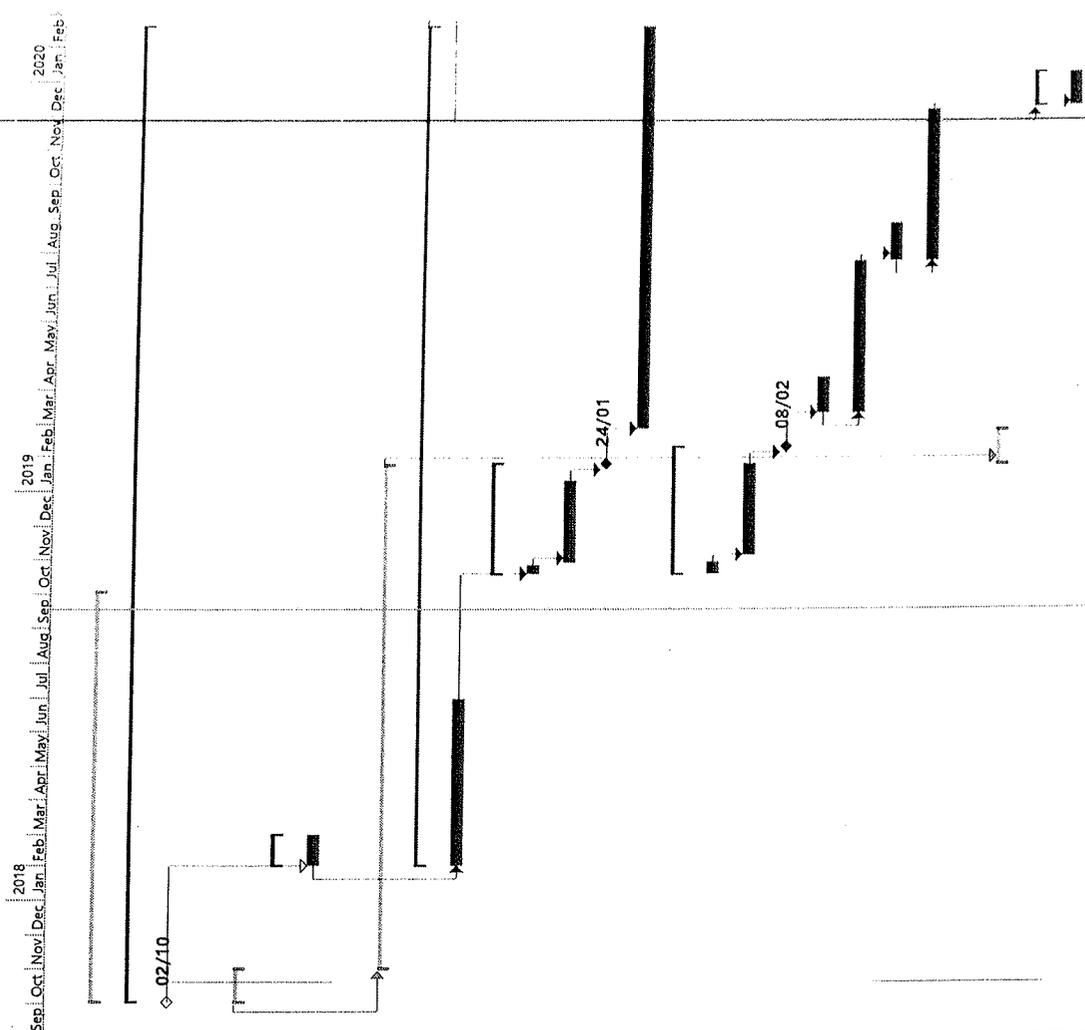

Project: SRB 7.3 Provision of 180 BM Date: 14/9/2018	Actual Task Timeframe Grant Agreement Signing	Estimated Project Activities Summary	Progress
	Actual Project Activities Summary	Group of Activities	

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

RHP: CHP SERBIA - SRB 7.4 - DESIGN SERVICES FOR 358 APARTMENTS AND ADDITIONAL 350 APARTMENTS - BASELINE AND ACTUAL SCHEDULE -

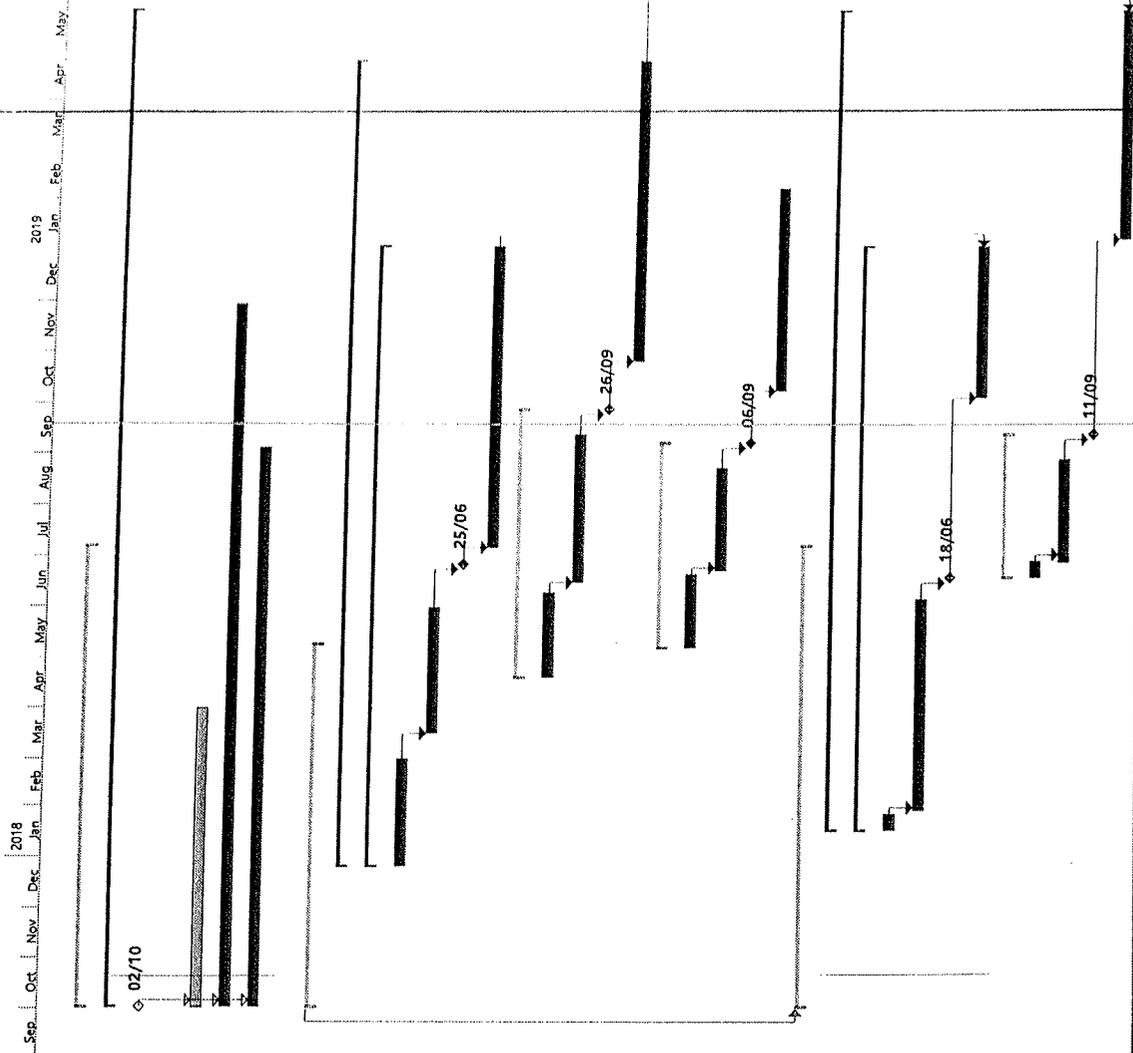

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 7.4 OVERALL PROJECT IMPLEMENTATION			
2	BASELINE	376	02/10/17	06/07/18
3	ACTUAL	600	02/10/17	24/05/19
4	GRANT AGREEMENT (GA) SIGNING	0	02/10/17	02/10/17
5	BENEFICIARY SELECTION	423	02/10/17	28/11/18
6	BENEFICIARY SELECTION (358+350) / Baseline	180	02/10/17	30/03/18
7	BENEFICIARY SELECTION (358) / Actual	423	02/10/17	28/11/18
8	BENEFICIARY SELECTION (350) / Actual	337	02/10/17	03/09/18
9	DESIGN & REVIEW SERVICES (358+350) APARTMENTS			
10	DESIGN / Baseline	219	02/10/17	03/05/18
13	DESIGN / Actual	495	28/12/17	24/04/19
14	Tender procedure for Design service (358 apartments)	373	26/12/17	02/01/19
15	TD Preparation and Approval (incl. CEB No-Objection)	65	26/12/17	28/02/18
16	TD Launch (from tender launch to EVR No-Objection)	76	16/03/18	30/05/18
17	Contract Signature (358)	1	25/06/18	25/06/18
18	Design service (358)	181	06/07/18	02/01/19
19	Tender procedure for Design service (217 apartments)	161	19/04/18	26/09/18
20	TD Preparation and Approval (incl. CEB No-Objection)	51	19/04/18	08/06/18
21	TD Launch (from tender launch to EVR No-Objection)	89	15/06/18	11/09/18
22	Contract Signature (217)	1	26/09/18	26/09/18
23	Design service (217)	181	26/10/18	24/04/19
24	Tender procedure for Design service (133 apartments)	123	07/05/18	06/09/18
25	TD Preparation and Approval (incl. CEB No-Objection)	44	07/05/18	19/06/18
26	TD Launch (from tender launch to EVR No-Objection)	62	22/06/18	22/08/18
27	Contract Signature (133)	1	06/09/18	06/09/18
28	Design service (133)	122	08/10/18	06/02/19
29	REVIEW OF DESIGN / Baseline	279	02/10/17	06/07/18
32	REVIEW OF DESIGN / Actual	493	17/01/18	24/05/19
33	Tender procedure for Review of Design (358 apartments)	351	17/01/18	02/01/19
34	TD Preparation and Approval (incl. CEB No-Objection)	10	17/01/18	26/01/18
35	TD Launch (from tender launch to EVR No-Objection)	127	29/01/18	04/06/18
36	Contract Signature (358)	0	18/06/18	18/06/18
37	Review of design (358)	91	04/10/18	02/01/19
38	Tender procedure for Review of Design (217 + 133 apartments)	86	18/06/18	11/09/18
39	TD Preparation and Approval (incl. CEB No-Objection)	10	18/06/18	27/06/18
40	TD Launch (from tender launch to EVR No-Objection)	62	27/06/18	27/08/18
41	Contract Signature (217 + 133)	1	11/09/18	11/09/18
42	Review of design (217 + 133)	138	07/01/19	24/05/19


Project: SRB 7.4 Design Services for 358 Apts and Addit 350 Ap  
 Date: 14/9/2018

Legend:  
 Estimated Project Activities Summary  
 Actual Project Activities Summary  
 Progress  
 Group of Activities

(\*) Final Progress Report & Expenditure Verification Report and Final Acceptance by CEB are shown in components that have the longest project implementation timeframe within the same Sub-project.

**RHP: CHP SERBIA -  
SRB 8.1: CONSTRUCTION OF 358 APARTMENTS  
- BASELINE AND ACTUAL SCHEDULE -**


ID	Task Name	Duration Calendar Days	Start	Finish
1	CHP: SRB 8.1 OVERALL PROJECT IMPLEMENTATION	1122	01/01/18	26/01/21
2	BASELINE	1031	01/01/18	27/01/20
7	ACTUAL	1107	16/01/18	26/01/21
8	GRANT AGREEMENT (GA) SIGNING	1	31/03/18	31/01/18
9	SCR-PIU-LSG AGREEMENT SIGNING	1	23/03/18	23/03/18
10	PROCUREMENT PLAN			
11	PROCUREMENT PLAN / Baseline	7	16/01/18	01/02/18
15	PROCUREMENT PLAN / Actual	79	26/03/18	12/06/18
16	Preparation of PAF Procurement Plan (PIU)	67	26/03/18	31/05/18
17	Review of Draft PAF Procurement Plan (CEB)	11	01/06/18	11/06/18
18	PAF Procurement Plan - No Objection Note #1 (CEB)	1	12/06/18	12/06/18
19	CONSTRUCTION WORKS & SUPERVISION SERVICE	707	21/09/18	27/08/20
20	CONSTRUCTION WORKS / Baseline	694	21/09/18	06/05/20
26	CONSTRUCTION WORKS / Actual	574	01/02/19	27/08/20
27	Tender procedure for Construction works	124	01/02/19	04/06/19
28	TD Preparation and Approval (incl. CEB No-Objection)	15	01/02/19	15/02/19
29	TD Launch (from tender launch to CEB No-Objection)	188	22/02/19	20/05/19
30	Contract Signature	1	04/06/19	04/06/19
31	Construction Works	421	04/07/19	27/08/20
32	SUPERVISION SERVICE / Baseline	694	21/09/18	06/05/20
38	SUPERVISION SERVICE / Actual	574	01/02/19	27/08/20
39	Tender procedure for Supervision of works	124	01/02/19	04/06/19
40	TD Preparation and Approval (incl. CEB No-Objection)	15	01/02/19	15/02/19
41	TD Launch (from tender launch to CEB No-Objection)	188	22/02/19	20/05/19
42	Contract Signature	1	04/06/19	04/06/19
43	Supervision of Works & Coordinator H&S	421	04/07/19	27/08/20
44	PROJECT CLOSEOUT PHASE	407	17/12/19	26/01/21
45	PROJECT CLOSEOUT PHASE / Baseline	316	17/12/19	27/10/20
53	PROJECT CLOSEOUT PHASE / Actual	303	30/03/20	26/01/21
54	Tender Procedure for Technical Inspection	241	30/03/20	25/11/20
55	TD Preparation and Approval (incl. CEB No-Objection)	15	30/03/20	13/04/20
56	TD Launch (incl. start date of launch, end date of evaluation)	188	20/04/20	16/07/20
57	Contract Signature	1	31/07/20	31/07/20
58	Technical Inspection and Occupancy Permit	91	27/08/20	25/11/20
59	Final Progress Report and Expenditure Verification R30	30	26/11/20	25/12/20
60	Final Acceptance by CEB	30	28/12/20	26/01/21



Project: SRB8.1  
Construction of 358 Apts  
Date: 14/02/2018


Summary (baseline)

**RHP: CHP SERBIA -  
SRB 8.1.1: CONSTRUCTION OF 250 APARTMENTS\_OVCA  
- BASELINE AND ACTUAL SCHEDULE -**

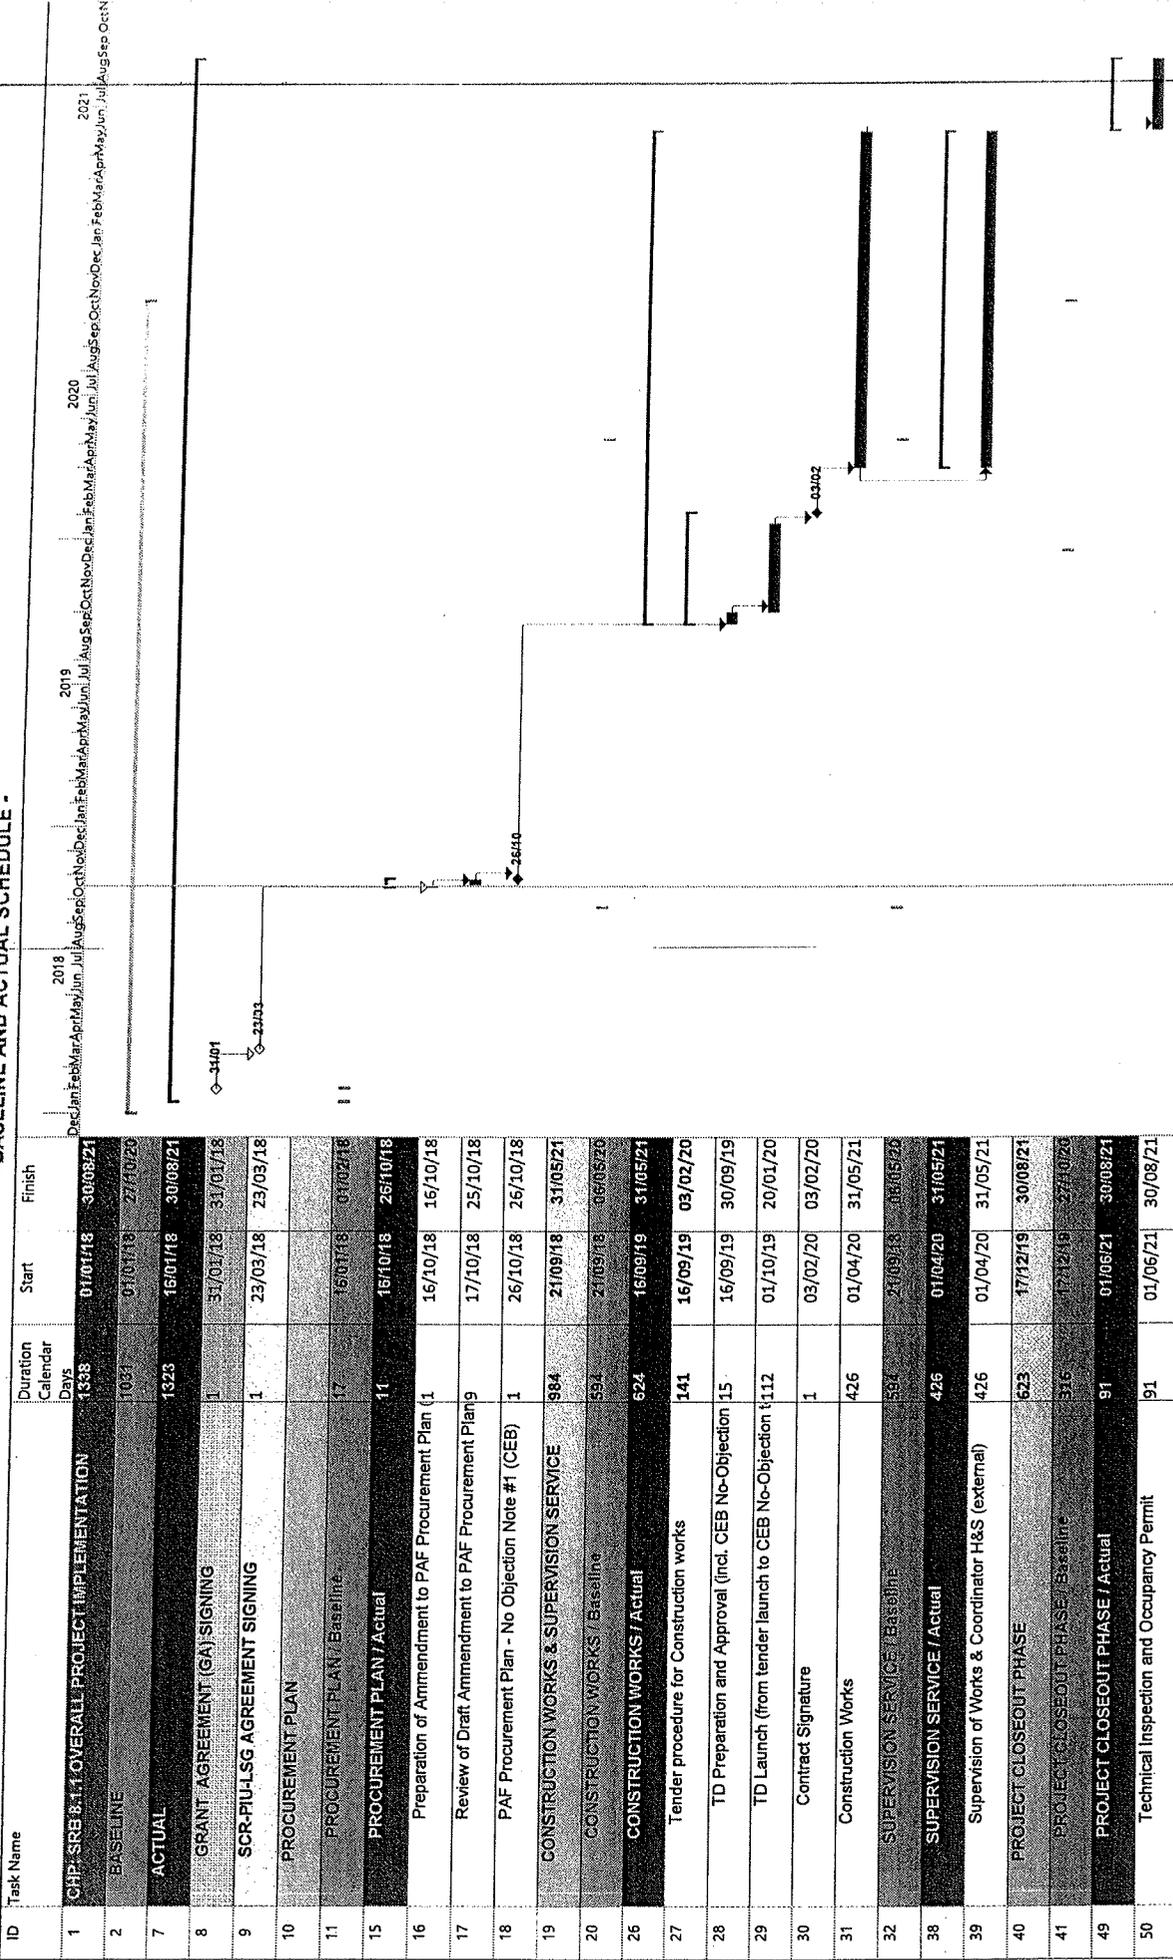


ID	Task Name	Duration Calendar Days	Start	Finish
1	CHP-SRB 8.1.1 OVERALL PROJECT IMPLEMENTATION	1338	01/01/18	30/08/21
2	BASELINE	1033	01/01/18	27/10/20
7	ACTUAL	1323	16/01/18	30/08/21
8	GRANT AGREEMENT (G) SIGNING	1	31/01/18	31/01/18
9	SCR-PIU-LSG AGREEMENT SIGNING	1	23/03/18	23/03/18
10	PROCUREMENT PLAN			
11	PROCUREMENT PLAN / Baseline	17	16/01/18	01/02/18
15	PROCUREMENT PLAN / Actual	11	16/10/18	26/10/18
16	Preparation of Amendment to PAF Procurement Plan (1)		16/10/18	16/10/18
17	Review of Draft Amendment to PAF Procurement Plan		17/10/18	25/10/18
18	PAF Procurement Plan - No Objection Note #1 (CEB)	1	26/10/18	26/10/18
19	CONSTRUCTION WORKS & SUPERVISION SERVICE	384	21/09/18	31/05/21
20	CONSTRUCTION WORKS / Baseline	394	21/09/18	06/05/20
26	CONSTRUCTION WORKS / Actual	324	16/09/19	31/05/21
27	Tender procedure for Construction works	141	16/09/19	03/02/20
28	TD Preparation and Approval (incl. CEB No-Objection)	15	16/09/19	30/09/19
29	TD Launch (from tender launch to CEB No-Objection)	112	01/10/19	20/01/20
30	Contract Signature	1	03/02/20	03/02/20
31	Construction Works	426	01/04/20	31/05/21
32	SUPERVISION SERVICE / Baseline	394	21/09/18	06/05/20
38	SUPERVISION SERVICE / Actual	426	01/04/20	31/05/21
39	Supervision of Works & Coordinator H&S (external)	426	01/04/20	31/05/21
40	PROJECT CLOSEOUT PHASE	623	17/12/19	30/08/21
41	PROJECT CLOSEOUT PHASE / Baseline	316	17/12/19	27/10/20
49	PROJECT CLOSEOUT PHASE / Actual	91	01/06/21	30/08/21
50	Technical Inspection and Occupancy Permit	91	01/06/21	30/08/21

**RHP: CHP SERBIA - SRB 8.2 - CONSTRUCTION OF 30 PRE-FAB HOUSES  
- BASELINE AND ACTUAL SCHEDULE -**

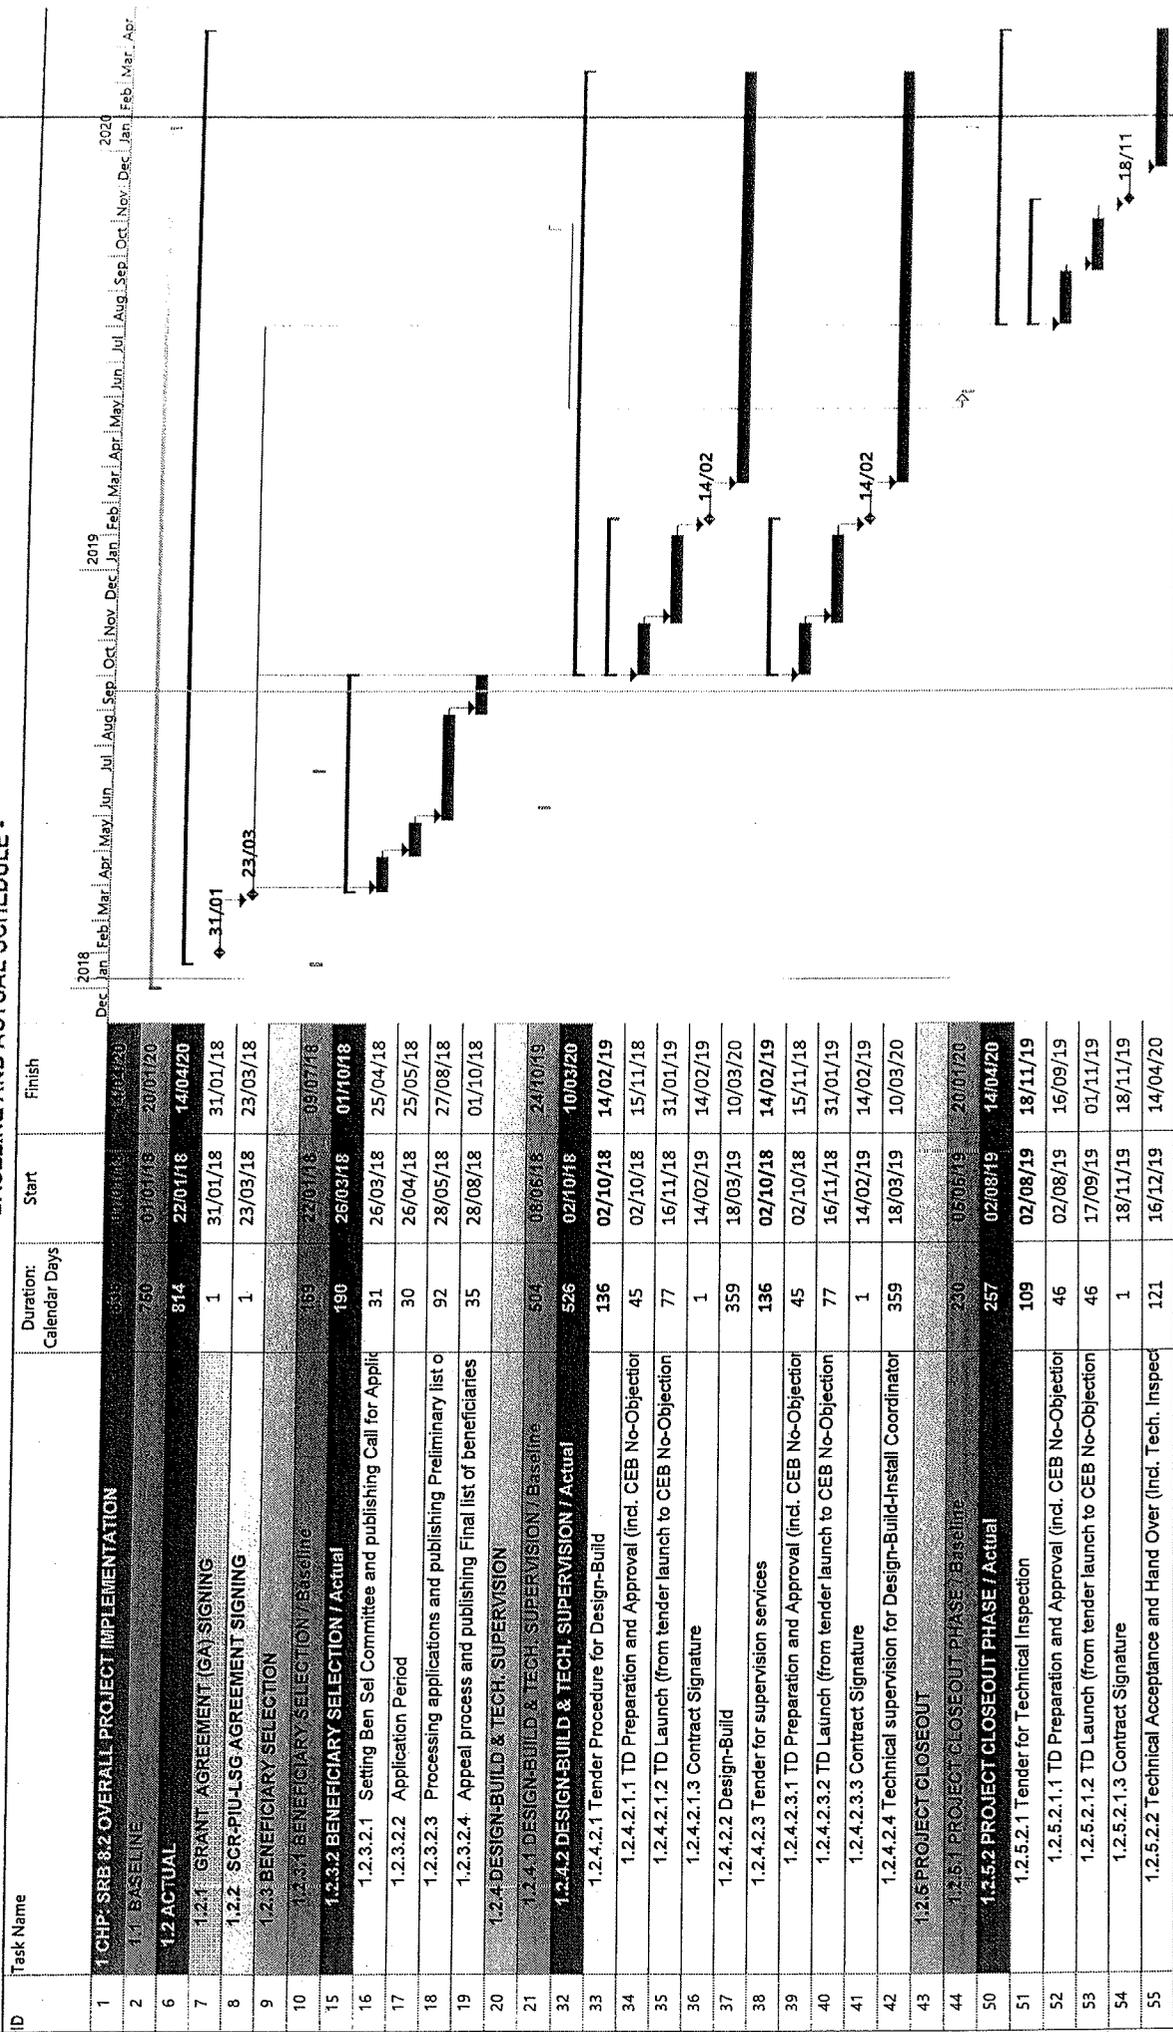

Task	Milestone	Summary (baseline)
Project: SRB 8.2 Provision of 30 P-e-Fab H. Date: 14/9/2018		

RHP: CHP SERBIA - SRB 8.3 - PROVISION OF 135 BUILDING MATERIAL PACKAGES (100 centralised + 35 decentralised) - BASELINE AND ACTUAL SCHEDULE.

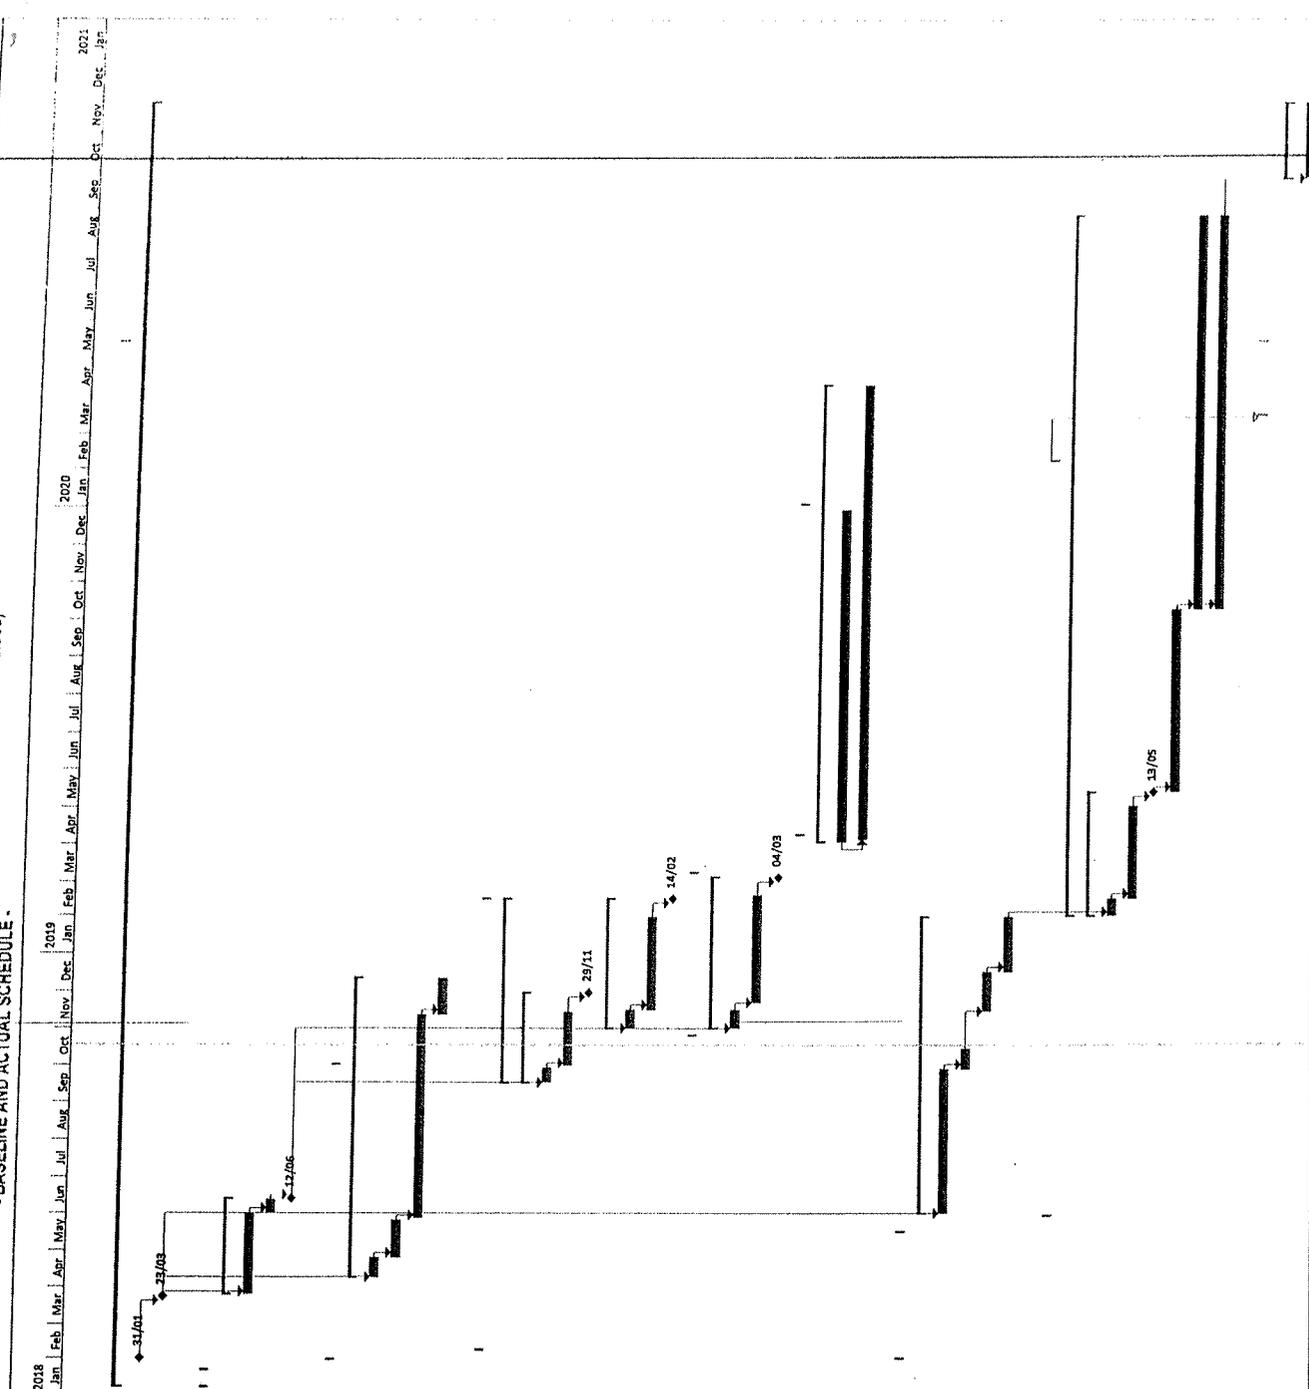

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP SRB 8.3 - OVERALL PROJECT IMPLEMENTATION	635	01/01/18	31/03/20
2	BASELINE	1053	03/01/18	26/11/20
6	ACTUAL			
7	GRANT AGREEMENT SIGNING	1	31/01/18	31/01/18
8	SCRIPULLS AGREEMENT SIGNING	1	23/03/18	23/03/18
9	PROCUREMENT PLAN	14	05/01/18	20/01/18
10	PROCUREMENT PLAN / Actual	79	26/03/18	12/06/18
14	Preparation of PAF Procurement Plan (PIU)	67	26/03/18	31/05/18
15	Review of Draft PAF Procurement Plan (CEB)	11	01/06/18	11/06/18
17	PAF Procurement Plan - No Objection Note #1 (CEB)	1	12/06/18	12/06/18
18	BENEFICIARY SELECTION 100 BM	24	01/07/18	25/07/18
19	BENEFICIARY SELECTION 35 BM / Actual	247	09/04/18	12/12/18
24	Setting the Ben Sel Committee and publishing call for applications	16	09/04/18	24/04/18
25	Application period	31	25/04/18	25/05/18
27	Processing Applications and publication of Preliminary List of Ben	168	28/05/18	12/11/18
28	Appeal procedure and publication of Final List of Beneficiaries	30	17/11/18	17/12/18
29	MATERIAL DELIVERY AND INSTALLATION - 100 BM via PIU	274	05/02/18	13/02/19
30	Tender Procedures for Technical Representatives / Baseline	151	17/09/18	14/02/19
39	Tender Procedures for Technical Representatives (a) / Actual	74	17/09/18	29/11/18
40	Tender Procedures for Technical Assessment / Actual	12	17/09/18	28/09/18
41	TD Preparation and Approval (incl. CEB No-Objection to TD)	44	01/10/18	14/11/18
42	TD Launch (from tender launch to CEB No-Objection to EvR)	1	29/11/18	29/11/18
43	Contract Signature	106	01/11/18	14/02/19
44	Tender Procedure for Supervision of Delivery and Instal / Actual	15	01/11/18	15/11/18
45	TD Preparation and Approval (incl. CEB No-Objection to TD)	76	16/11/18	30/01/19
46	TD Launch (from tender launch to CEB No-Objection to EvR)	1	14/02/19	14/02/19
47	Contract Signature	134	26/10/18	08/03/19
48	Tender Procedure for Supply of BM / Baseline	124	01/11/18	04/03/19
52	Tender Procedures for Supply of BM / Actual	15	01/11/18	15/11/18
53	TD Preparation and Approval (incl. CEB No-Objection to TD)	88	22/11/18	17/02/19
54	TD Launch (from tender launch to CEB No-Objection to EvR)	1	04/03/19	04/03/19
55	Contract Signature	270	08/04/18	03/01/20
56	Delivery and Installation 100 BM / Baseline	273	03/04/18	08/04/20
59	Delivery and Installation 100 BM / Actual	271	03/04/19	29/12/19
60	Material delivery and installation	371	04/04/19	09/04/20
61	Monitoring over Delivery and Installation	365	31/01/18	31/01/19
62	GRANT AWARD PROCEDURE - 35 BM via grants	108	31/01/18	16/05/18
63	GRANT AWARD PROCEDURE - 35 BM via grants / Baseline	244	01/08/18	31/01/19
64	GRANT AWARD PROCEDURE - 35 BM via grants / Actual	119	01/06/18	28/09/18
68	Verification of Final Beneficiaries (reserve lists earlier projects)	17	28/09/18	15/10/18
69	CEB No objection on award of direct grants to LSGs	32	15/11/18	17/12/18
70	Adoption of Decision on award of direct grants	45	17/12/18	31/01/19
71	Grant Contracts signature	619	30/09/18	07/02/20
72	GRANT SCHEME IMPLEMENTATION (LSGs)	572	01/02/19	26/03/20
73	GRANT SCHEME IMPLEMENTATION (LSGs) - 35 BM via grants / Actual	101	01/02/19	15/05/19
74	GRANT SCHEME IMPLEMENTATION (LSGs) - 35 BM via grants / Baseline	14	01/02/19	15/02/19
82	TD Launch (from tender launch to CEB No-Objection to EvR)	76	15/02/19	02/05/19
83	Contract Signature	1	13/05/19	13/05/19
84	Secondary Procurement Procedure for BM Supply (incl BoCs)	149	13/05/19	09/10/19
85	Material Delivery and Installation	322	09/10/19	26/08/20
86	Supervision of Material Delivery and Installation	235	16/03/20	26/11/20
87	PROJECT CLOSEOUT PHASE	62	25/09/20	26/11/20
88	PROJECT CLOSEOUT PHASE / Baseline	80	16/03/20	14/05/20
91	PROJECT CLOSEOUT PHASE / Actual	62	25/09/20	26/11/20
92	Verification of Material Installation			


Project: SRB 8.3  
 Provision of 135 BM Packages  
 Date: 10/10/2016

Actual Task Timeframe  
 Grant Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Group of Activities  
 Progress

RHP-CHP SERBIA - SRB 8.4 - PROVISION OF 79 VILLAGE HOUSES (50 centralised + 29 decentralised) - BASELINE AND ACTUAL SCHEDULE

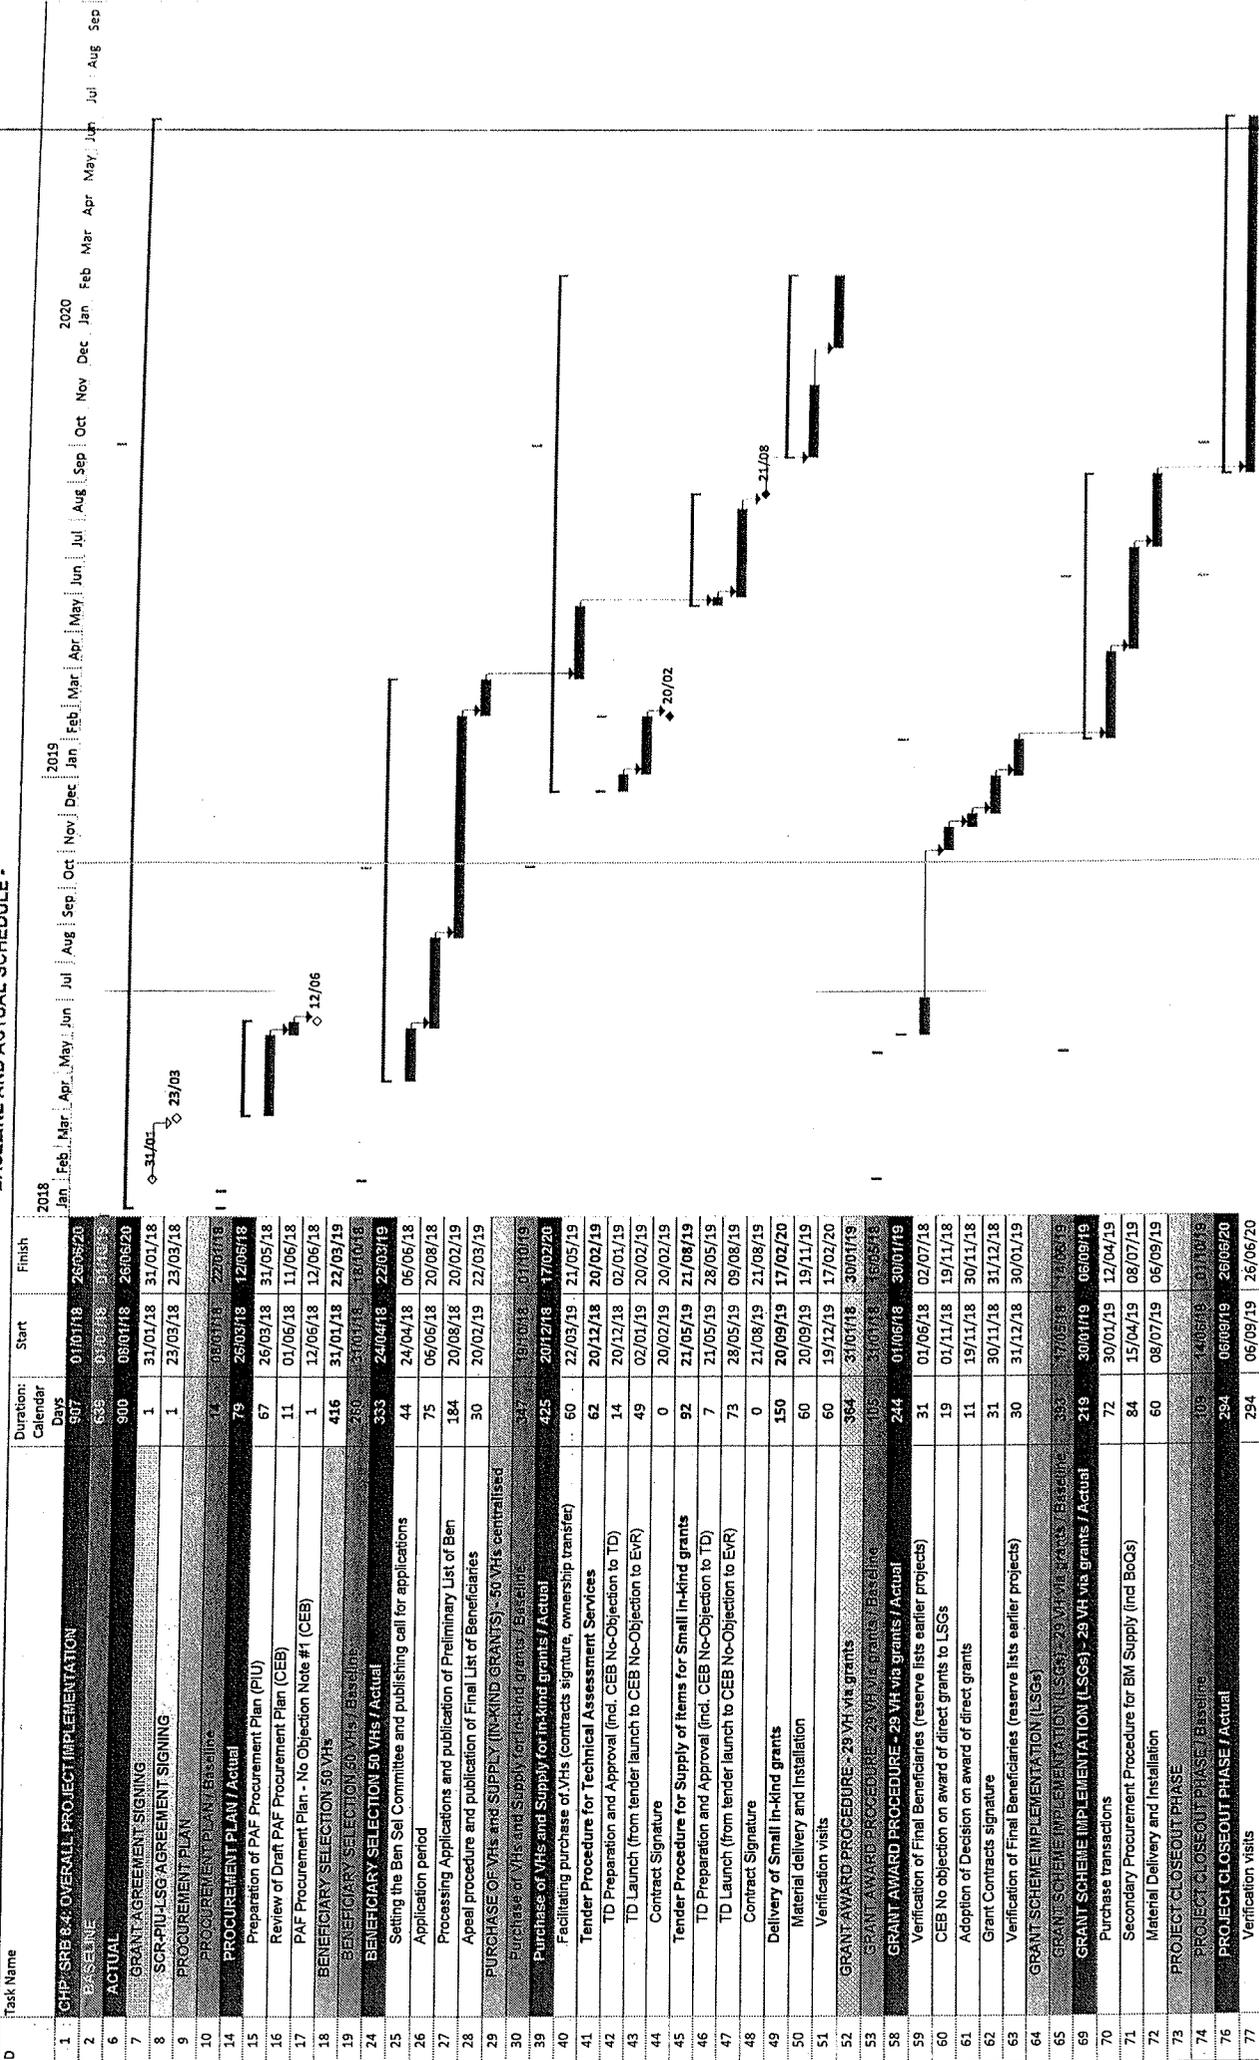

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP SRB 8.4: OVERALL PROJECT IMPLEMENTATION	907	01/01/18	26/08/20
2	BASELINE	635	01/01/18	31/03/18
6	ACTUAL	900	03/01/18	26/08/20
7	GRANT AGREEMENT SIGNING	1	31/01/18	31/01/18
8	SCRIPPLING AGREEMENT SIGNING	1	23/03/18	23/03/18
9	PROCUREMENT PLAN	1	01/01/18	01/01/18
10	PROCUREMENT PLAN Baseline	79	26/03/18	12/08/18
14	Preparation of PAF Procurement Plan (PIU)	67	26/03/18	31/05/18
15	Review of Draft PAF Procurement Plan (CEB)	11	01/06/18	11/06/18
16	PAF Procurement Plan - No Objection Note #1 (CEB)	1	12/06/18	12/06/18
17	BENEFICIARY SELECTION 50 VHs	416	31/01/18	22/03/19
18	BENEFICIARY SELECTION 50 VHs Baseline	280	31/01/18	18/03/18
24	BENEFICIARY SELECTION 50 VHs / Actual	333	24/04/18	22/03/19
25	Setting the Ben Sel Committee and publishing call for applications	44	24/04/18	06/06/18
26	Application period	75	06/06/18	20/08/18
27	Processing Applications and publication of Preliminary List of Ben	184	20/08/18	20/02/19
28	Appeal procedure and publication of Final List of Beneficiaries	30	20/02/19	22/03/19
29	PURCHASE OF VHs and SUPPLY (IN-KIND GRANTS) - 50 VHs centralised	347	19/03/18	01/01/19
30	Purchase of VHs and Supply for in-kind grants / Actual	425	20/12/18	17/02/20
39	Facilitating purchase of VHs (contracts signature, ownership transfer)	60	22/03/19	21/05/19
41	Tender Procedure for Technical Assessment Services	62	20/12/18	20/02/19
42	TD Preparation and Approval (incl. CEB No-Objection to TD)	14	20/12/18	02/03/19
43	TD Launch (from tender launch to CEB No-Objection to EVR)	49	02/03/19	20/02/19
44	Contract Signature	0	20/02/19	20/02/19
45	Tender Procedure for Supply of items for Small in-kind grants	92	21/05/19	21/08/19
46	TD Preparation and Approval (incl. CEB No-Objection to TD)	7	21/05/19	28/05/19
47	TD Launch (from tender launch to CEB No-Objection to EVR)	73	28/05/19	09/08/19
48	Contract Signature	0	21/08/19	21/08/19
49	Delivery of Small in-kind grants	150	20/09/19	17/02/20
50	Material delivery and installation	60	20/09/19	19/11/19
51	Verification visits	60	19/12/19	17/02/20
52	GRANT AWARD PROCEDURE - 29 VH via grants	364	31/07/18	30/01/19
53	GRANT AWARD PROCEDURE - 29 VH via grants Baseline	105	31/07/18	16/05/18
58	GRANT AWARD PROCEDURE - 29 VH via grants / Actual	244	01/08/18	30/01/19
59	Verification of Final Beneficiaries (reserve lists earlier projects)	31	01/08/18	02/07/18
60	CEB No objection on award of direct grants to LSGs	19	01/11/18	19/11/18
61	Adoption of Decision on award of direct grants	11	19/11/18	30/11/18
62	Grant Contracts signature	31	30/11/18	31/12/18
63	Verification of Final Beneficiaries (reserve lists earlier projects)	30	31/12/18	30/01/19
64	GRANT SCHEME IMPLEMENTATION (LSGs)	357	17/02/19	17/02/19
65	GRANT SCHEME IMPLEMENTATION (LSGs) - 29 VH via grants / Actual	219	30/01/19	06/09/19
69	Purchase transactions	72	30/01/19	12/04/19
71	Secondary Procurement Procedure for BM Supply (incl BoOs)	84	15/04/19	08/07/19
72	Material Delivery and Installation	60	08/07/19	06/09/19
73	PROJECT CLOSEOUT PHASE	109	14/05/19	01/01/20
74	PROJECT CLOSEOUT PHASE Baseline	284	06/09/19	26/06/20
75	PROJECT CLOSEOUT PHASE / Actual	284	06/09/19	26/06/20
77	Verification visits	294	06/09/19	26/06/20


Project: SRB 8.4  
 Provision of 79 VHs  
 Date: 16/10/2018

Actual Task Timeframe  
 Grant Agreement Signing

Estimated Project Activities Summary  
 Actual Project Activities Summary

Group of Activities  
 Progress

RHP CHP SERBIA - SRB 9.1 - CONSTRUCTION OF 350 APARTMENTS  
- BASELINE SCHEDULE -

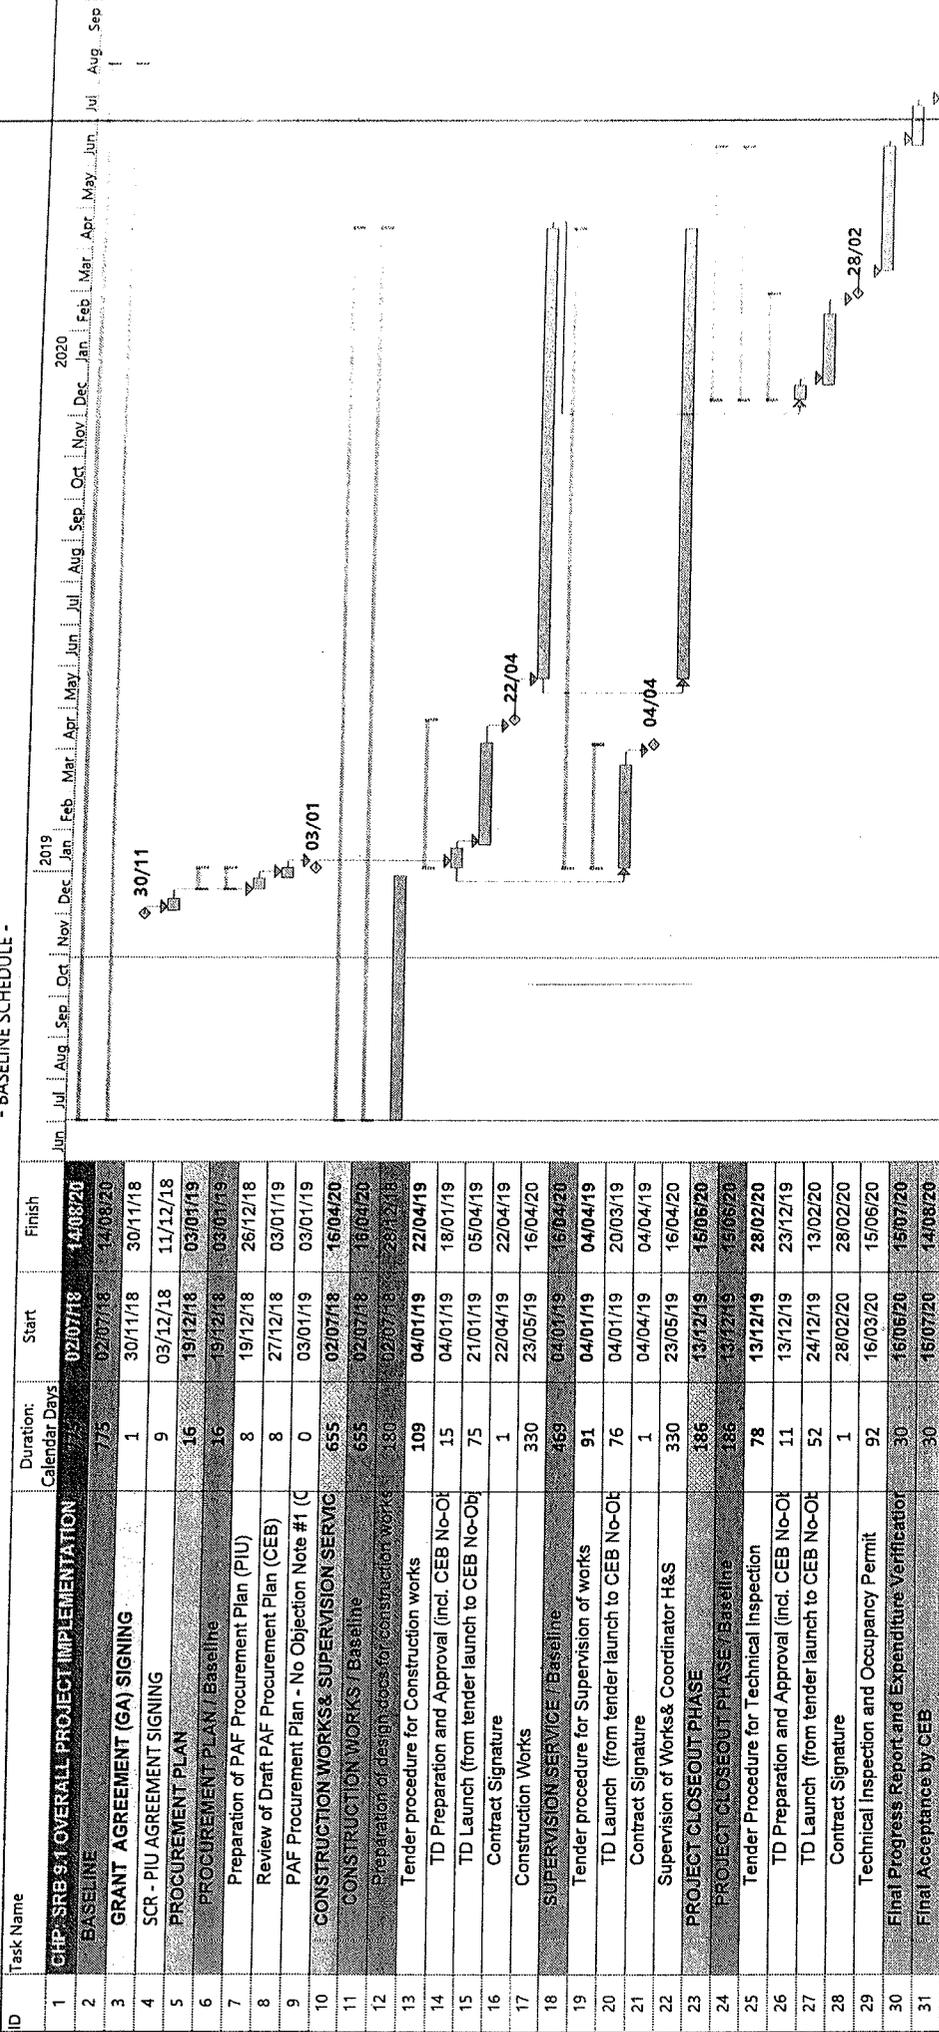


Project: SRB 9.1  
Construction of 350 Apts  
Date: 29/10/2018

Task Milestone Summary Project Summary

**RHP: CHP SERBIA - SRB 9.1b - PURCHASE OF 100 APARTMENTS  
- BASELINE SCHEDULE -**


ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 9.1b OVERALL PROJECT IMPLEMENTATION	316	30/11/18	11/10/19
2	GRANT AGREEMENT (GA) SIGNING	1	30/11/18	30/11/18
3	SCR/PIU AGREEMENT SIGNING	9	03/12/18	11/12/18
4	PROCUREMENT PLAN / Baseline	16	19/12/18	03/01/19
5	Preparation of PAF Procurement Plan (PIU)	8	19/12/18	26/12/18
6	Review of Draft PAF Procurement Plan (CEB)	8	27/12/18	03/01/19
7	PAF Procurement Plan - No Objection Note #1 (CEB)	0	03/01/19	03/01/19
8	BENEFICIARY SELECTION / Baseline	62	12/12/18	11/02/19
9	Verification of Beneficiary List (UNHCR and OSCE)	62	12/12/18	11/02/19
10	PROCUREMENT OF SERVICES OF APPRAISAL / Baseline	67	04/01/19	05/03/19
11	TD Preparation (up to CEB No-objection to TD)	11	04/01/19	14/01/19
12	Tendering (from TD launch to CEB No-objection on EVR)	35	15/01/19	18/02/19
13	Contract signature	1	05/03/19	05/03/19
14	SELECTION, PURCHASE and AWARD OF APARTMENTS / Baseline	212	12/02/19	11/09/19
15	Selection of apartments in competitive process	120	12/02/19	11/06/19
16	Govt Decision on purchase of apartments	30	12/06/19	11/07/19
17	Signing purchase contracts	32	12/07/19	12/08/19
18	Award of apartments to beneficiaries (incl signature of contracts with beneficiaries)	30	13/08/19	11/09/19
19	PROJECT CLOSEOUT / Baseline	30	12/09/19	11/10/19
20	Final report	30	12/09/19	11/10/19

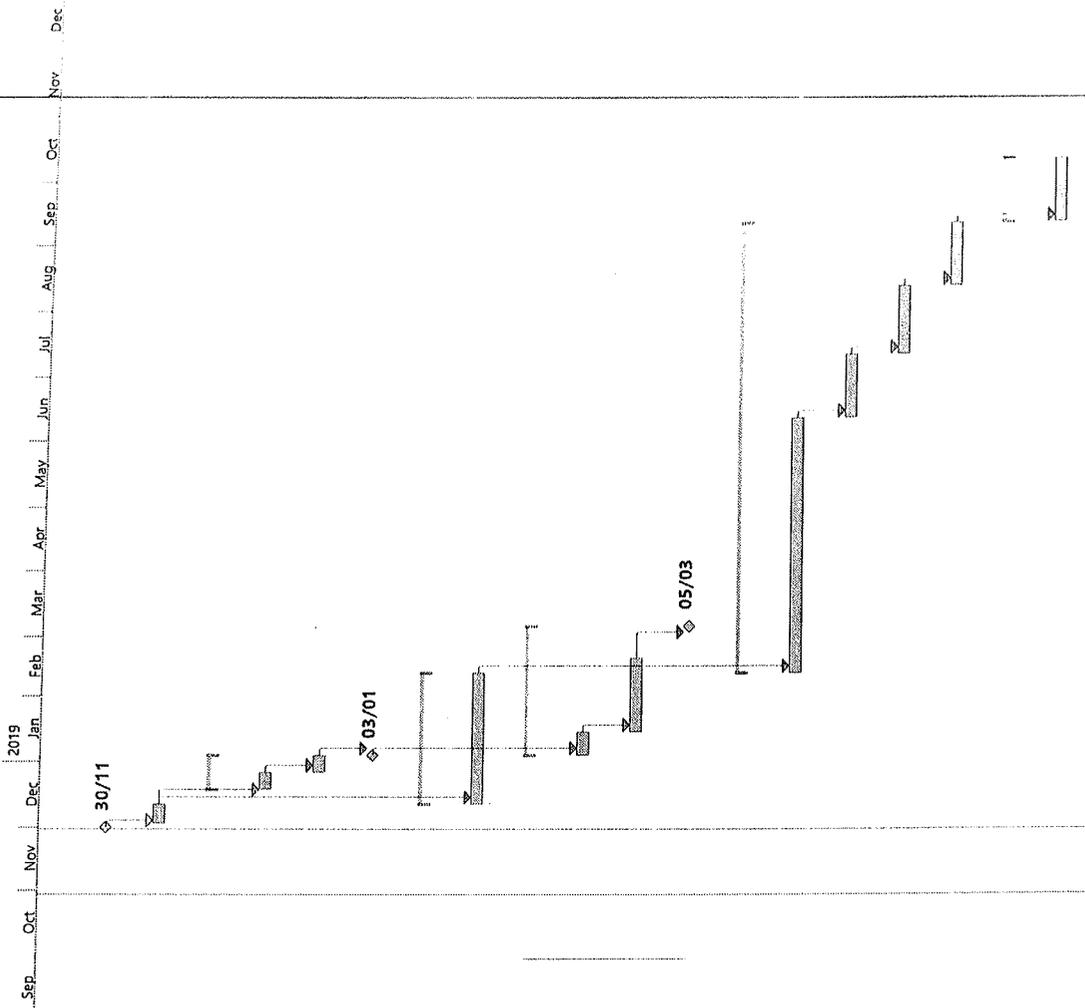

Project: SRB 9.1b Purchase of 100 A 29/10/2018	Grant Agreement Signing	Estimated Project Activities Summary	Actual Project Activities Summary
--	-------------------------	--------------------------------------	-----------------------------------

# RHP: CHP SERBIA - SRB 9.2 - CONSTRUCTION OF 50 PRE-FAB HOUSES - BASELINE SCHEDULE -

ID	Task Name	Duration: Calendar Days	Start	Finish
1	CHP-SRB 9.2 OVERALL PROJECT IMPLEMENTATION	637	30/11/18	27/08/20
2	BASELINE	637	30/11/18	27/08/20
3	GRANT AGREEMENT (GA) SIGNING	1	30/11/18	30/11/18
4	SCR-PIU AGREEMENT SIGNING	9	03/12/18	11/12/18
5	BENEFICIARY SELECTION			
6	BENEFICIARY SELECTION / Baseline	60	03/12/18	31/01/19
7	Verification of Beneficiaries selected under SRB8	60	03/12/18	31/01/19
8	DESIGN-BUILD & TECH. SUPERVISION			
9	DESIGN-BUILD & TECH. SUPERVISION / Baseline	495	01/02/19	09/06/20
10	Tender Procedure for Design-Build	102	01/02/19	13/05/19
11	TD Preparation and Approval (incl. CEB No-Objection to TD)	8	01/02/19	08/02/19
12	TD Launch (from tender launch to CEB No-Objection to EVR)	75	11/02/19	26/04/19
13	Contract Signature	1	13/05/19	13/05/19
14	Design-Build	365	11/06/19	09/06/20
15	Tender for supervision services	102	01/02/19	13/05/19
16	TD Preparation and Approval (incl. CEB No-Objection to TD)	8	01/02/19	08/02/19
17	TD Launch (from tender launch to CEB No-Objection to EVR)	75	11/02/19	26/04/19
18	Contract Signature	1	13/05/19	13/05/19
19	Technical supervision for Design-Build-Install Coordinator for H&S	365	11/06/19	09/06/20
20	PROJECT CLOSEOUT			
21	PROJECT CLOSEOUT PHASE / Baseline	247	25/12/19	27/08/20
22	Tender for Technical Inspection	69	25/12/19	02/03/20
23	TD Preparation and Approval (incl. CEB No-Objection to TD)	7	25/12/19	31/12/19
24	TD Launch (from tender launch to CEB No-Objection to EVR)	45	01/01/20	14/02/20
25	Contract Signature	1	02/03/20	02/03/20
26	Technical Acceptance and Hand Over (Incl. Tech. Inspection)	91	31/03/20	29/06/20
27	Issuance of occupancy permits	91	29/05/20	27/08/20




Project: SRB 9.2  
Construction of 5  
Date: 29/10/2018

Actual Task Timeframe  
Grant Agreement Signing

Estimated Project Activities Summary  
Actual Project Activities Summary


Progress  
Group of Activities

RHP CHP SERBIA - SRB 9.3 - PROVISION OF 200 BM PACKAGES  
- BASELINE SCHEDULE -

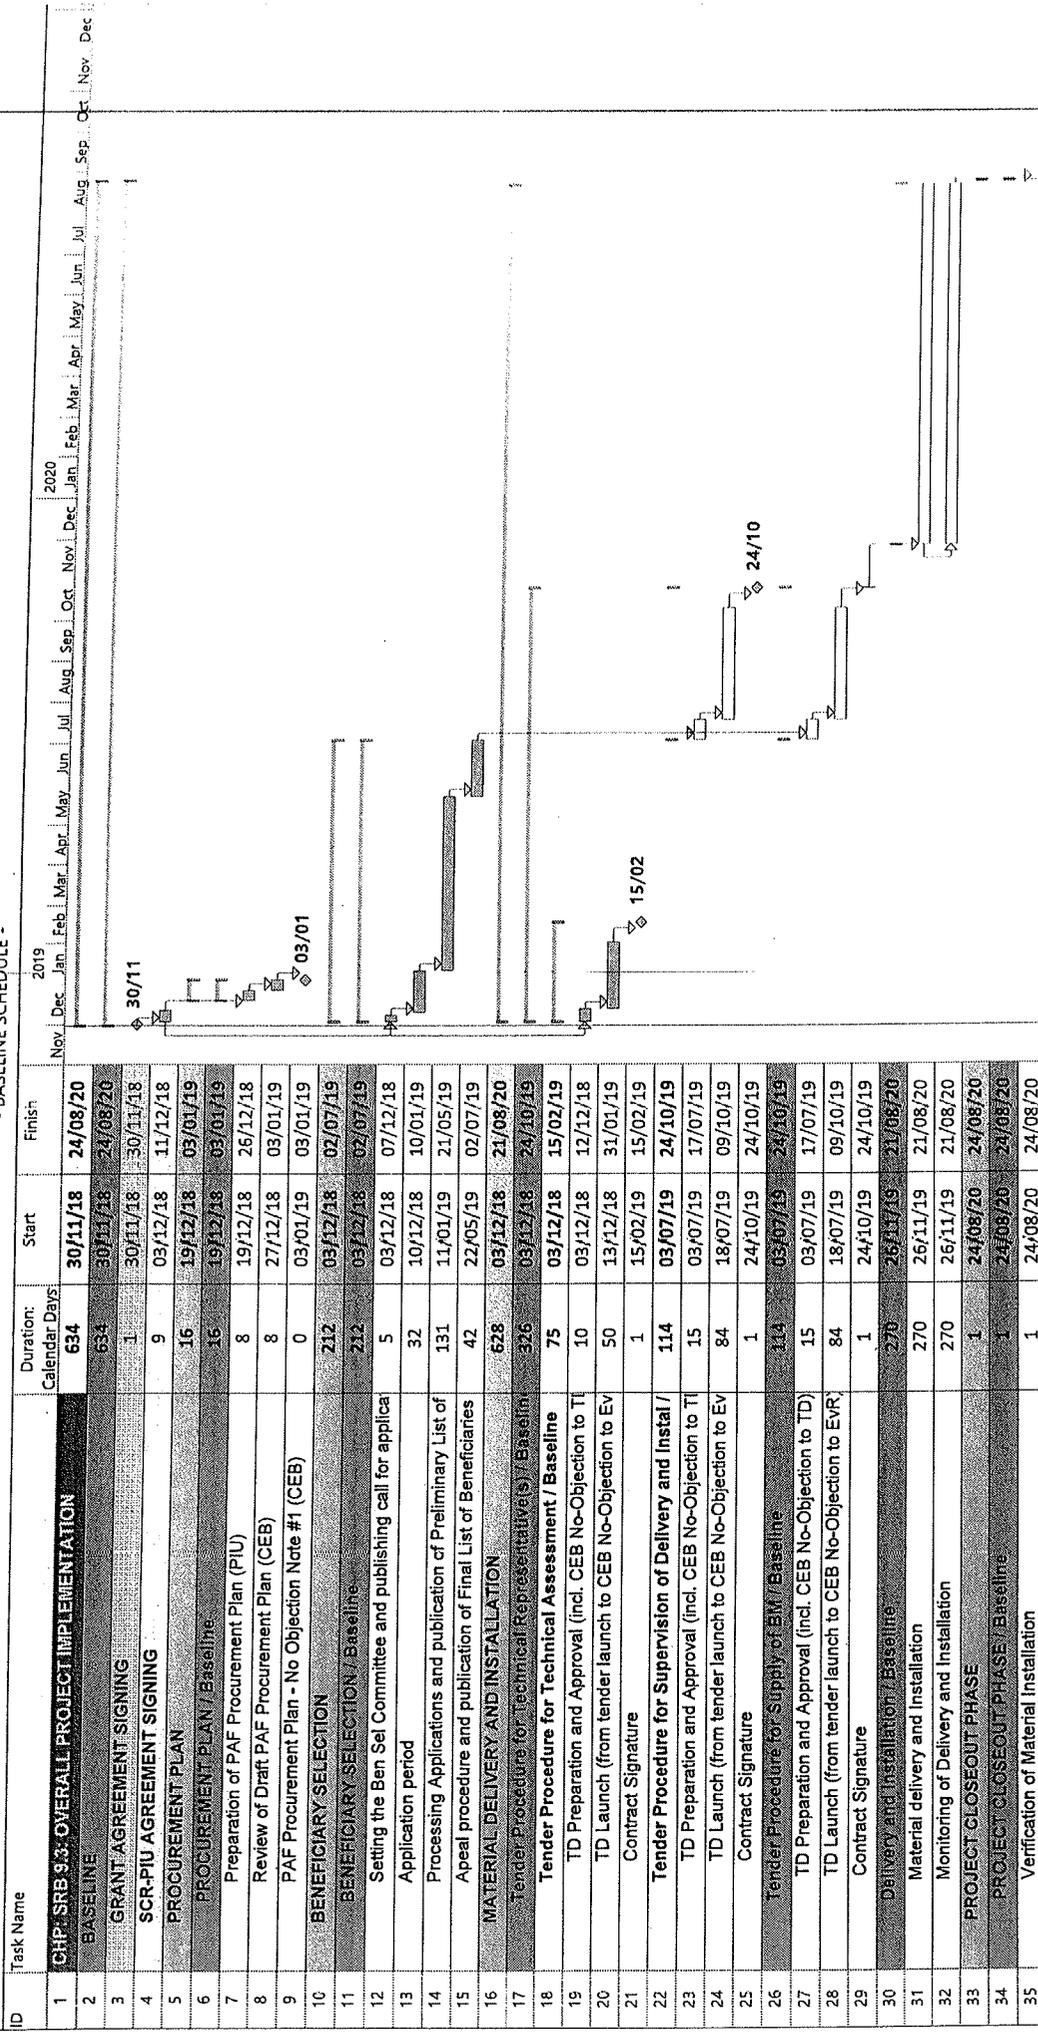

Project: SRB 9.3 Provision of 200 B Date: 29/10/2018

RHP CHP SERBIA - SRB 9.4 - PROVISION OF 200 VILLAGE HOUSES  
- BASELINE SCHEDULE -

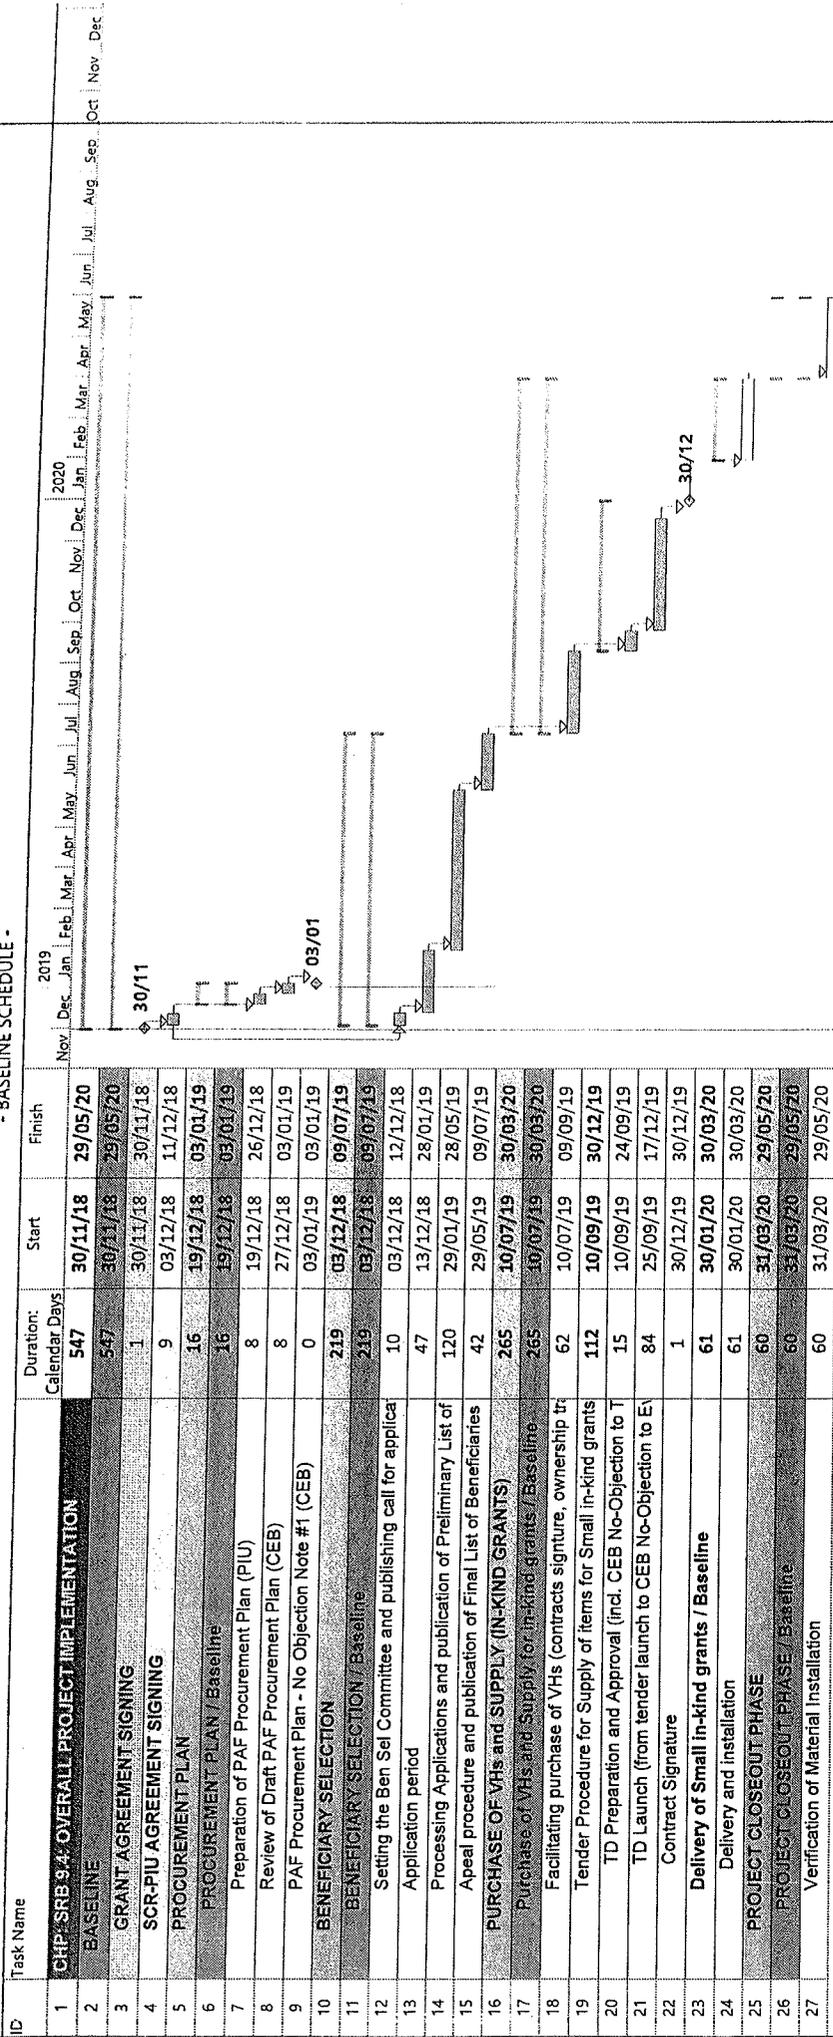

---

---

---
